

September 2025 Monthly Construction Status Report

Updated: 10.07.2025



A1-A2 - Fonwood Tunnel

WHCRWA Ongoing Construction Projects

Segment B1-B2

3 MILES OF 84-INCH DIAMETER AND 8 MILES OF 96-INCH WATERLINES FROM WEST OF BRITTMOORE ROAD TO WEST OF I-45

Segment B3

4.4 MILES OF 96-INCH DIAMETER WATER LINES FROM WEST OF I-45 TO THE SOUTH SIDE OF HOPPER RD. VIA TUNNEL

Central Pump Station

CONSTRUCTION OF A CENTRAL PUMP STATION THAT WILL RECEIVE WATER FROM THE RE-PUMP STATION AND THEN TRANSFER WATER TO MUDS

Segment A1-A2

11 MILES OF 96-INCH WATER LINE FROM HOPPER RD. TO THE WHCRWA METER STATION NEAR THE NEWPP

RePump Station

CONSTRUCTION OF A 160 MGD REPUMP STATION FACILITY INCLUDING TWO 10 MILLION GALLON TANKS

NorthEast Meter Station

CONSTRUCTION OF A METER STATION AT COH/WHCRWA INTERFACE

Kinder Morgan 1, 2, 3, 4, 5, & 6 - (6 Projects)

6 MILES OF 66-INCH AND 1,300 LF OF 84-INCH WATERLINE FROM SEGMENT C1 CONNECTION TO THE I-10 METER STATION


I-10 Meter Station

CONSTRUCTION OF A METER STATION AT THE NFBWA INTERFACE


CIP Projects

CONTRACT 51, 63, 64, & 65


Current SWSP Construction Projects Overview

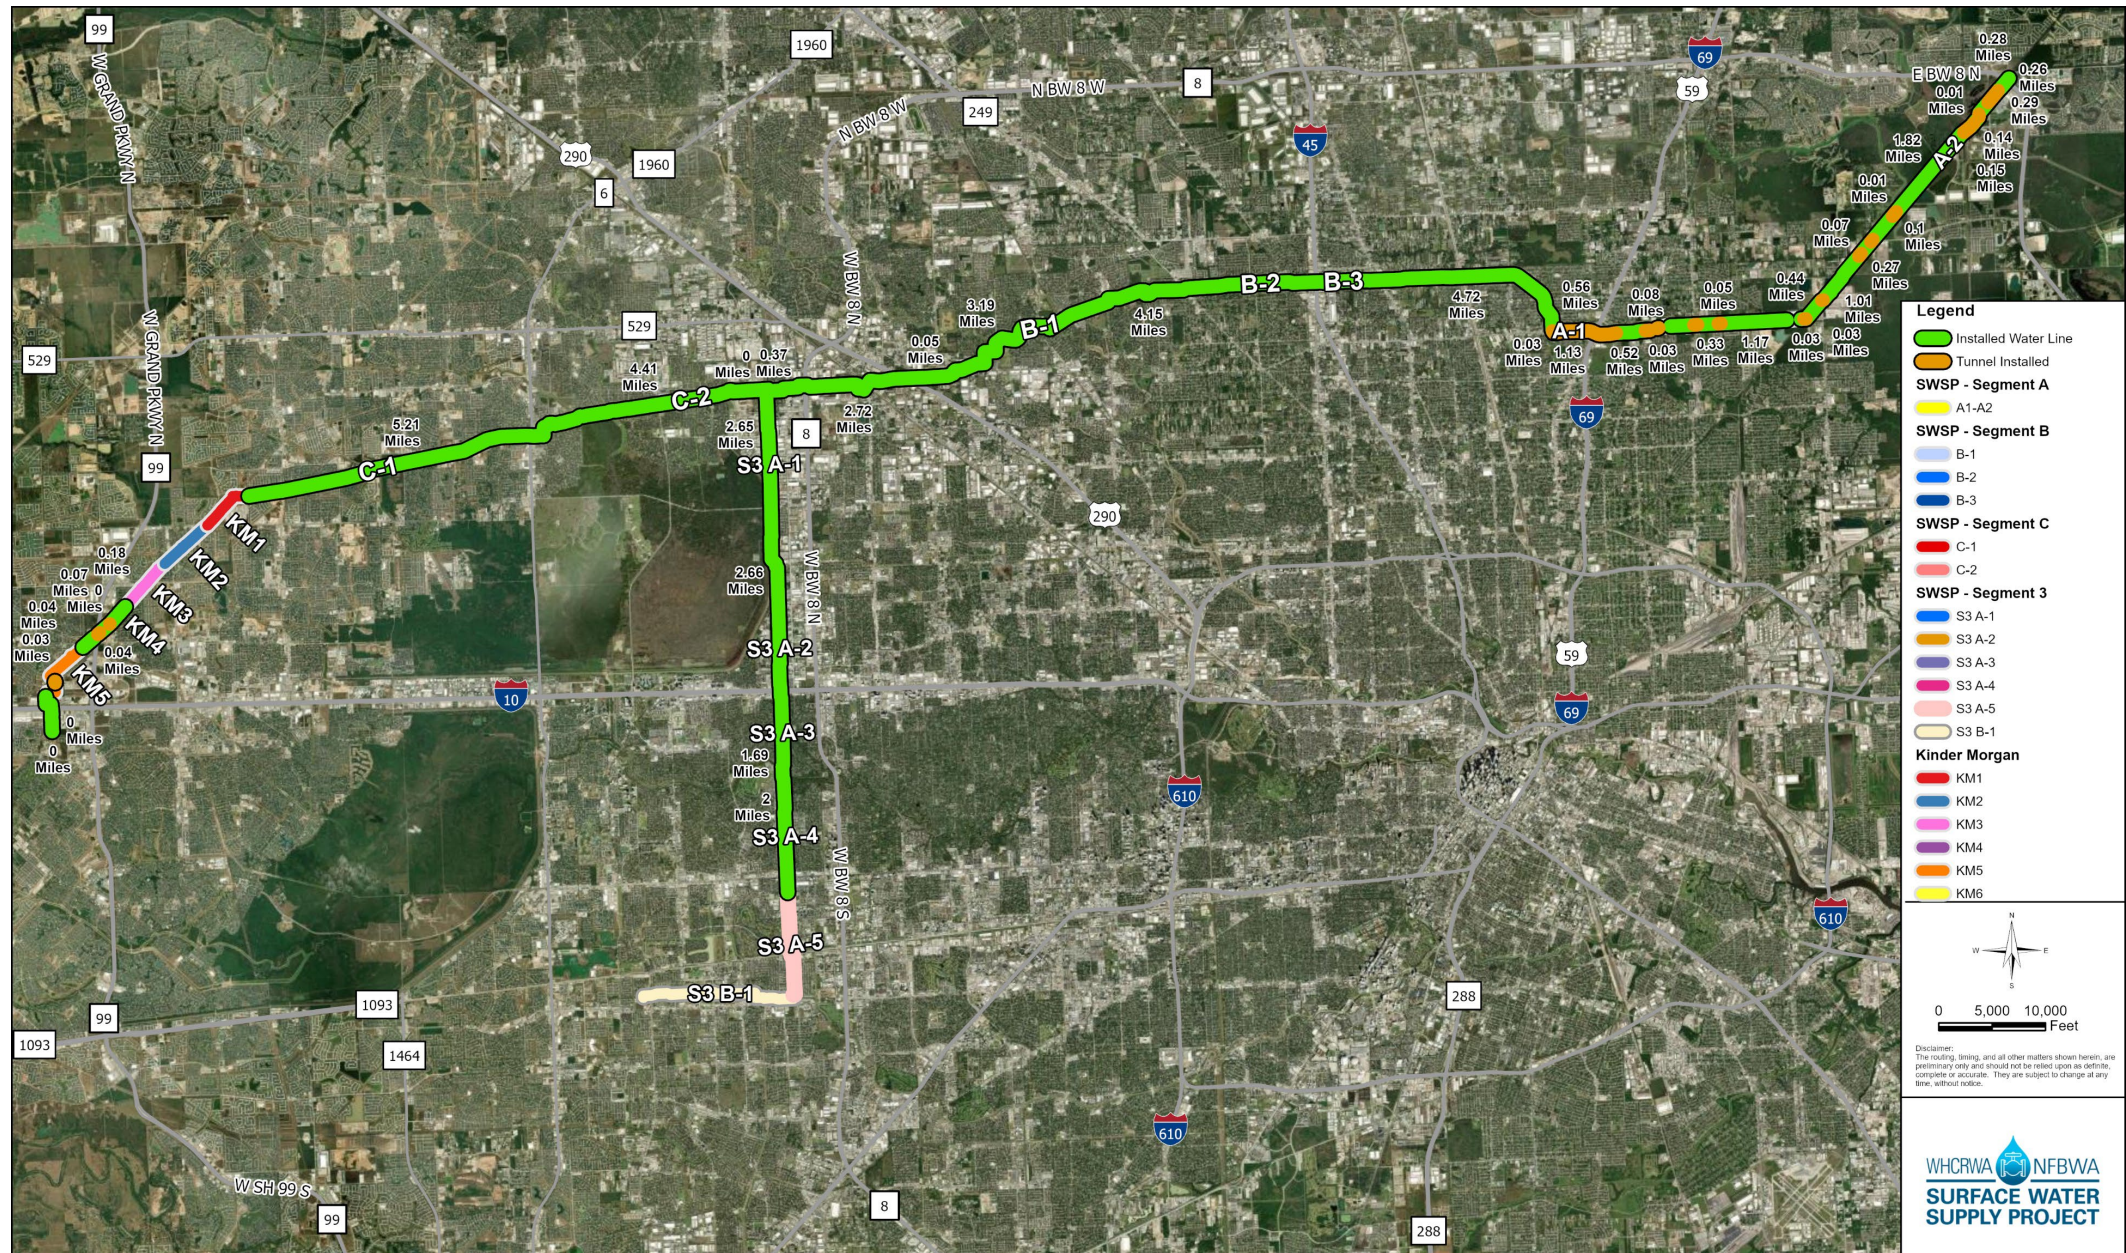

Construction Progress – Segment B1-B2

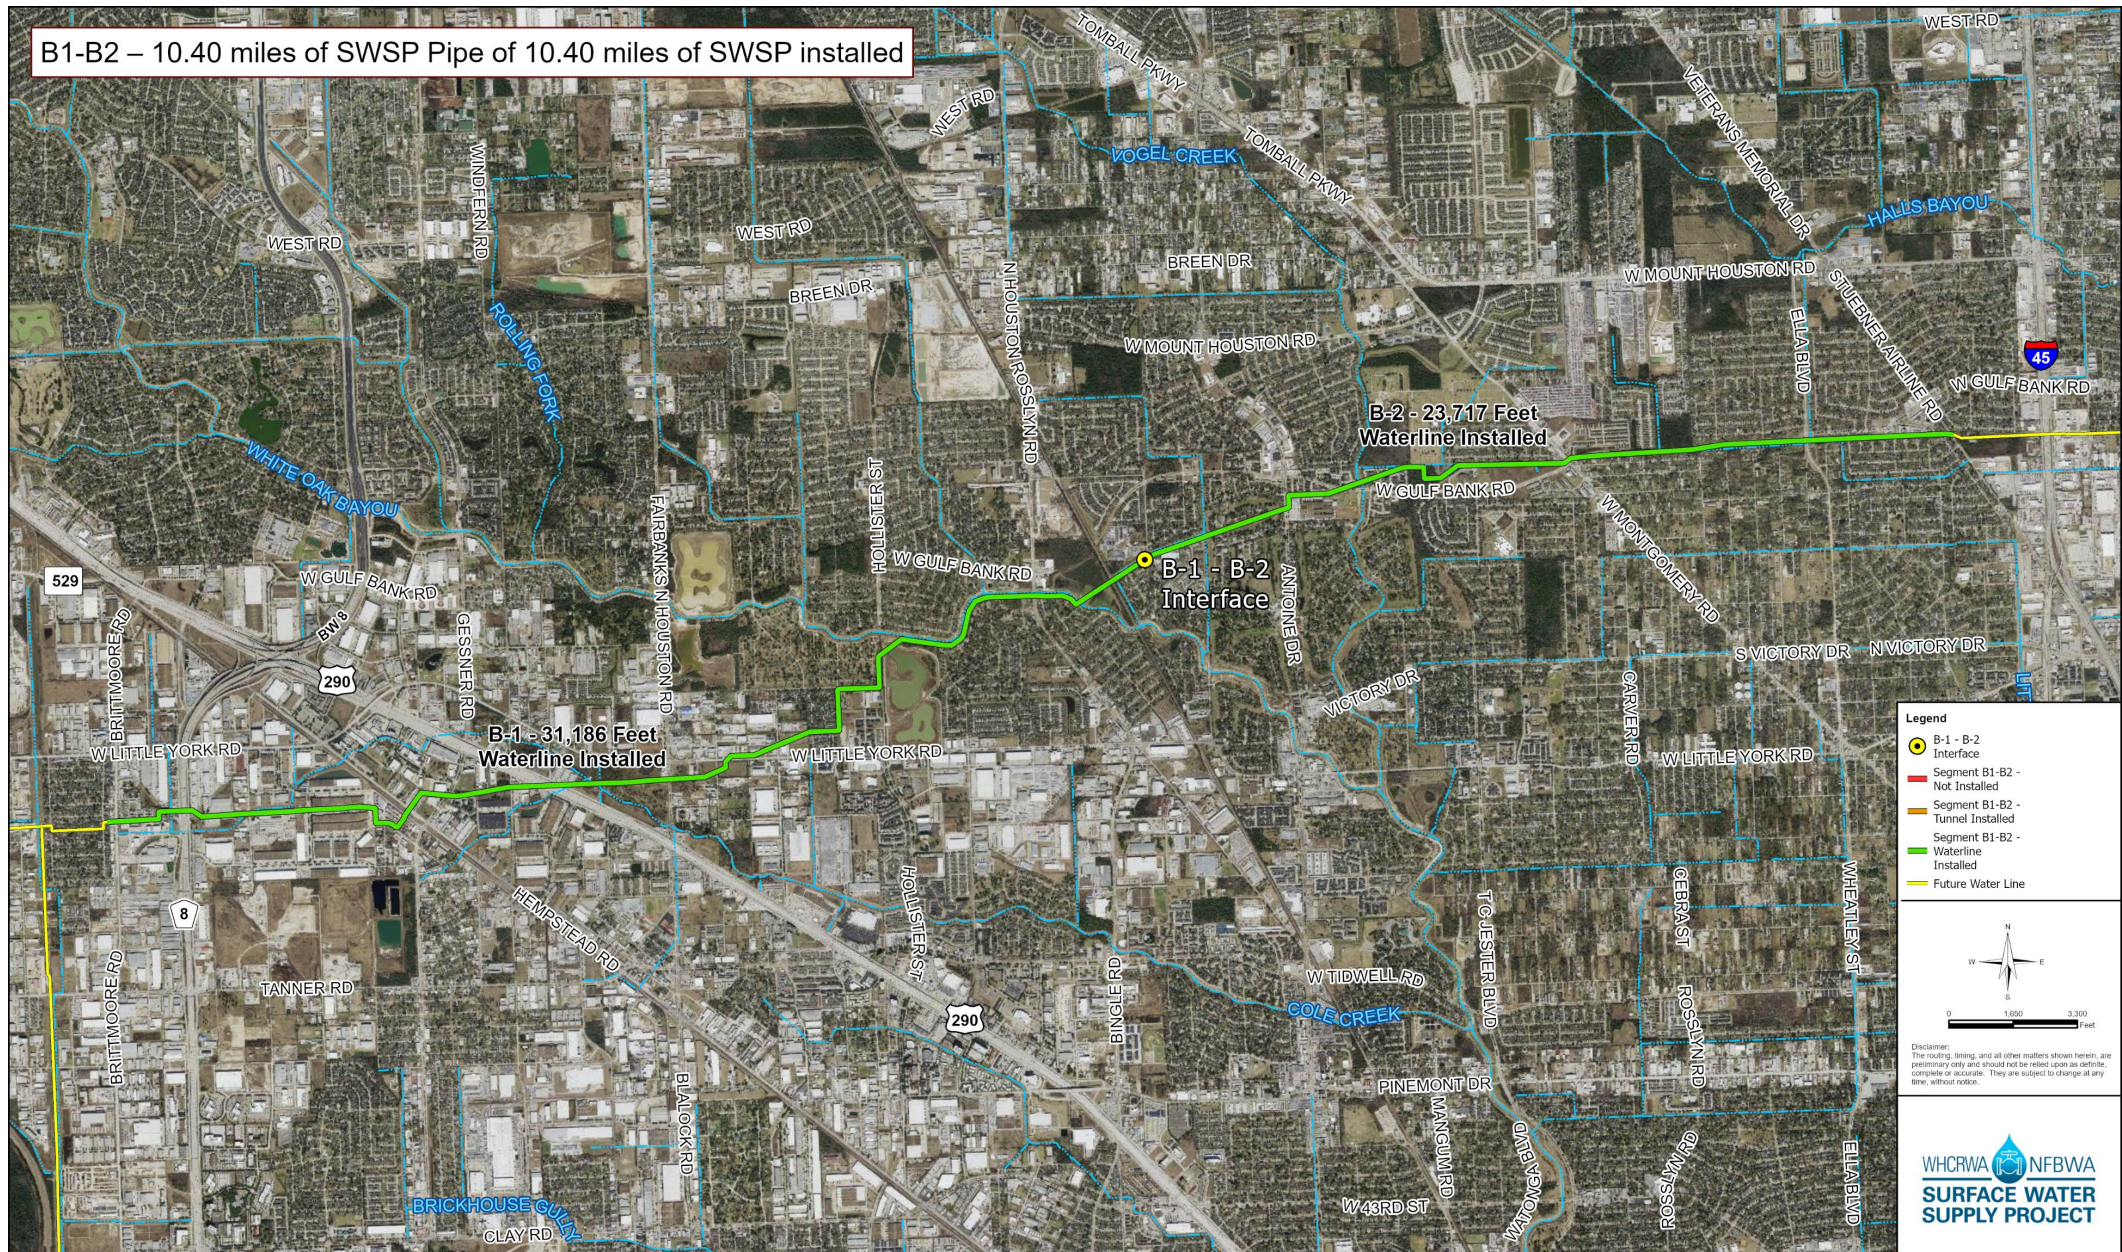


Construction Progress – Segment A1-A2

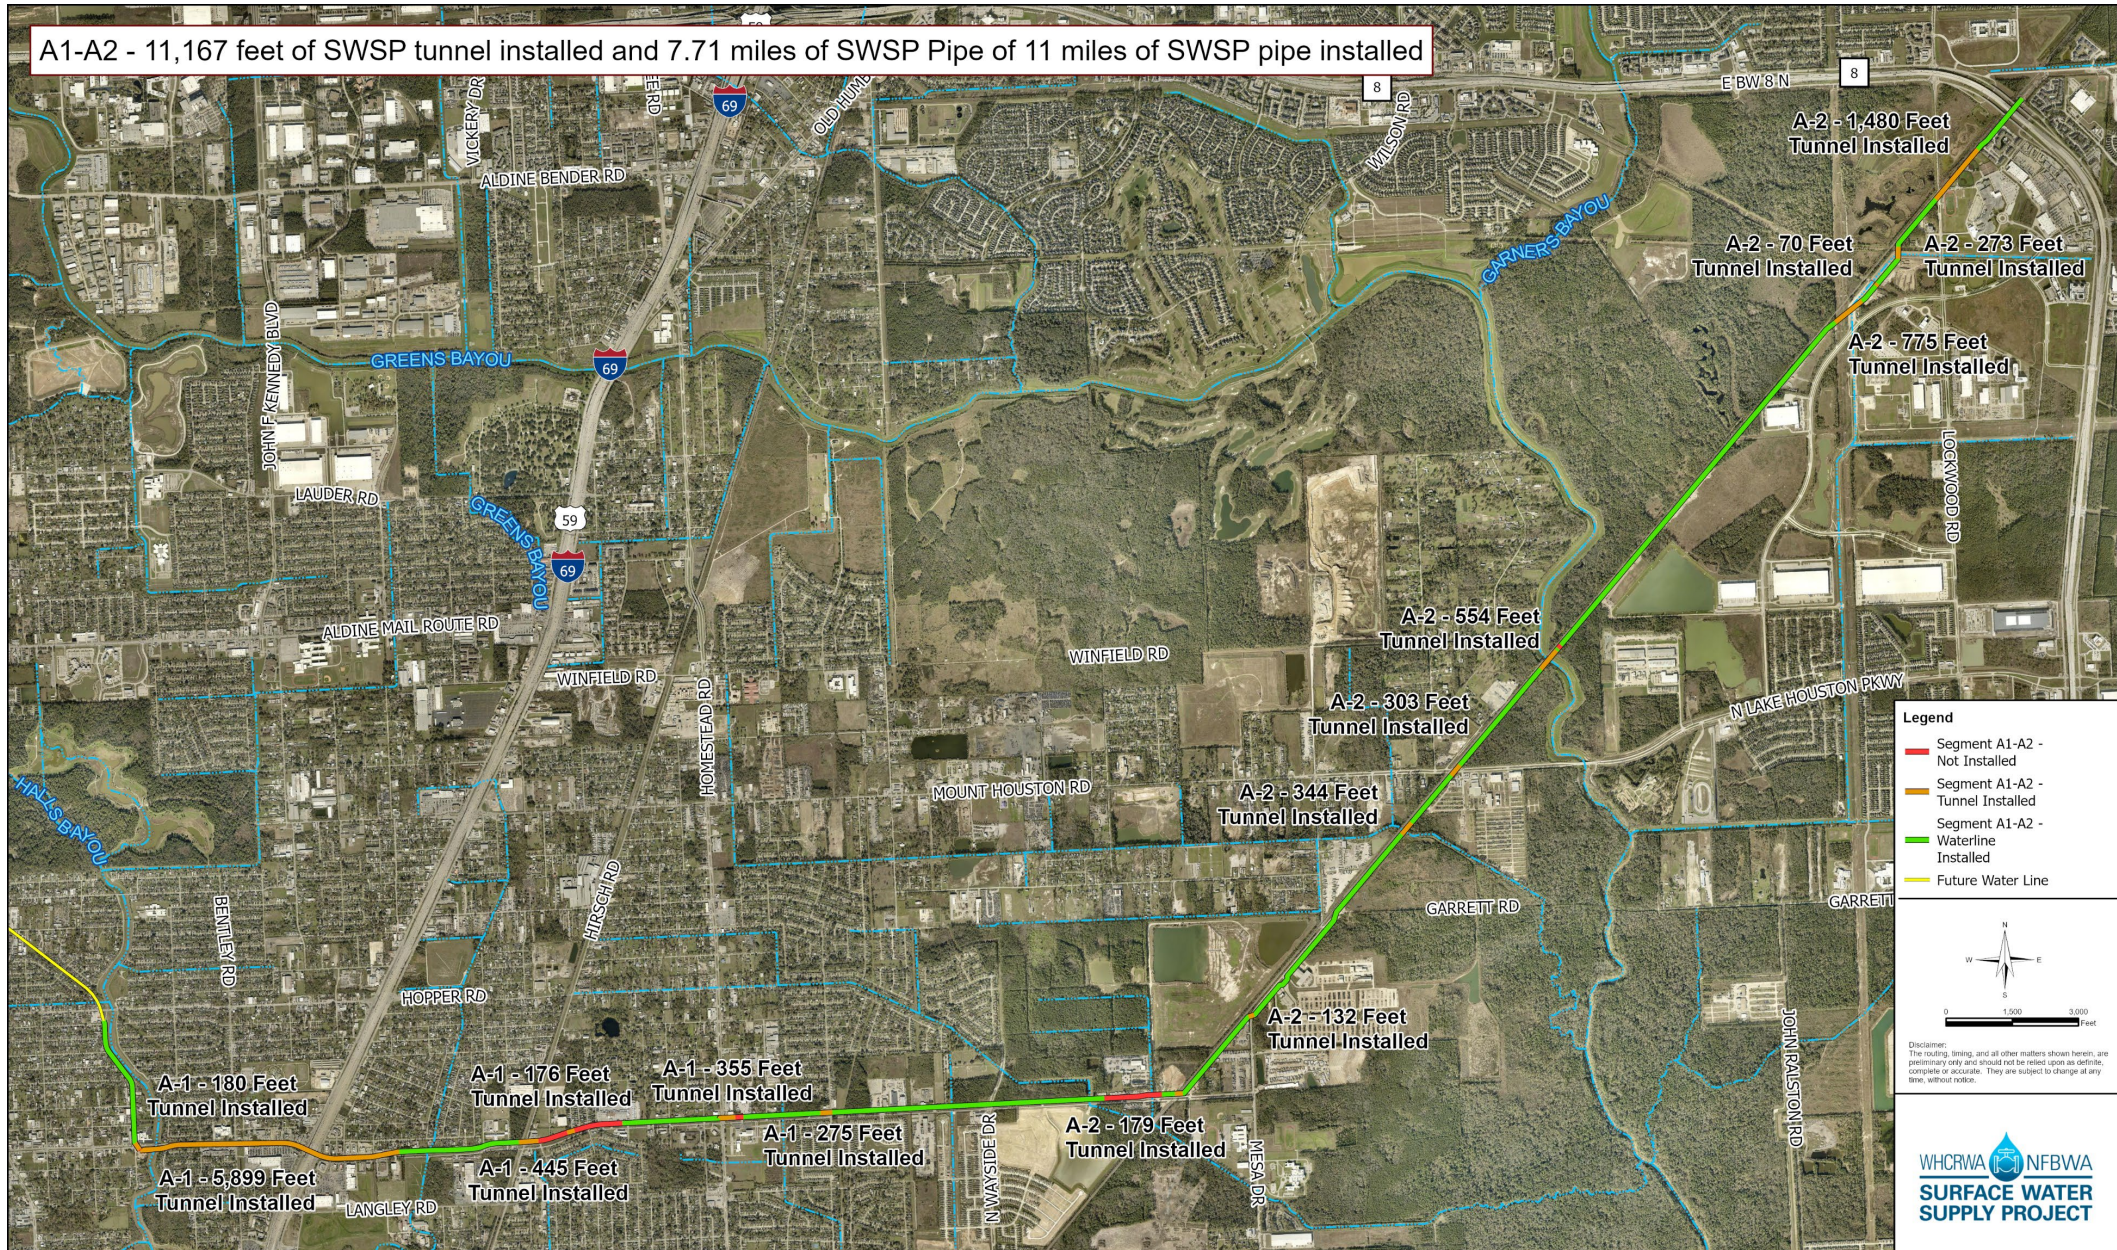

SWSP Contract Segment A1-A2 - Construction Progress

Construction Progress – Kinder Morgan-4


KM4 – 245 feet of SWSP Tunnel installed and 0.79 miles of SWSP Pipe of 1.1 miles of SWSP pipe installed

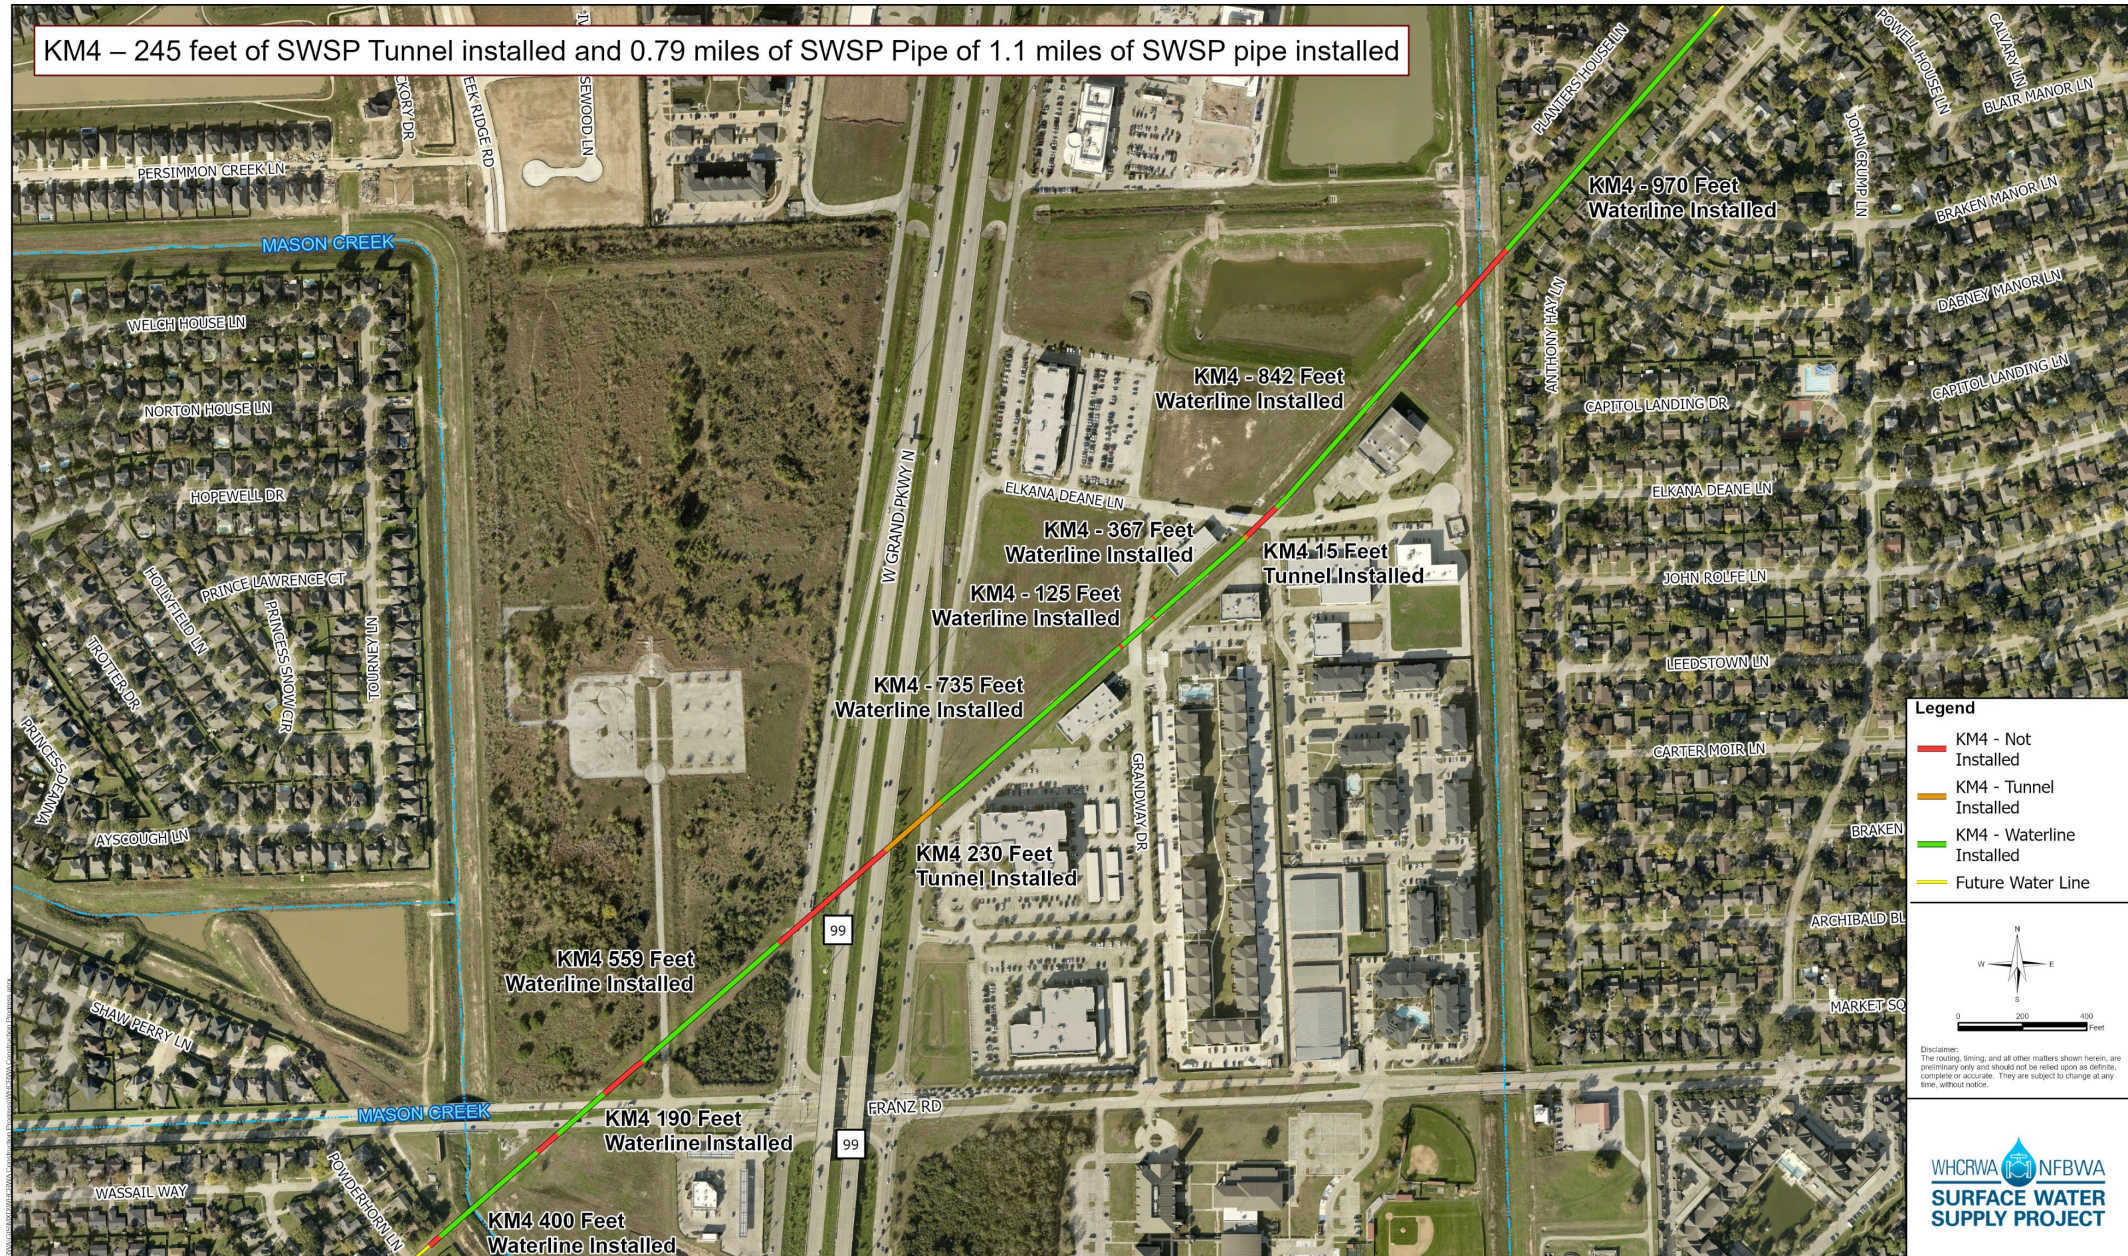

Kinder Morgan 4 - Construction Progress

Construction Progress – Kinder Morgan-5

KM4 – 135 feet of SWSP Tunnel installed and 0 miles of SWSP Pipe of 1 miles of SWSP pipe installed

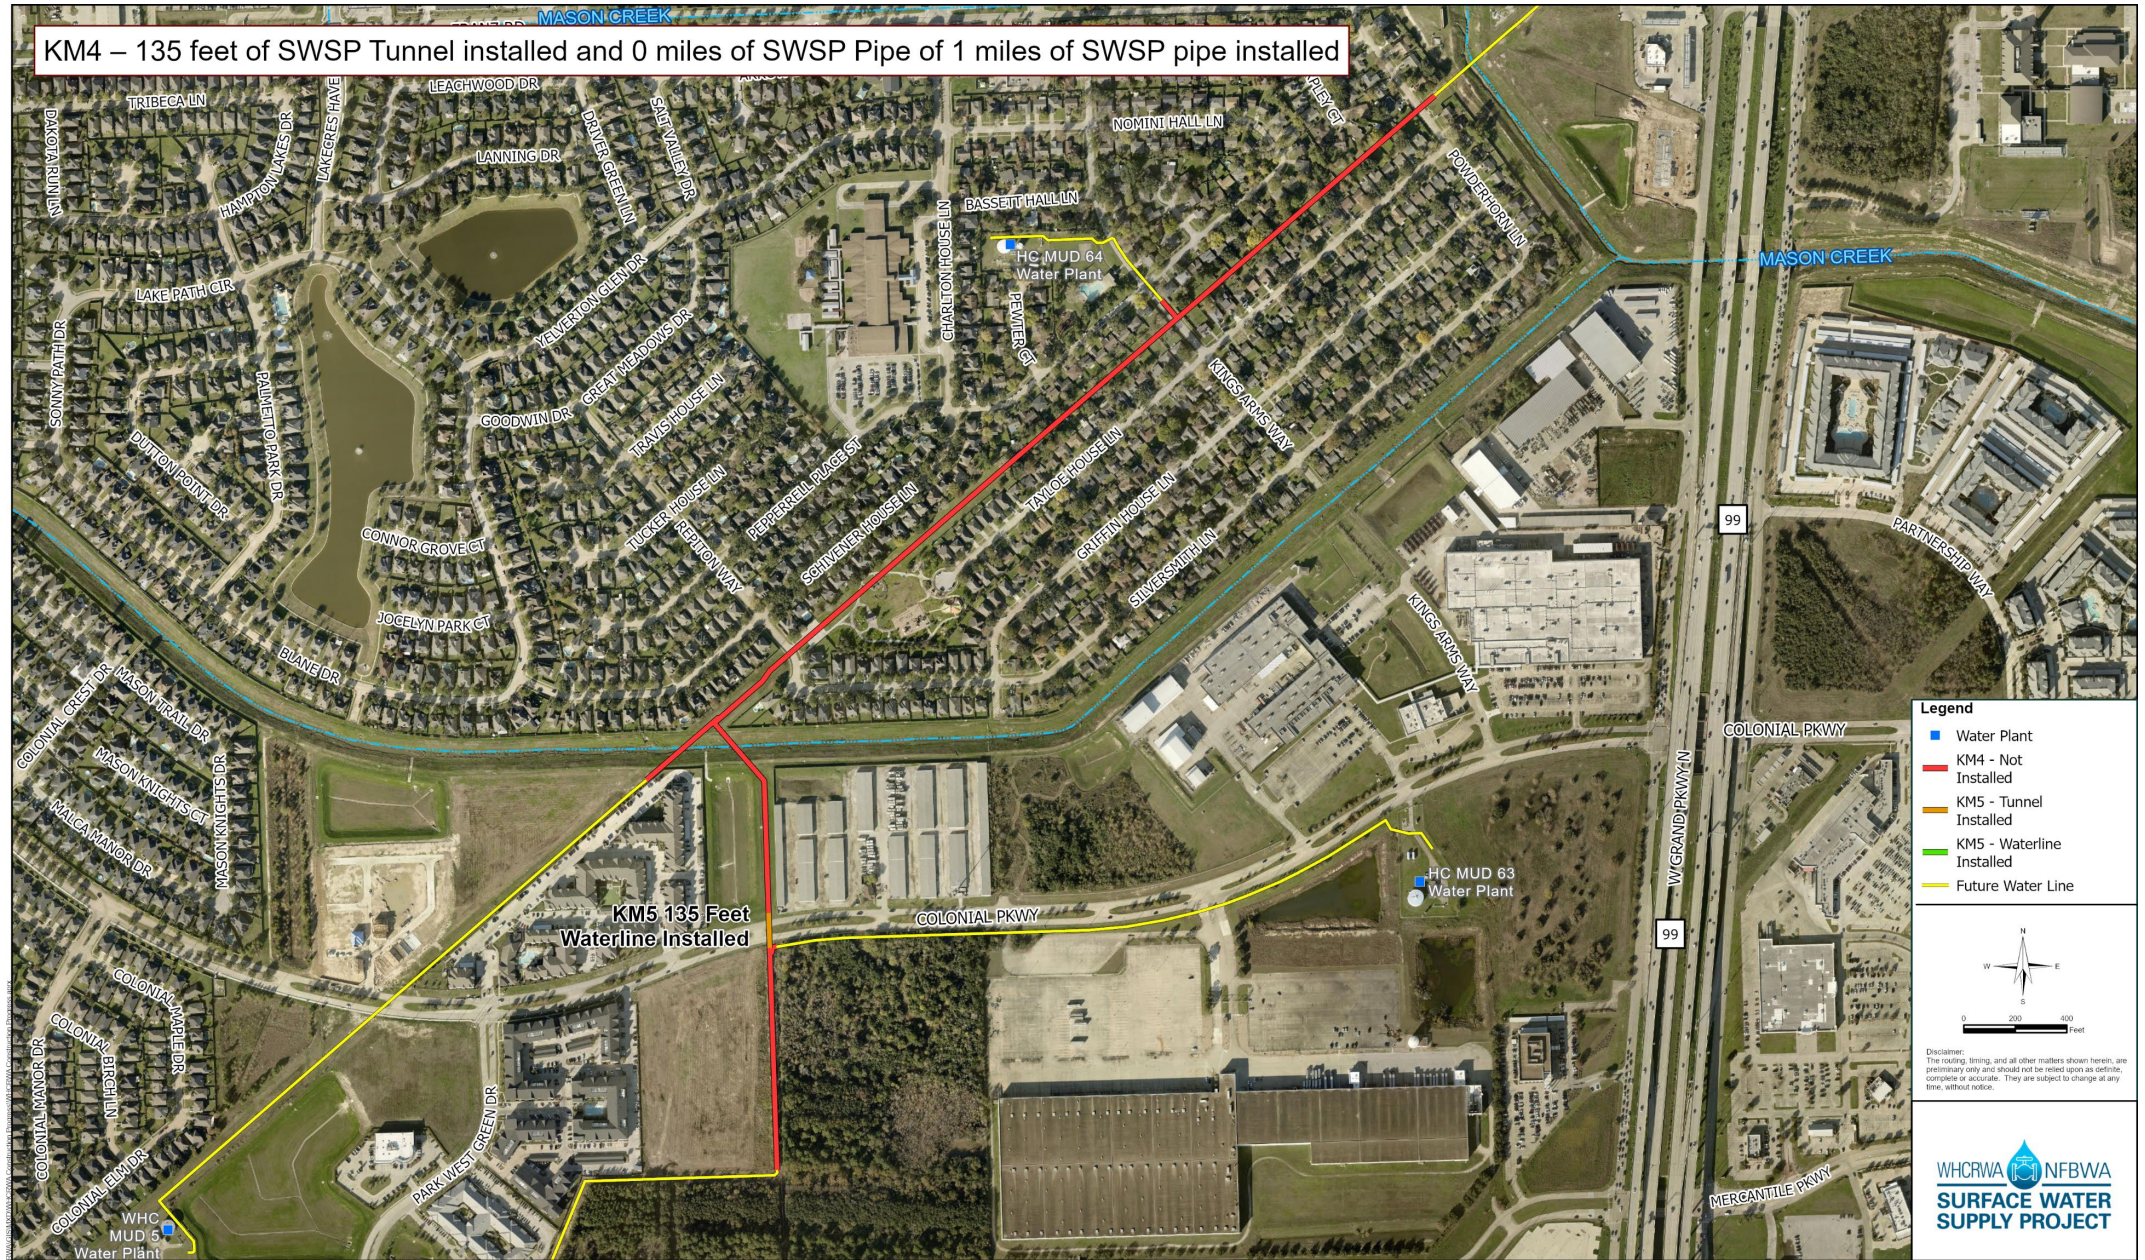


Kinder Morgan 5 - Construction Progress

WHCRA NFBWA
SURFACE WATER
SUPPLY PROJECT

GANNETT
FLEMING

Construction Progress – Kinder Morgan-6

KM6 – 0 feet of SWSP Tunnel installed and 0.67 miles of SWSP Pipe of 1 mile of SWSP pipe installed

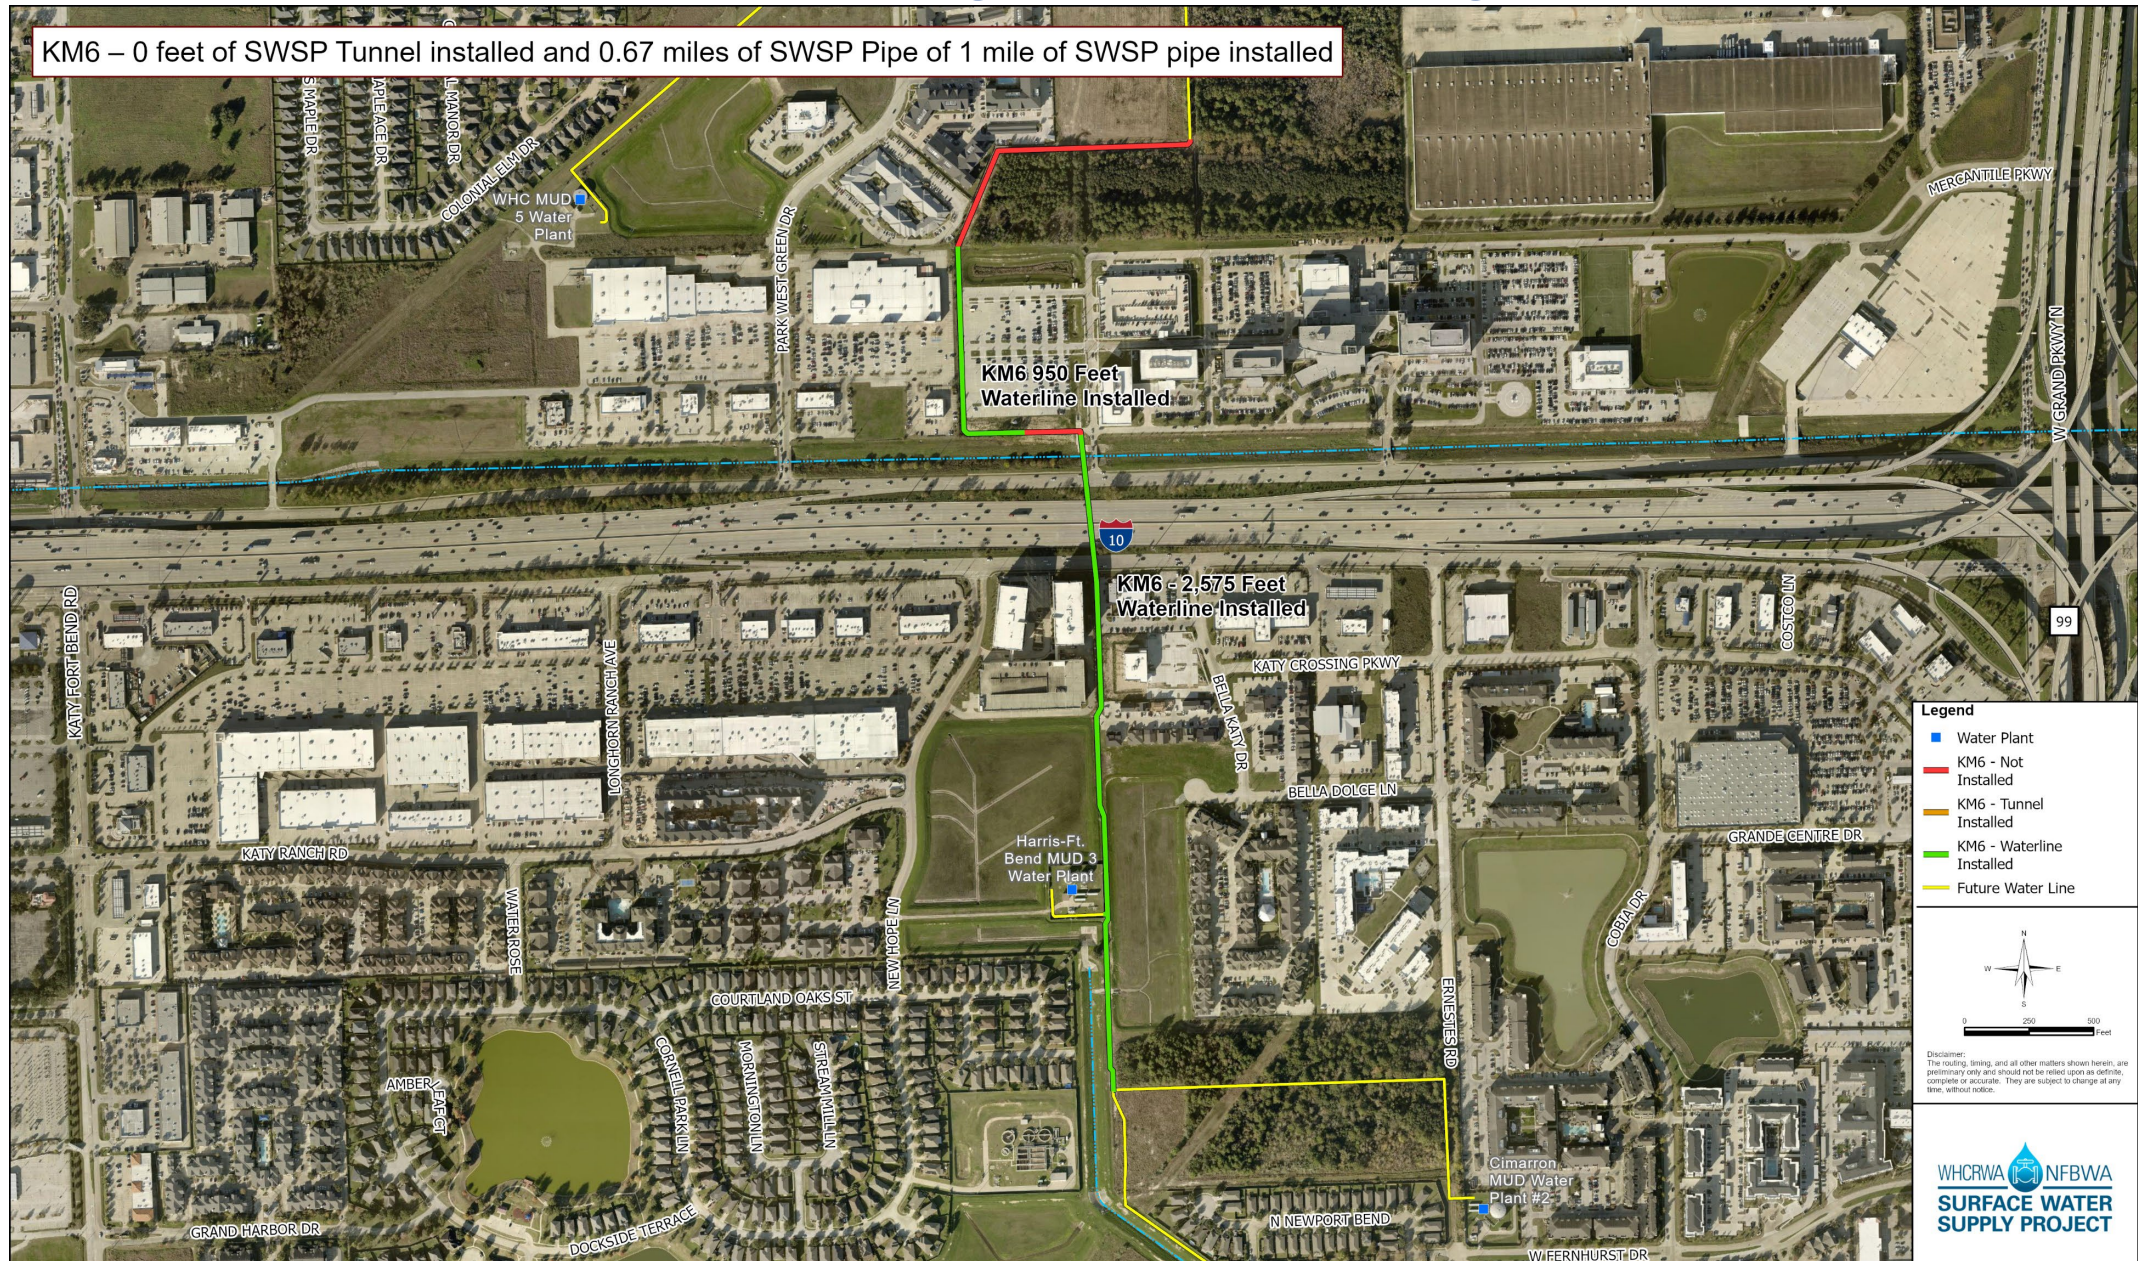

Kinder Morgan 6 - Construction Progress




Open Cut (LF) by Project

186K
Installed

17K
Remaining

ProjectID	Bid Quantity (LF)
A1-A2	44,582
B1-B2	42,456
B3	210
C1	33,292
C2	23,760
KM2	4,720
KM4	3,880
KM5	5,198
KM6	4,301
S3-A1	12,750
S3-A2	11,402
S3-A3	5,670
S3-A4	9,882
Total	202,103

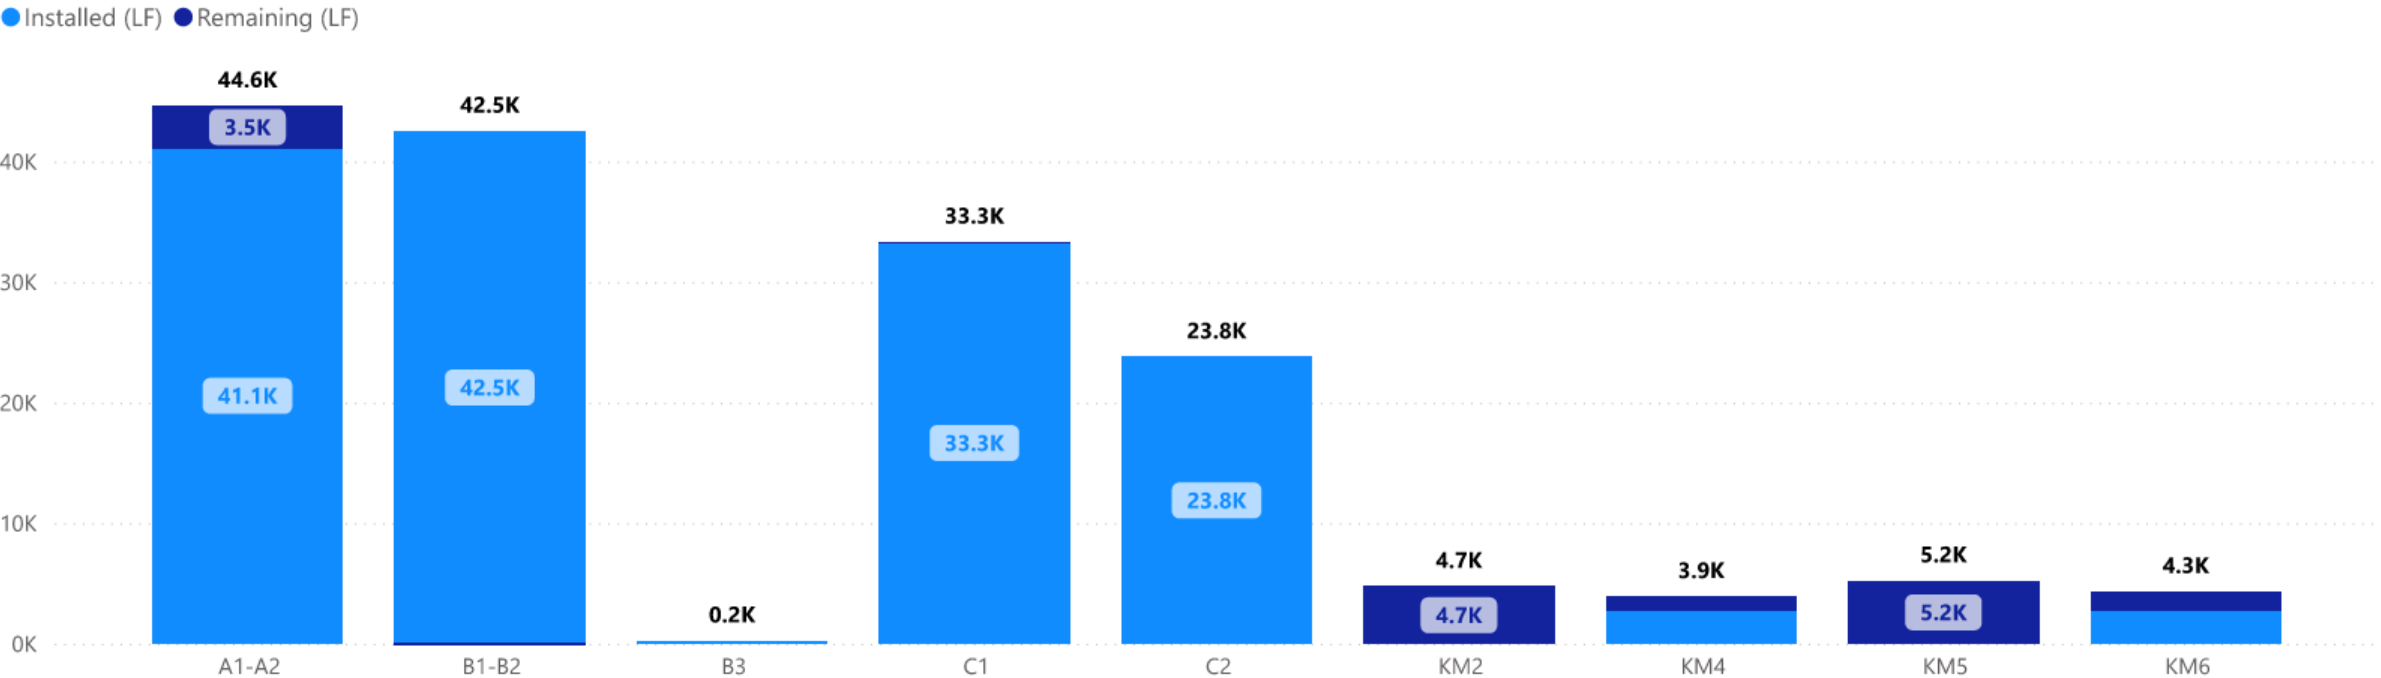




Tunneling (LF) by Project


60K
Installed

3K
Remaining

ProjectID	Bid Quantity (LF)
A1-A2	12,127
B1-B2	12,384
B3	22,885
C1	2,554
C2	1,599
KM2	611
KM4	1,665
KM5	831
KM6	563
S3-A1	1,270
S3-A2	2,626
S3-A3	3,076
S3-A4	1,198
Total	63,389

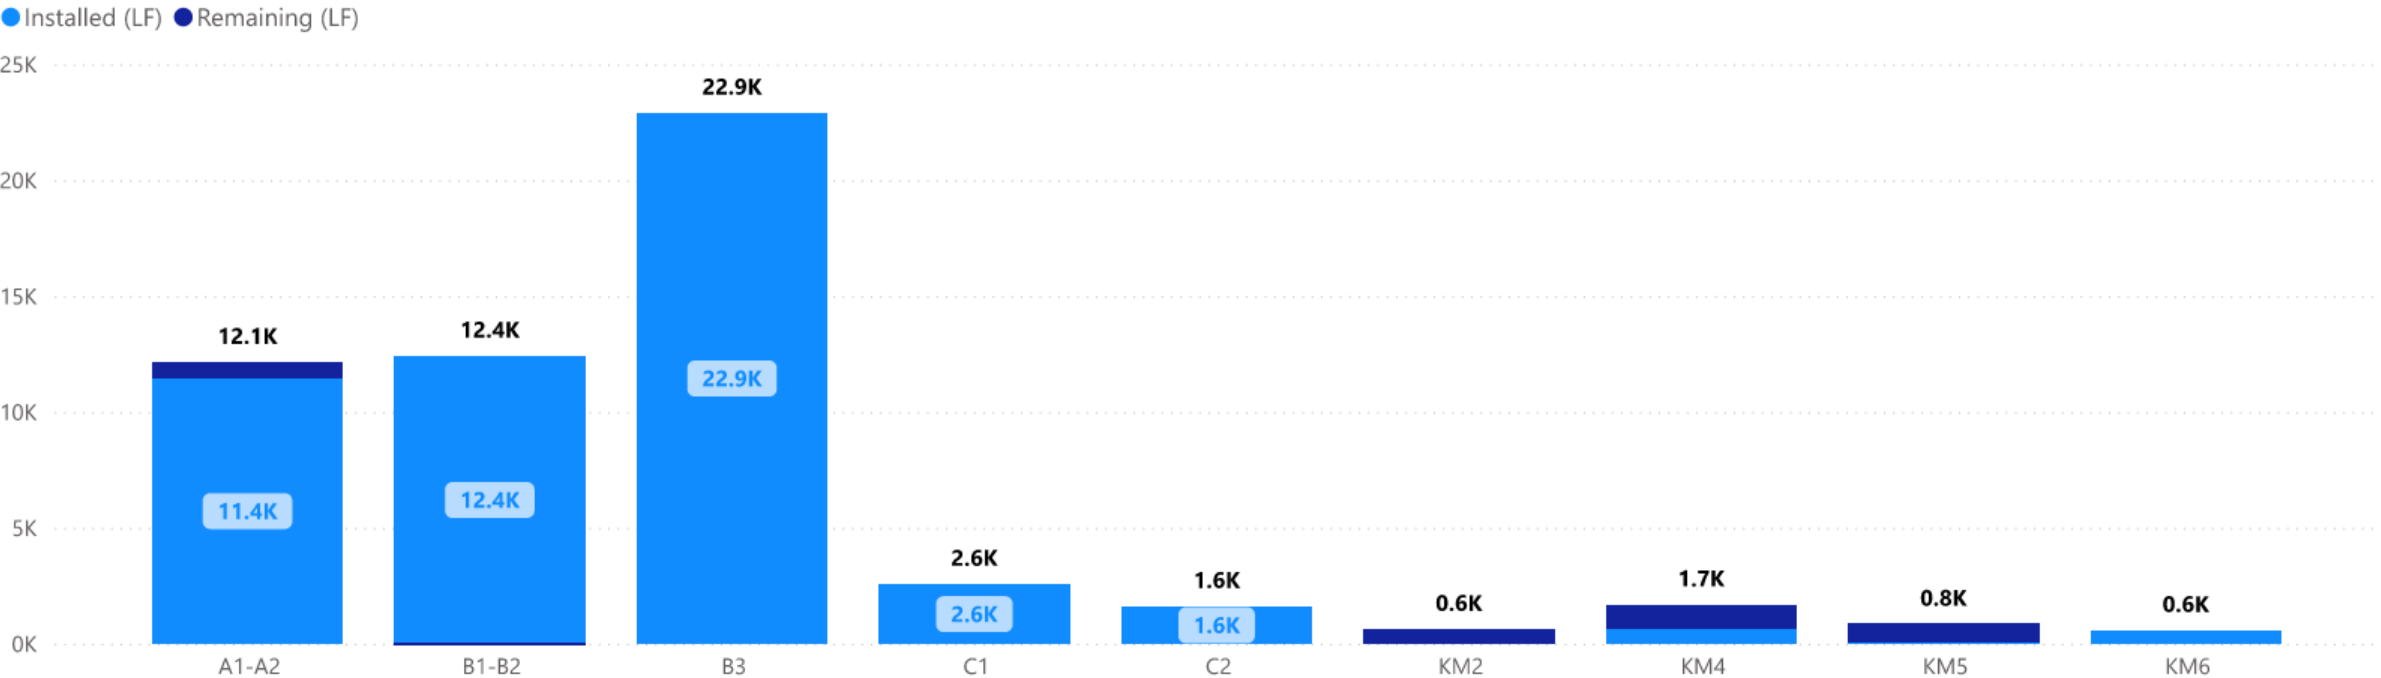

Segment B1|B2

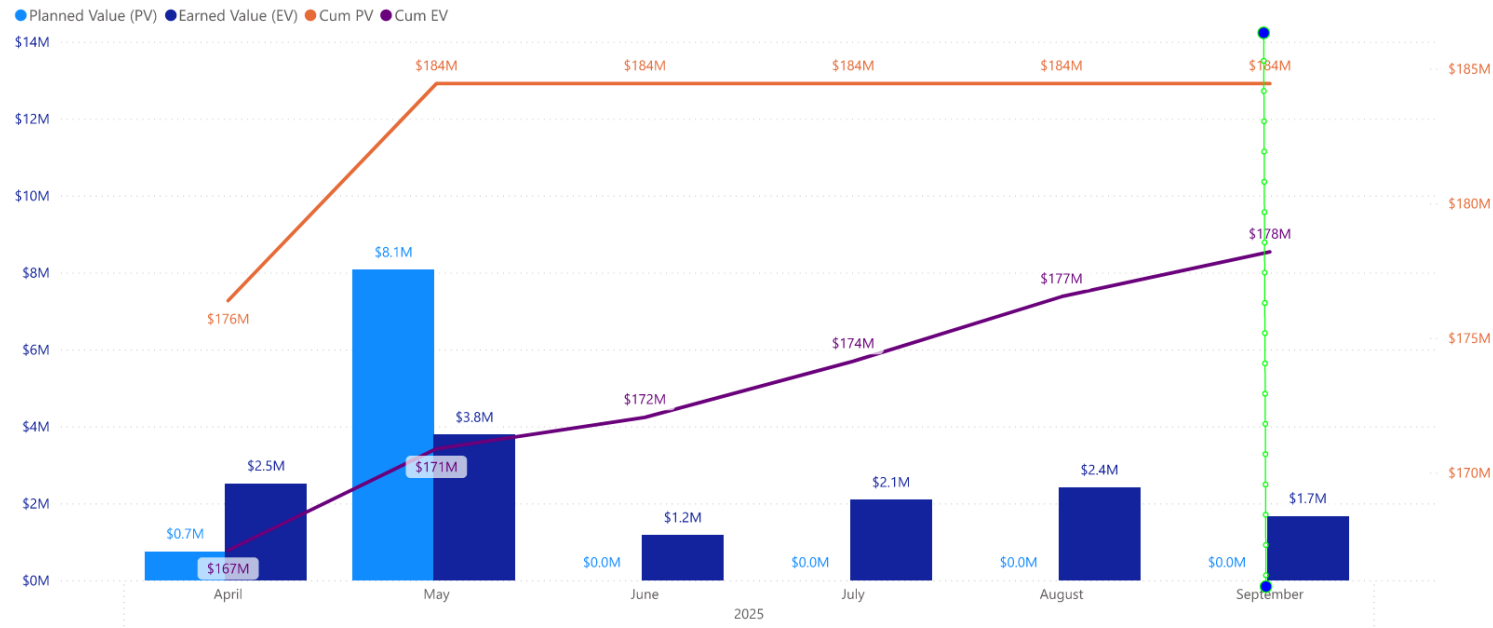

SWSP Segment B1-B2



Performing 96-In Walkthrough Inspection



Installing Security Fencing at BFV Site



Sod & Fence Installation E of Veterans Memorial


Project Name

B3

4/25/2025

9/25/2025

Segment B3

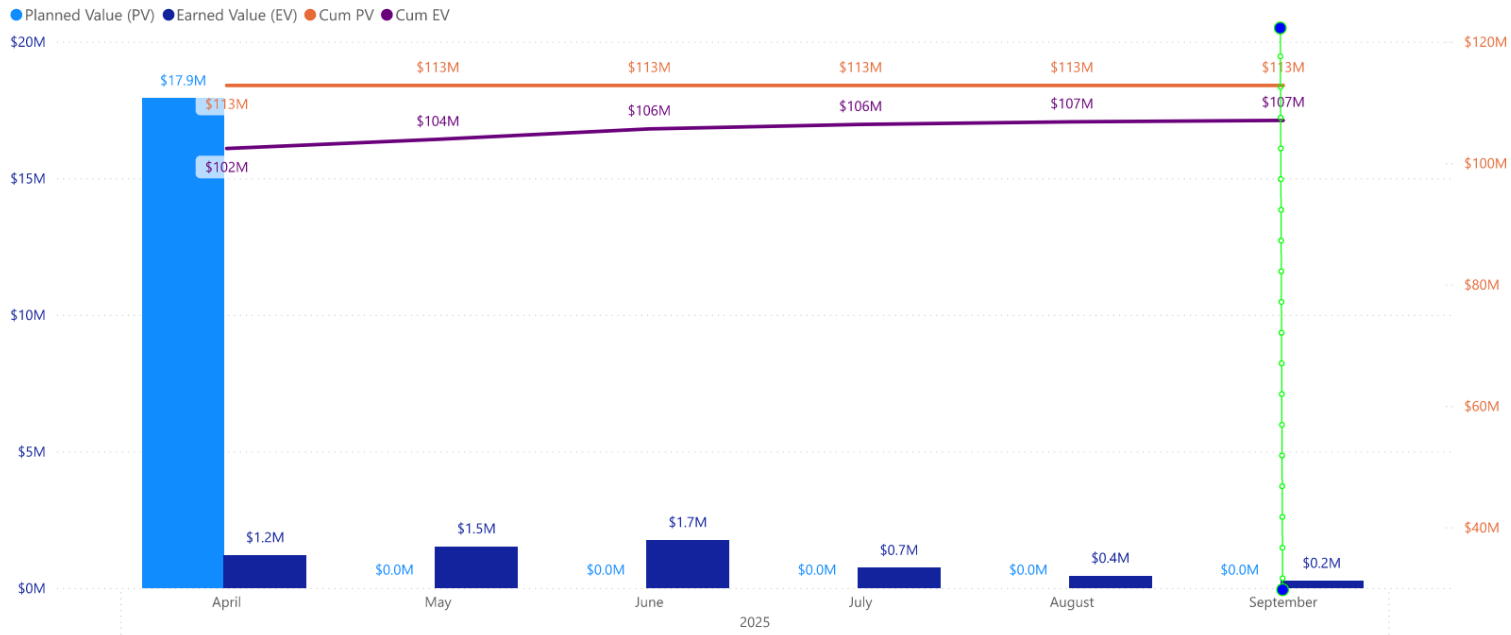

SWSP Segment B3



Site 1 – BFV Vault




Site 1 – BFV Commissioning Ongoing





Site 1 – BFV Electrical Installation Ongoing

Central Pump Station

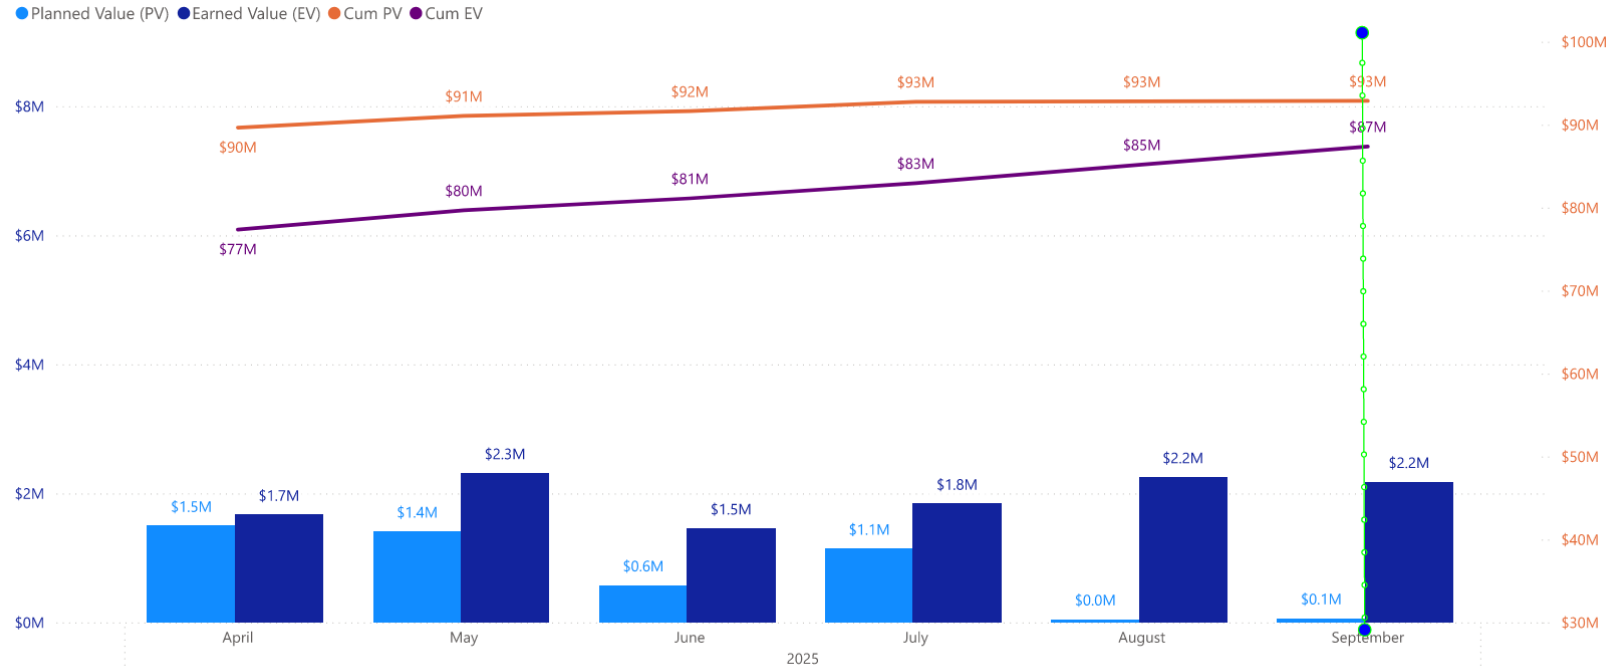


SWSP Central Pump Station

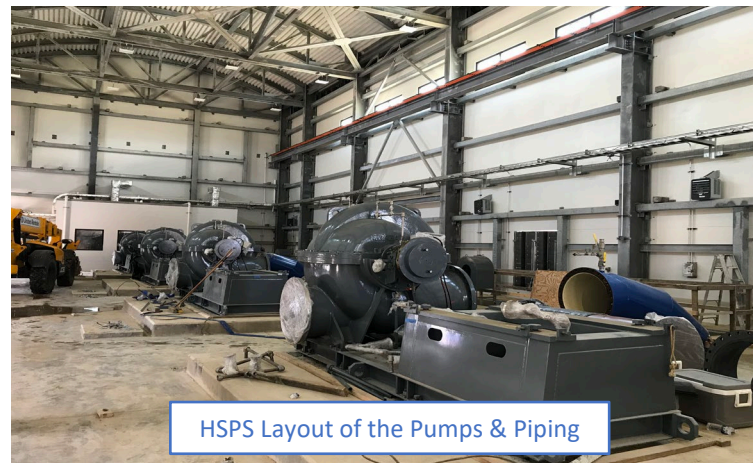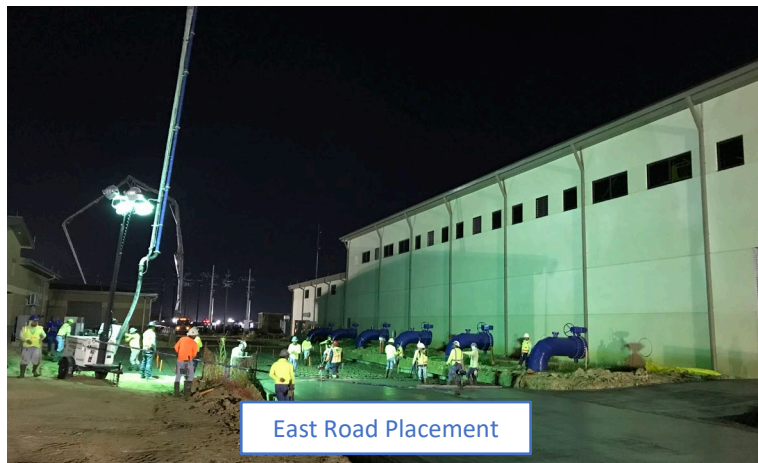


Project Name
 A1-A2
 4/25/2025 9/25/2025

Segment A1|A2

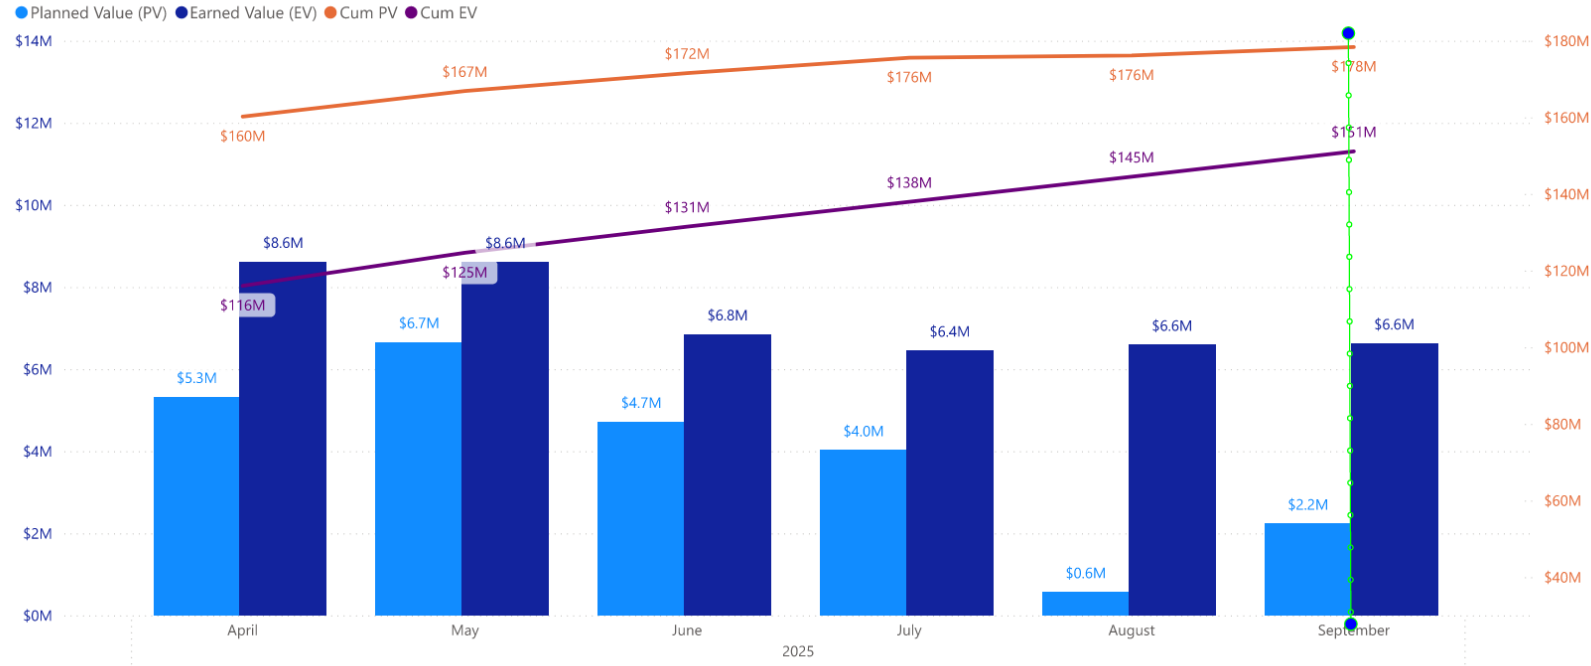


SWSP Segment A1-A2


Re-Pump Station

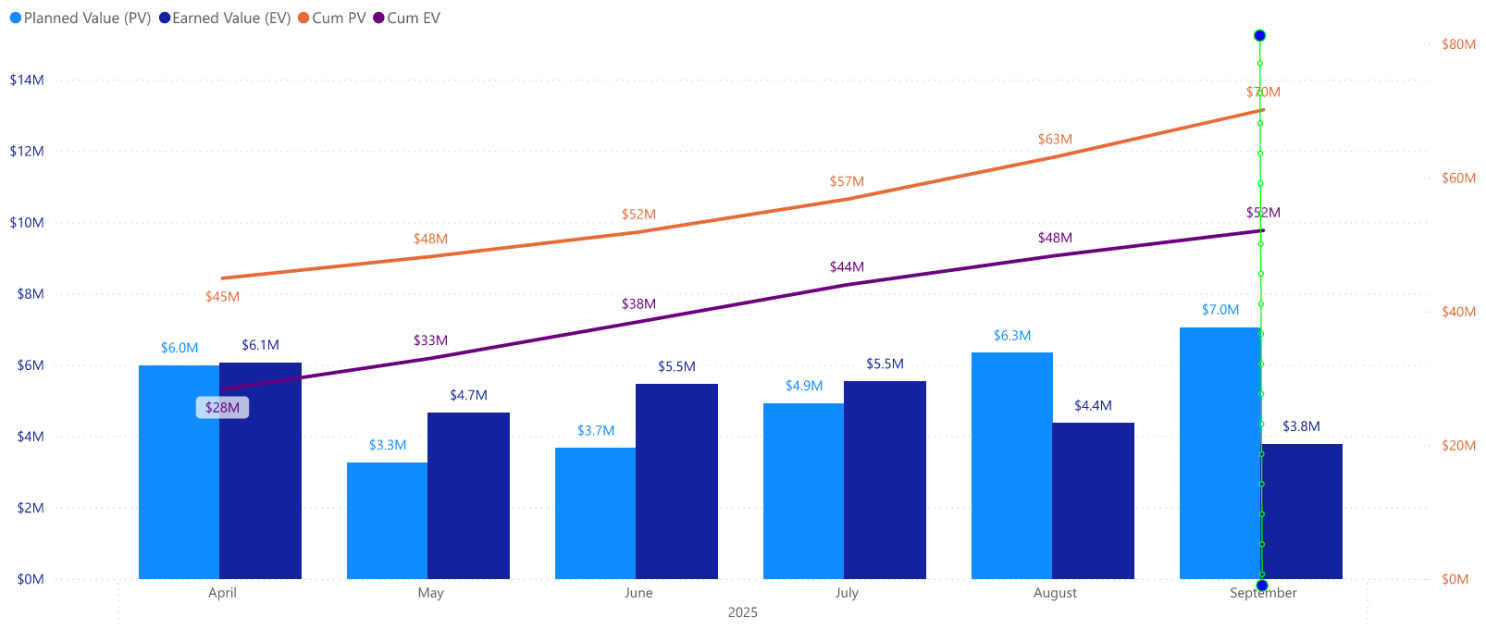

SWSP Repump Station

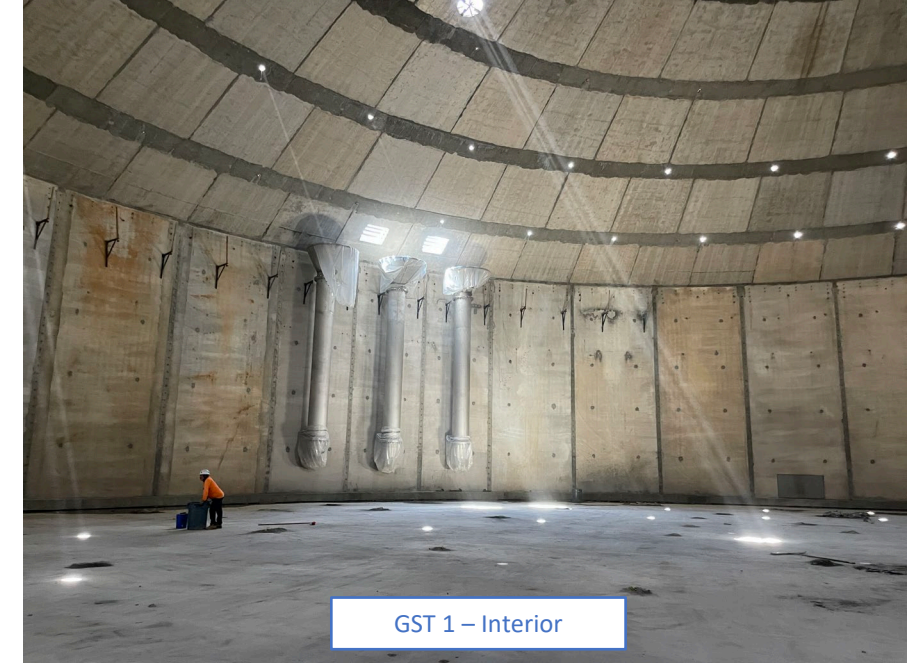

SWSP Northeast Meter Station

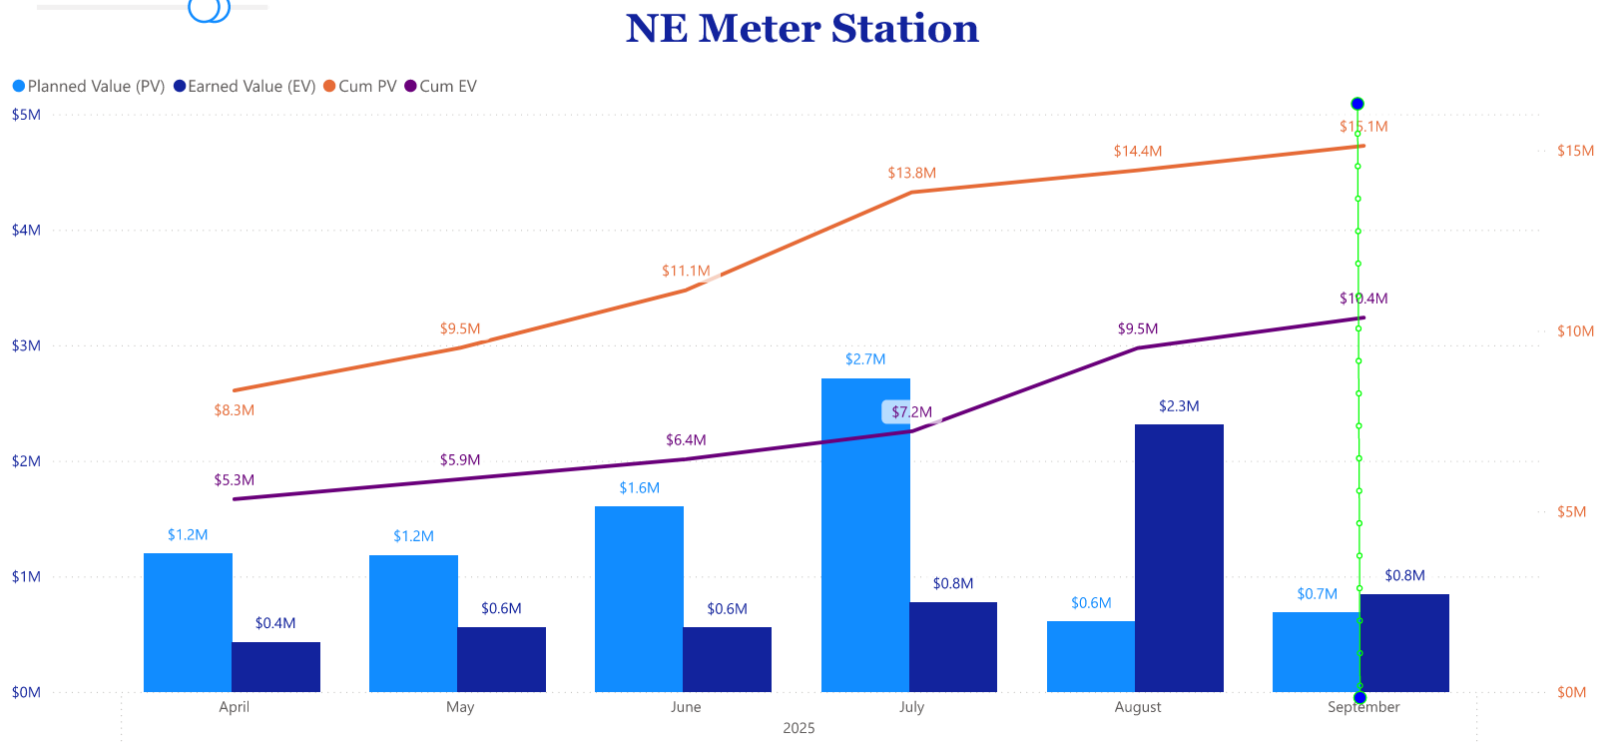

Perimeter Fence Installed



Generator Installed



Cla Val Enclosure being Installed



Project Name

KM4


4/25/2025

9/25/2025


Segment KM-4

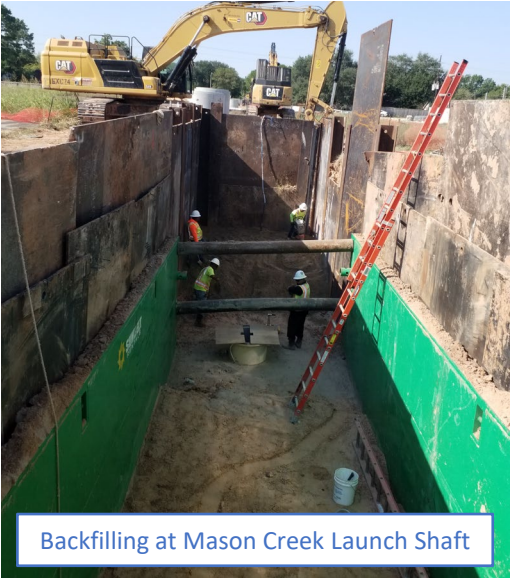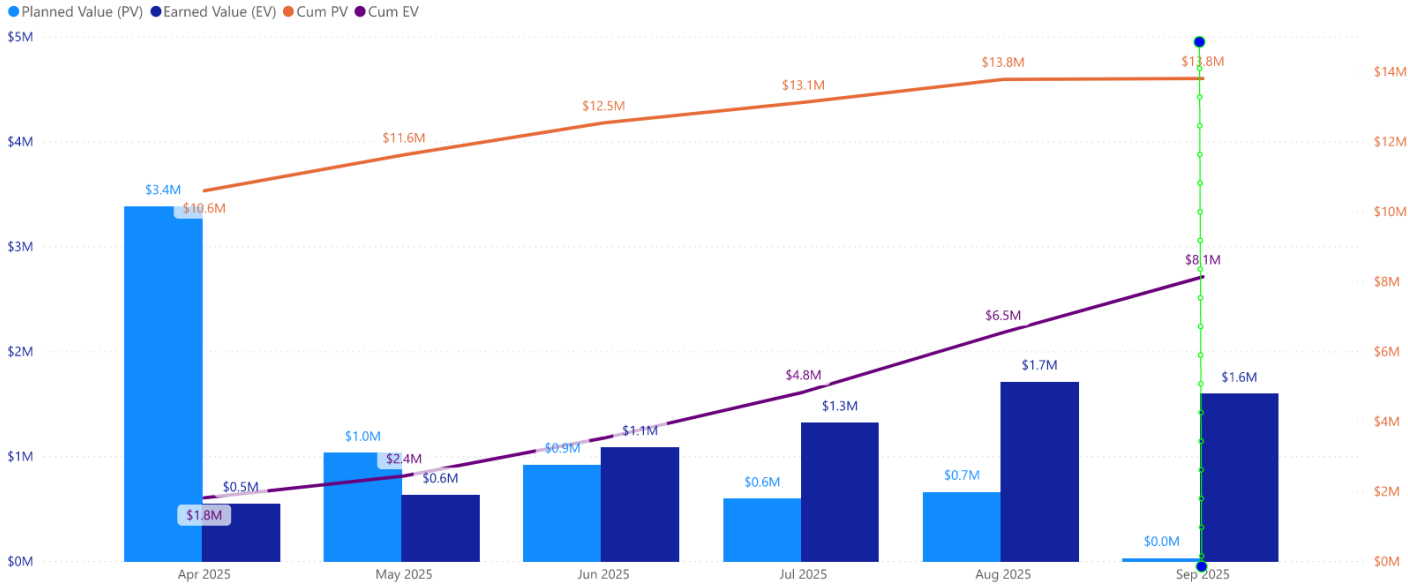


Segment KM-6

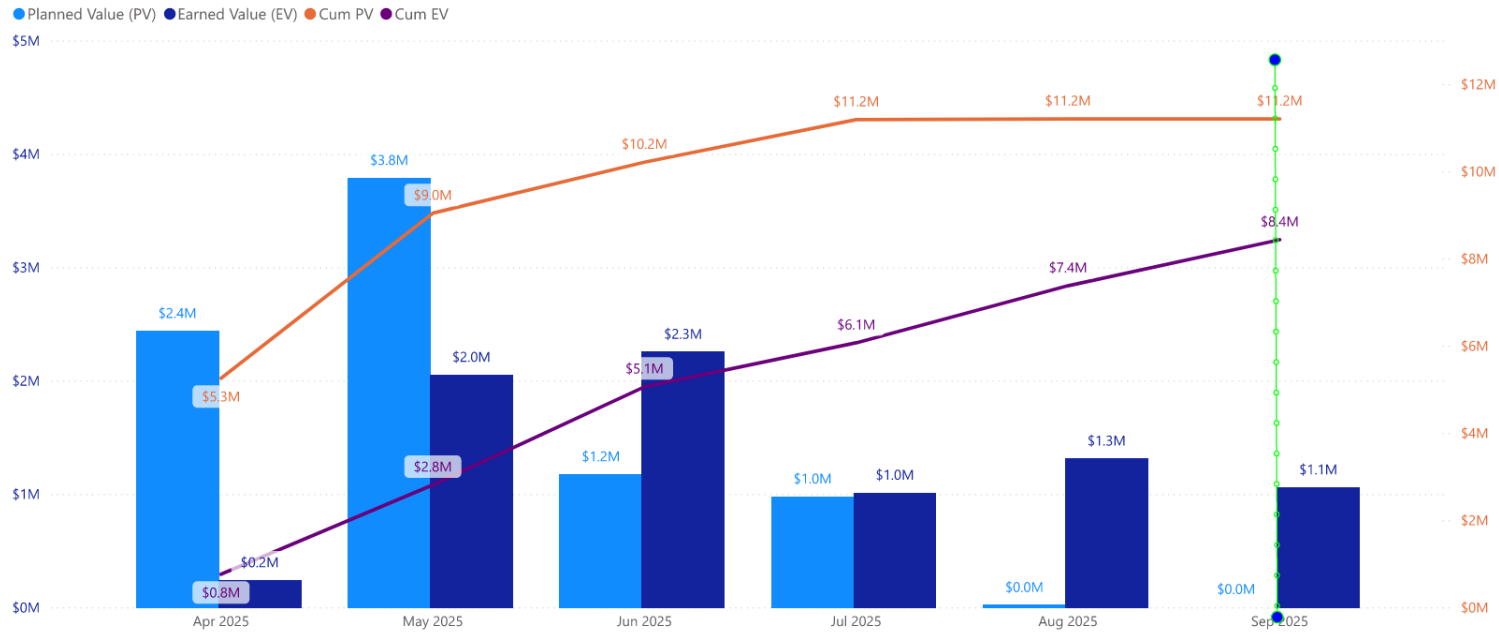

Segment KM-5

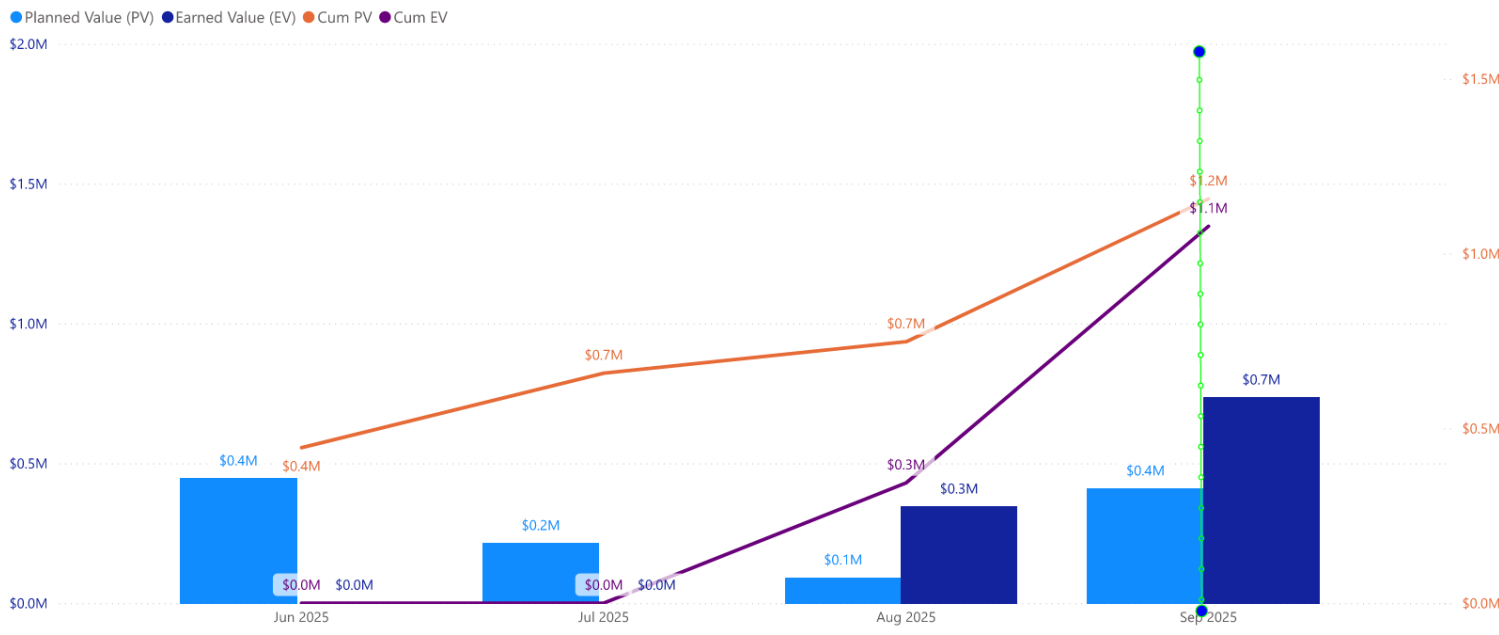

I-10 METER STATION

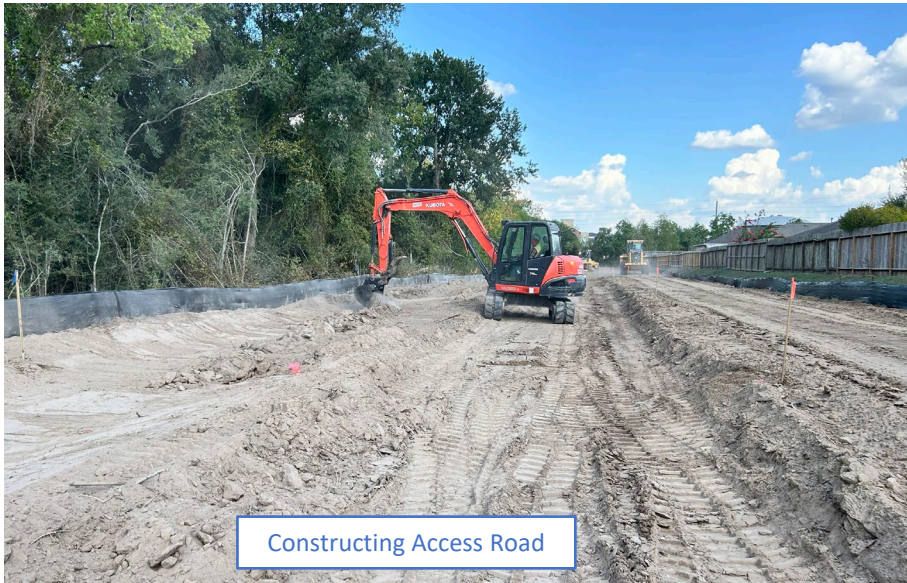

CIP CONTRACTS



Contract 64 – Shaft at Bear Creek



Contract 63 – 36-Inch Open Cut Waterline



Contract 65 – West Little York Tunnel Machine Retrieval



Contract 65 – West Little York Tunnel Liner Complete
