

June 2026 Monthly Construction Status Report

Updated: 07.07.2026



CPS – Chemical Injection Piping Installed

WHCRWA Ongoing Construction Projects

Central Pump Station

CONSTRUCTION OF A CENTRAL PUMP STATION THAT WILL RECEIVE WATER FROM THE RE-PUMP STATION AND THEN TRANSFER WATER TO MUDS

Segment A1-A2

11 MILES OF 96-INCH WATER LINE FROM HOPPER RD. TO THE WHCRWA METER STATION NEAR THE NEWPP, INCLUDING SWSP DISINFECTION

RePump Station

CONSTRUCTION OF A 160 MGD REPUMP STATION FACILITY INCLUDING TWO 10 MILLION GALLON TANKS

NorthEast Meter Station

CONSTRUCTION OF A METER STATION AT COH/WHCRWA INTERFACE

Kinder Morgan 1, 2, 3, 4, 5, & 6 - (6 Projects)

6 MILES OF 66-INCH AND 1,300 LF OF 84-INCH WATERLINE FROM SEGMENT C1 CONNECTION TO THE I-10 METER STATION


I-10 Meter Station

CONSTRUCTION OF A METER STATION AT THE NFBWA INTERFACE

CIP Projects

CONTRACT 51
CONTRACT 63
CONTRACT 64
CONTRACT 65

Current SWSP Construction Projects Overview

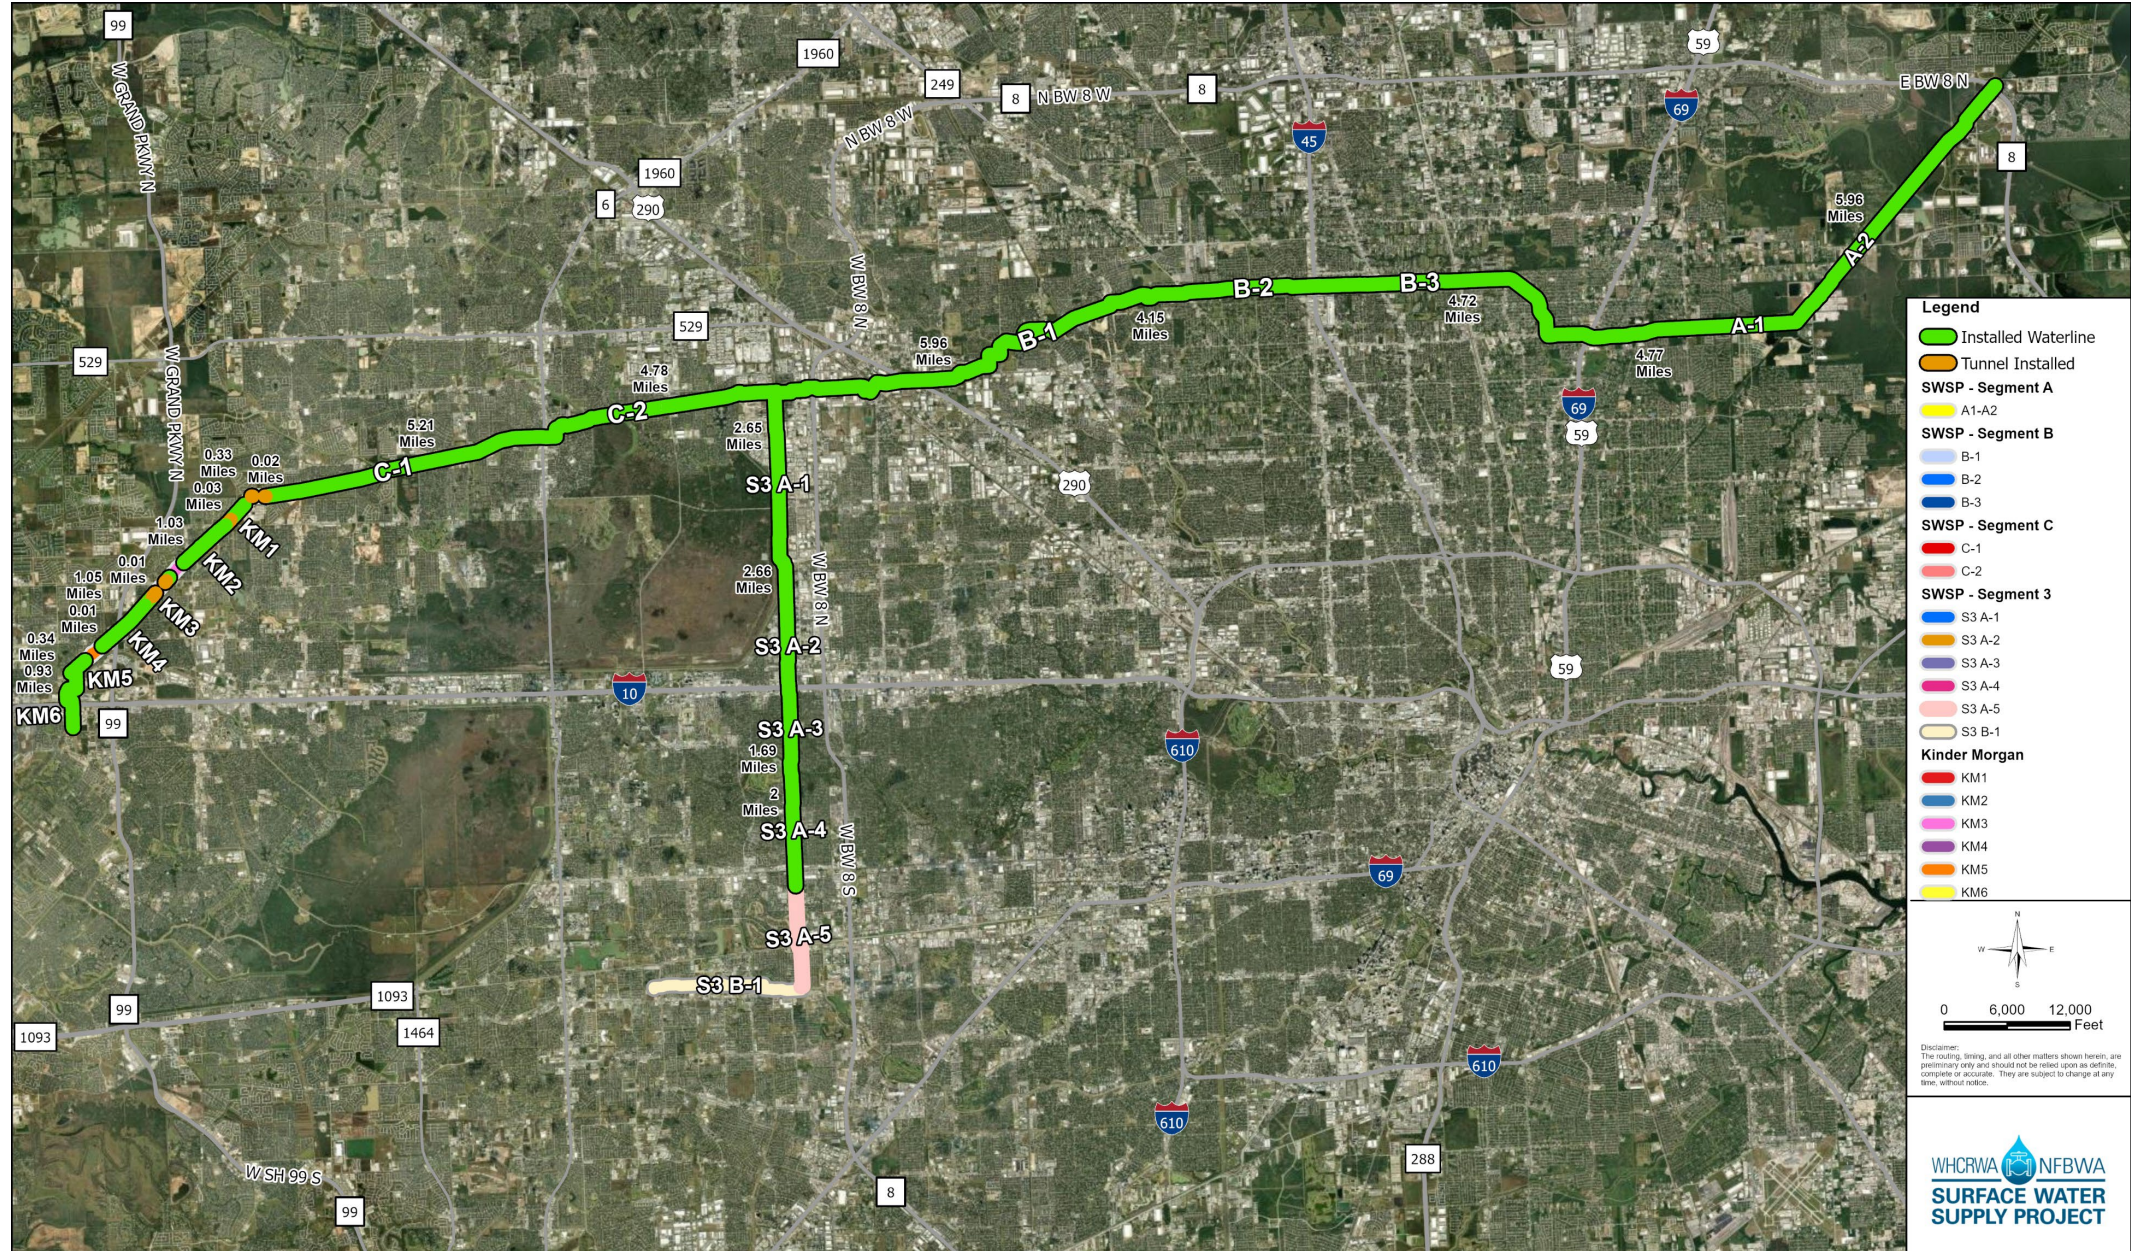


Tunneling (LF) by Project

● Installed (LF) ● Remaining (LF)

65K
Budgeted

64K
Installed

0K
Remaining

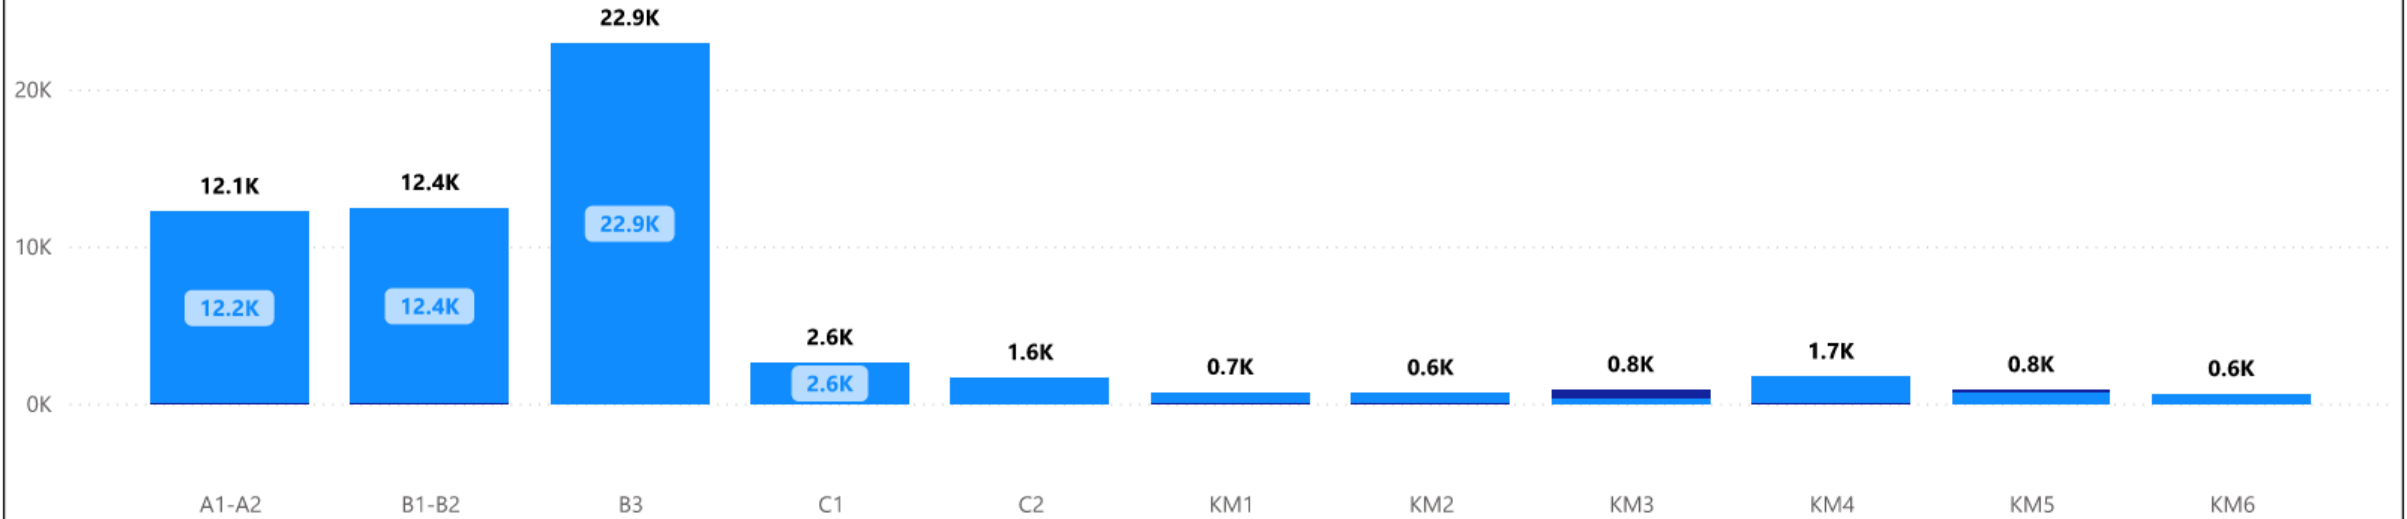


Open Cut (LF) by Project

● Installed (LF) ● Remaining (LF)


211K
Budgeted

202K
Installed

9K
Remaining

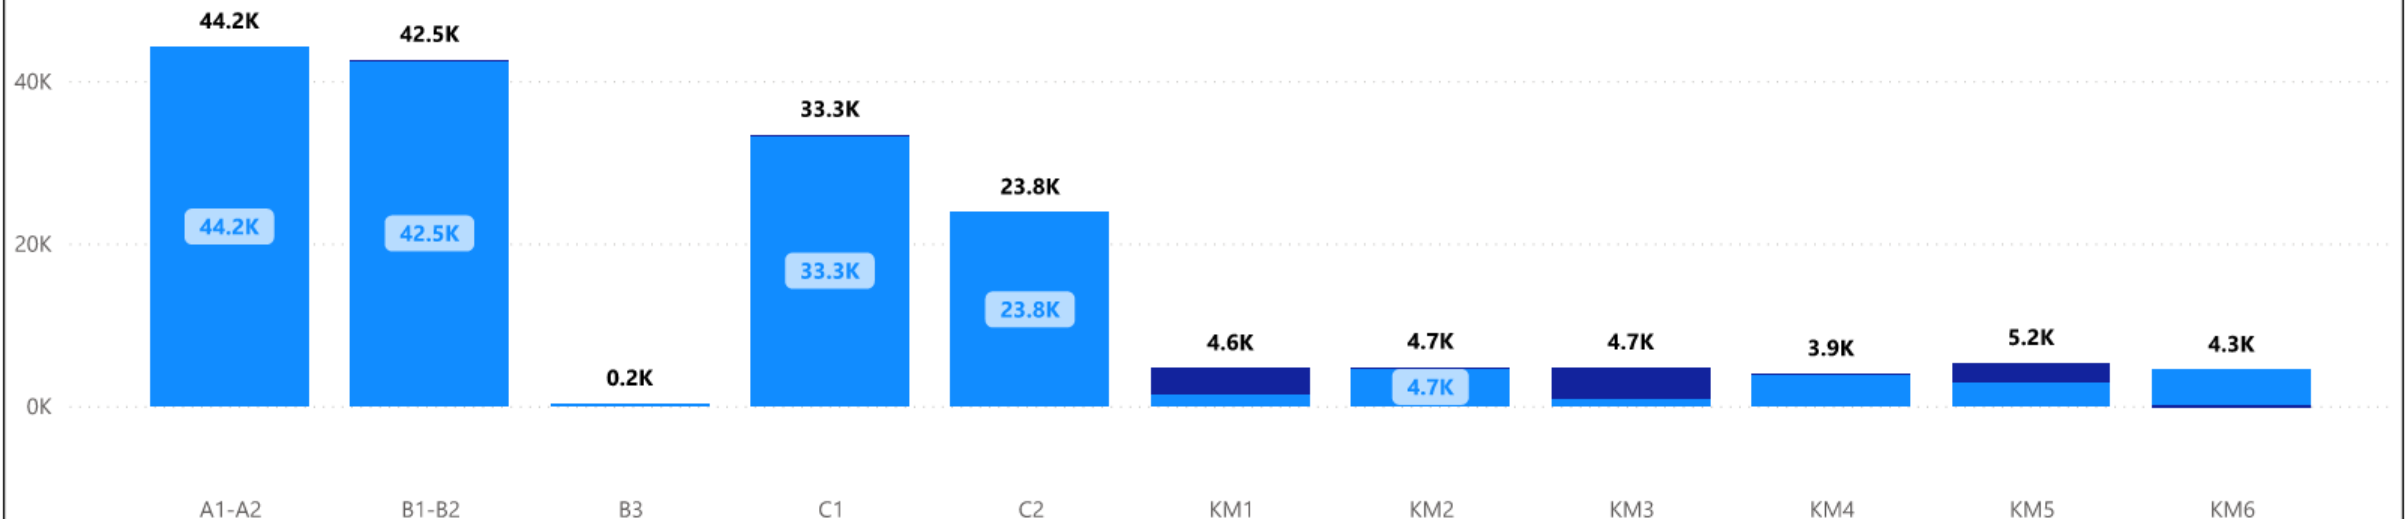


Construction Progress – Segment A1-A2

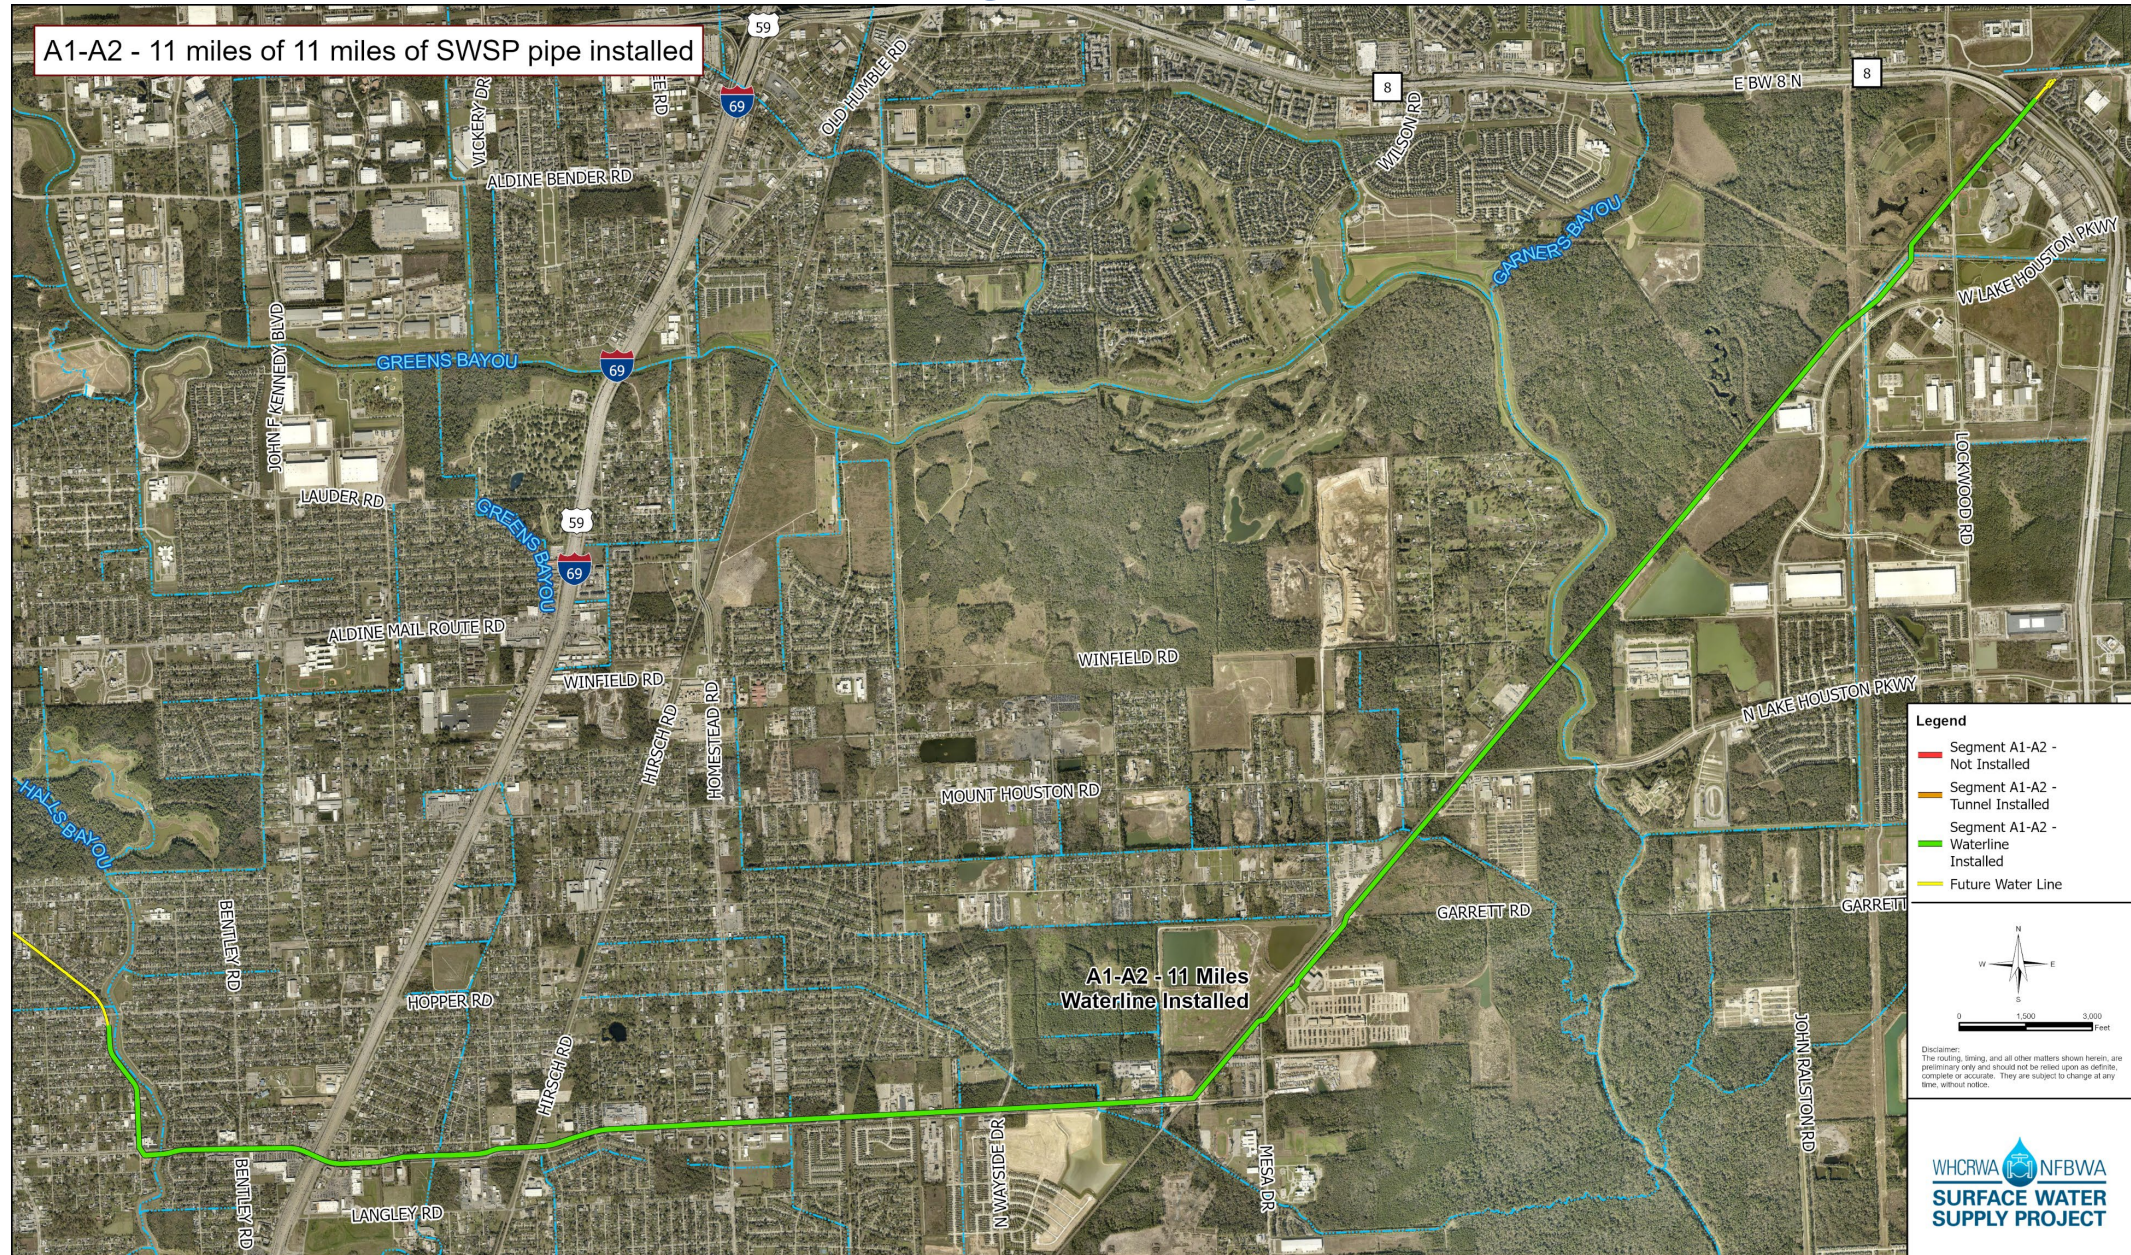

Segment A1|A2

Planned Value (PV) Earned Value (EV) Cum PV Cum EV

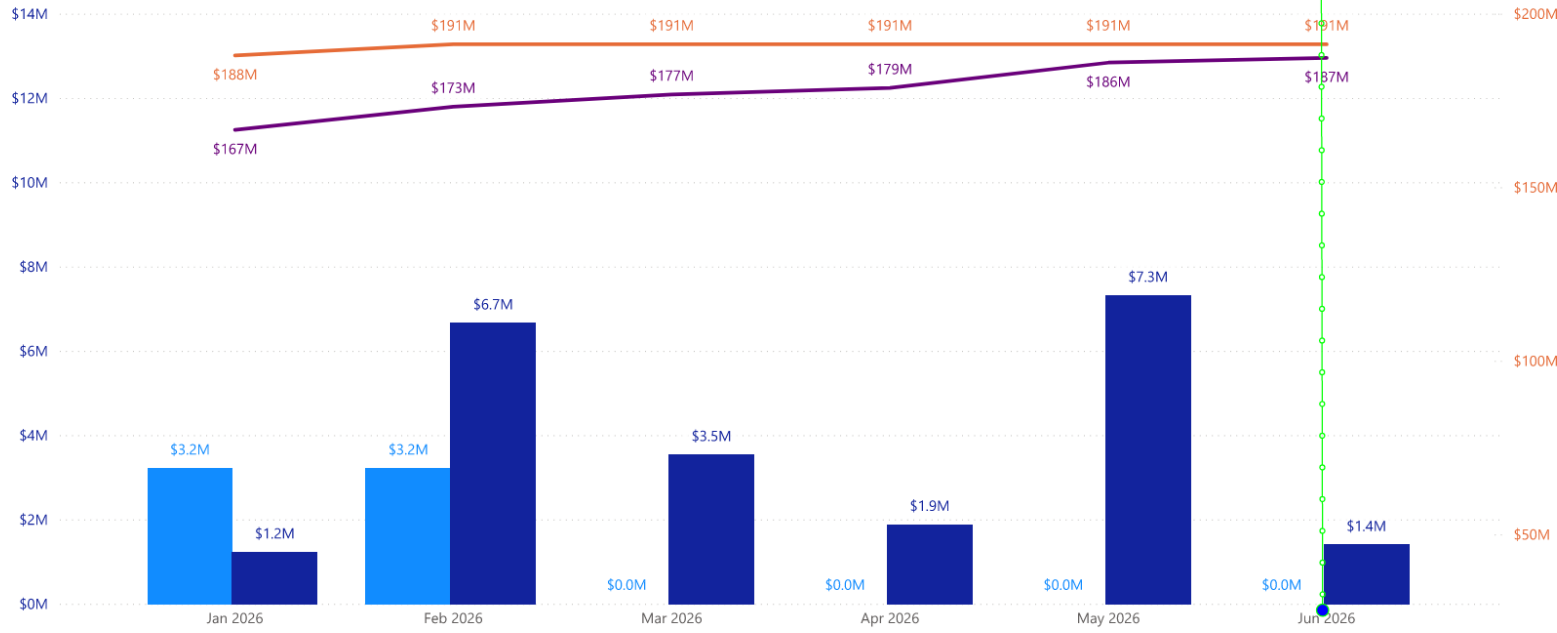


SWSP Segment A1-A2





Construction Progress – Kinder Morgan-1

KM1 – 666 feet of SWSP tunnel installed and 0.33 miles of 1 mile of SWSP pipe installed

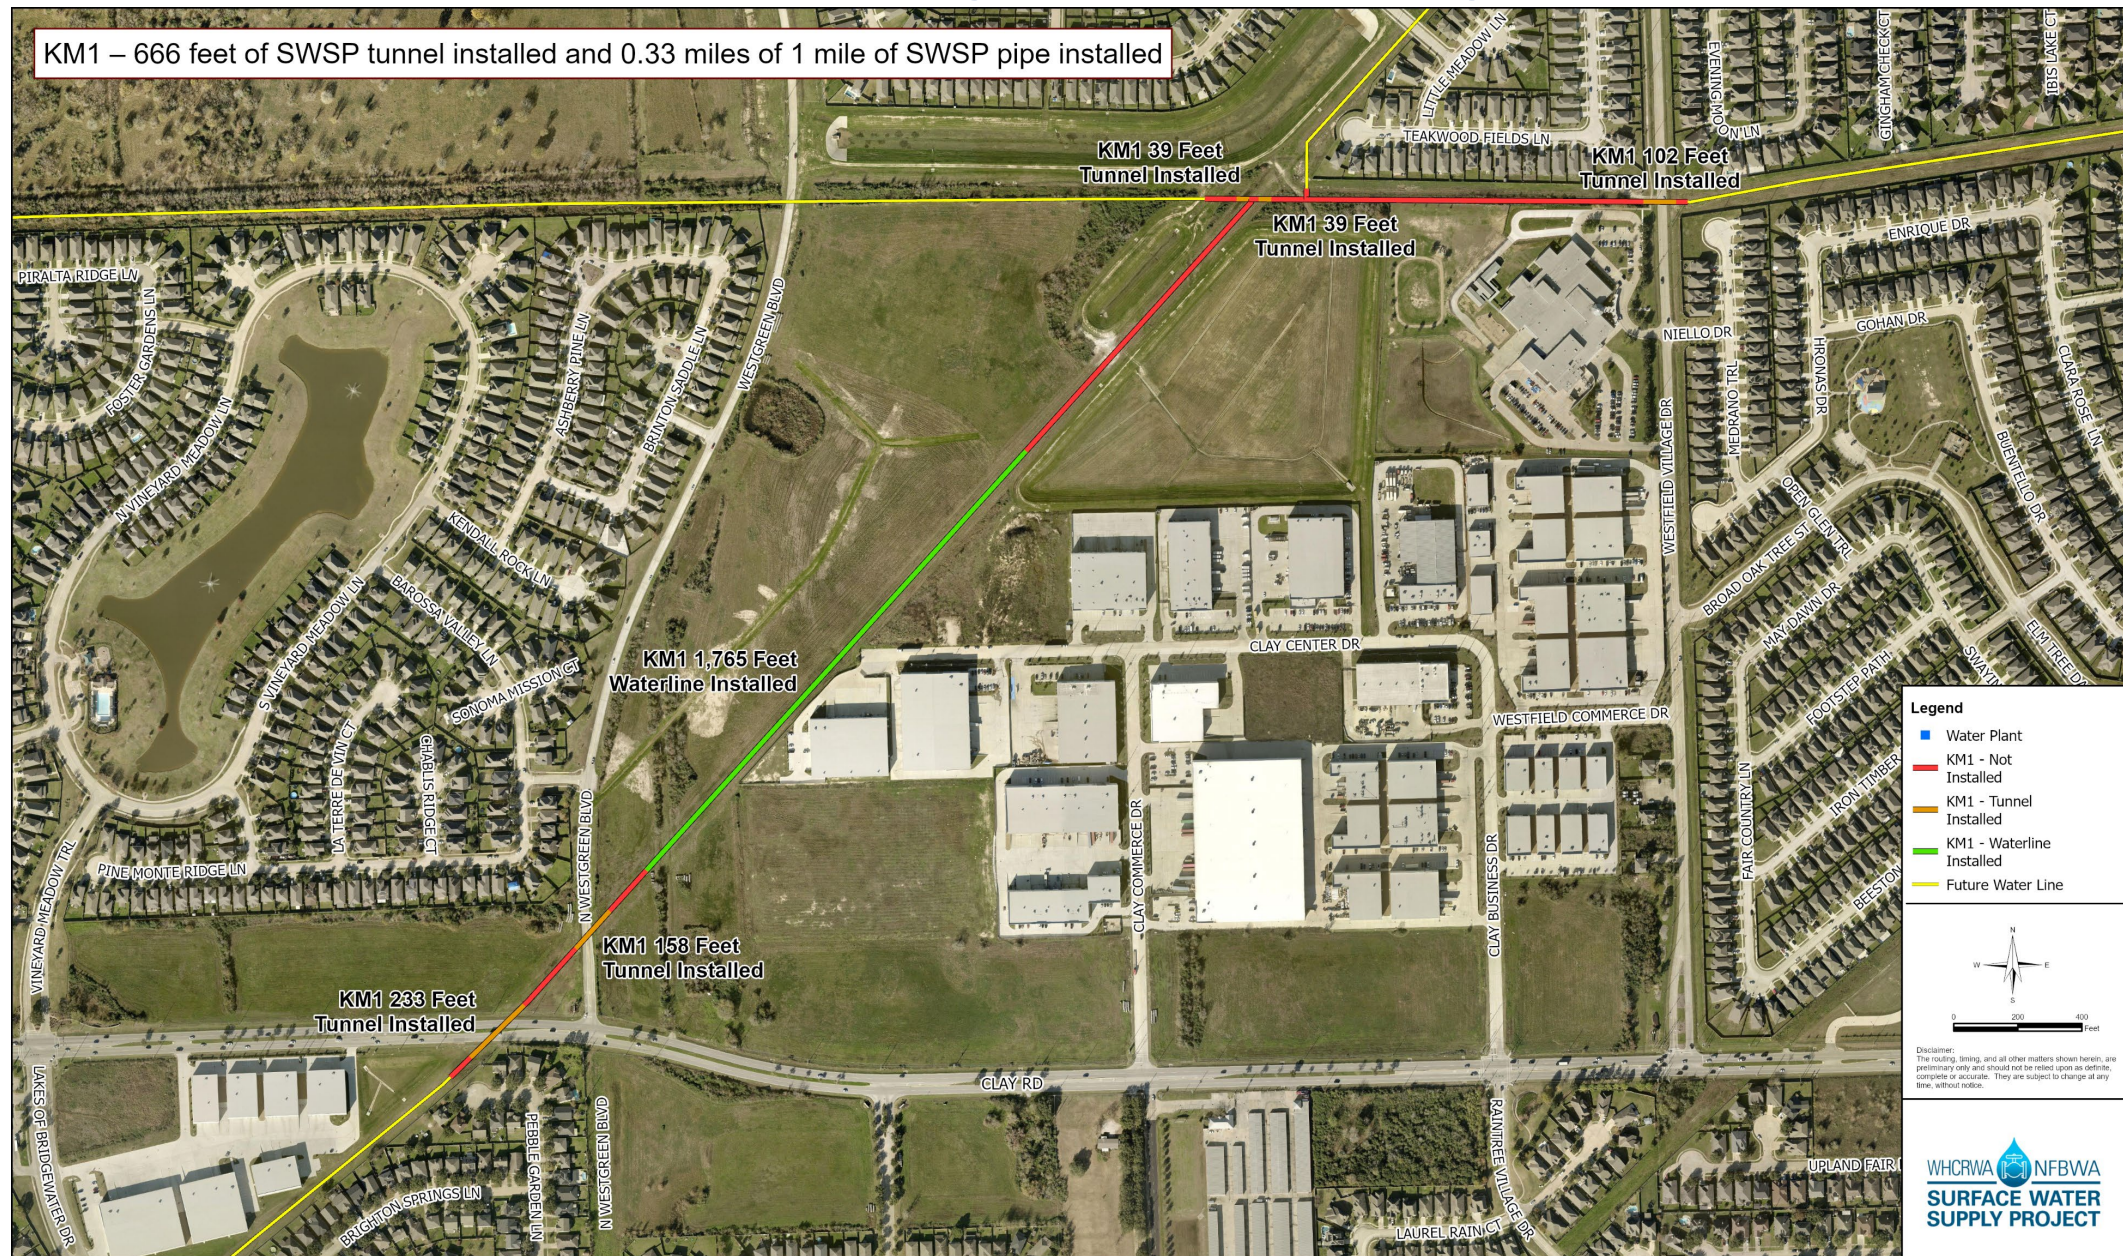


Kinder Morgan 1 - Construction Progress

Segment KM-1

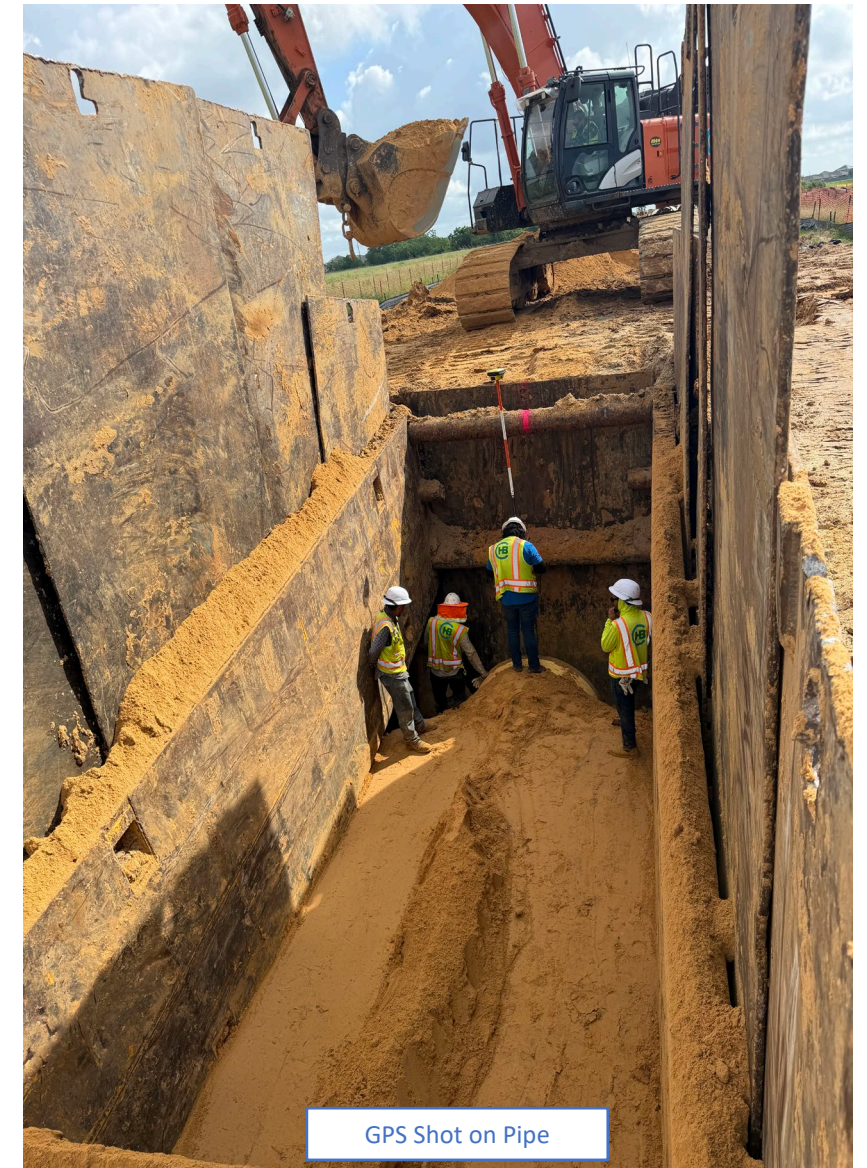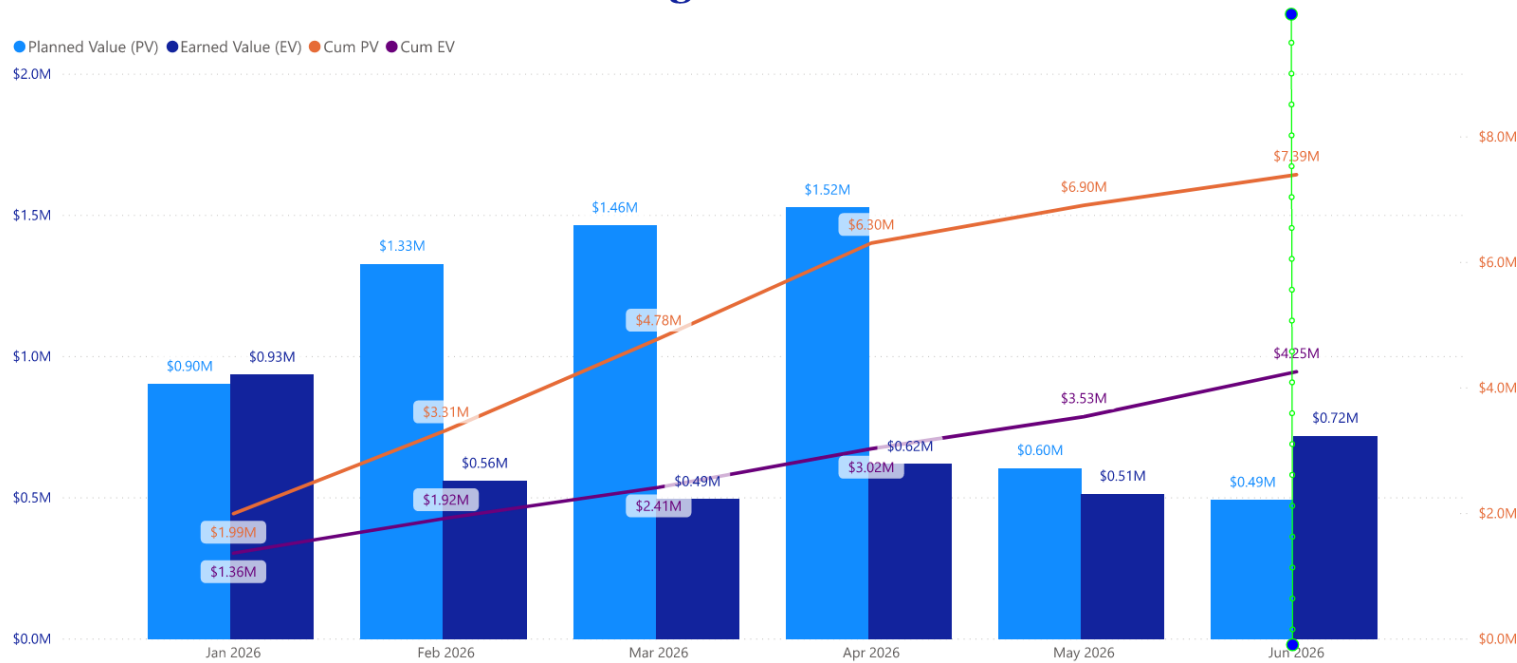


Construction Progress – Kinder Morgan-2

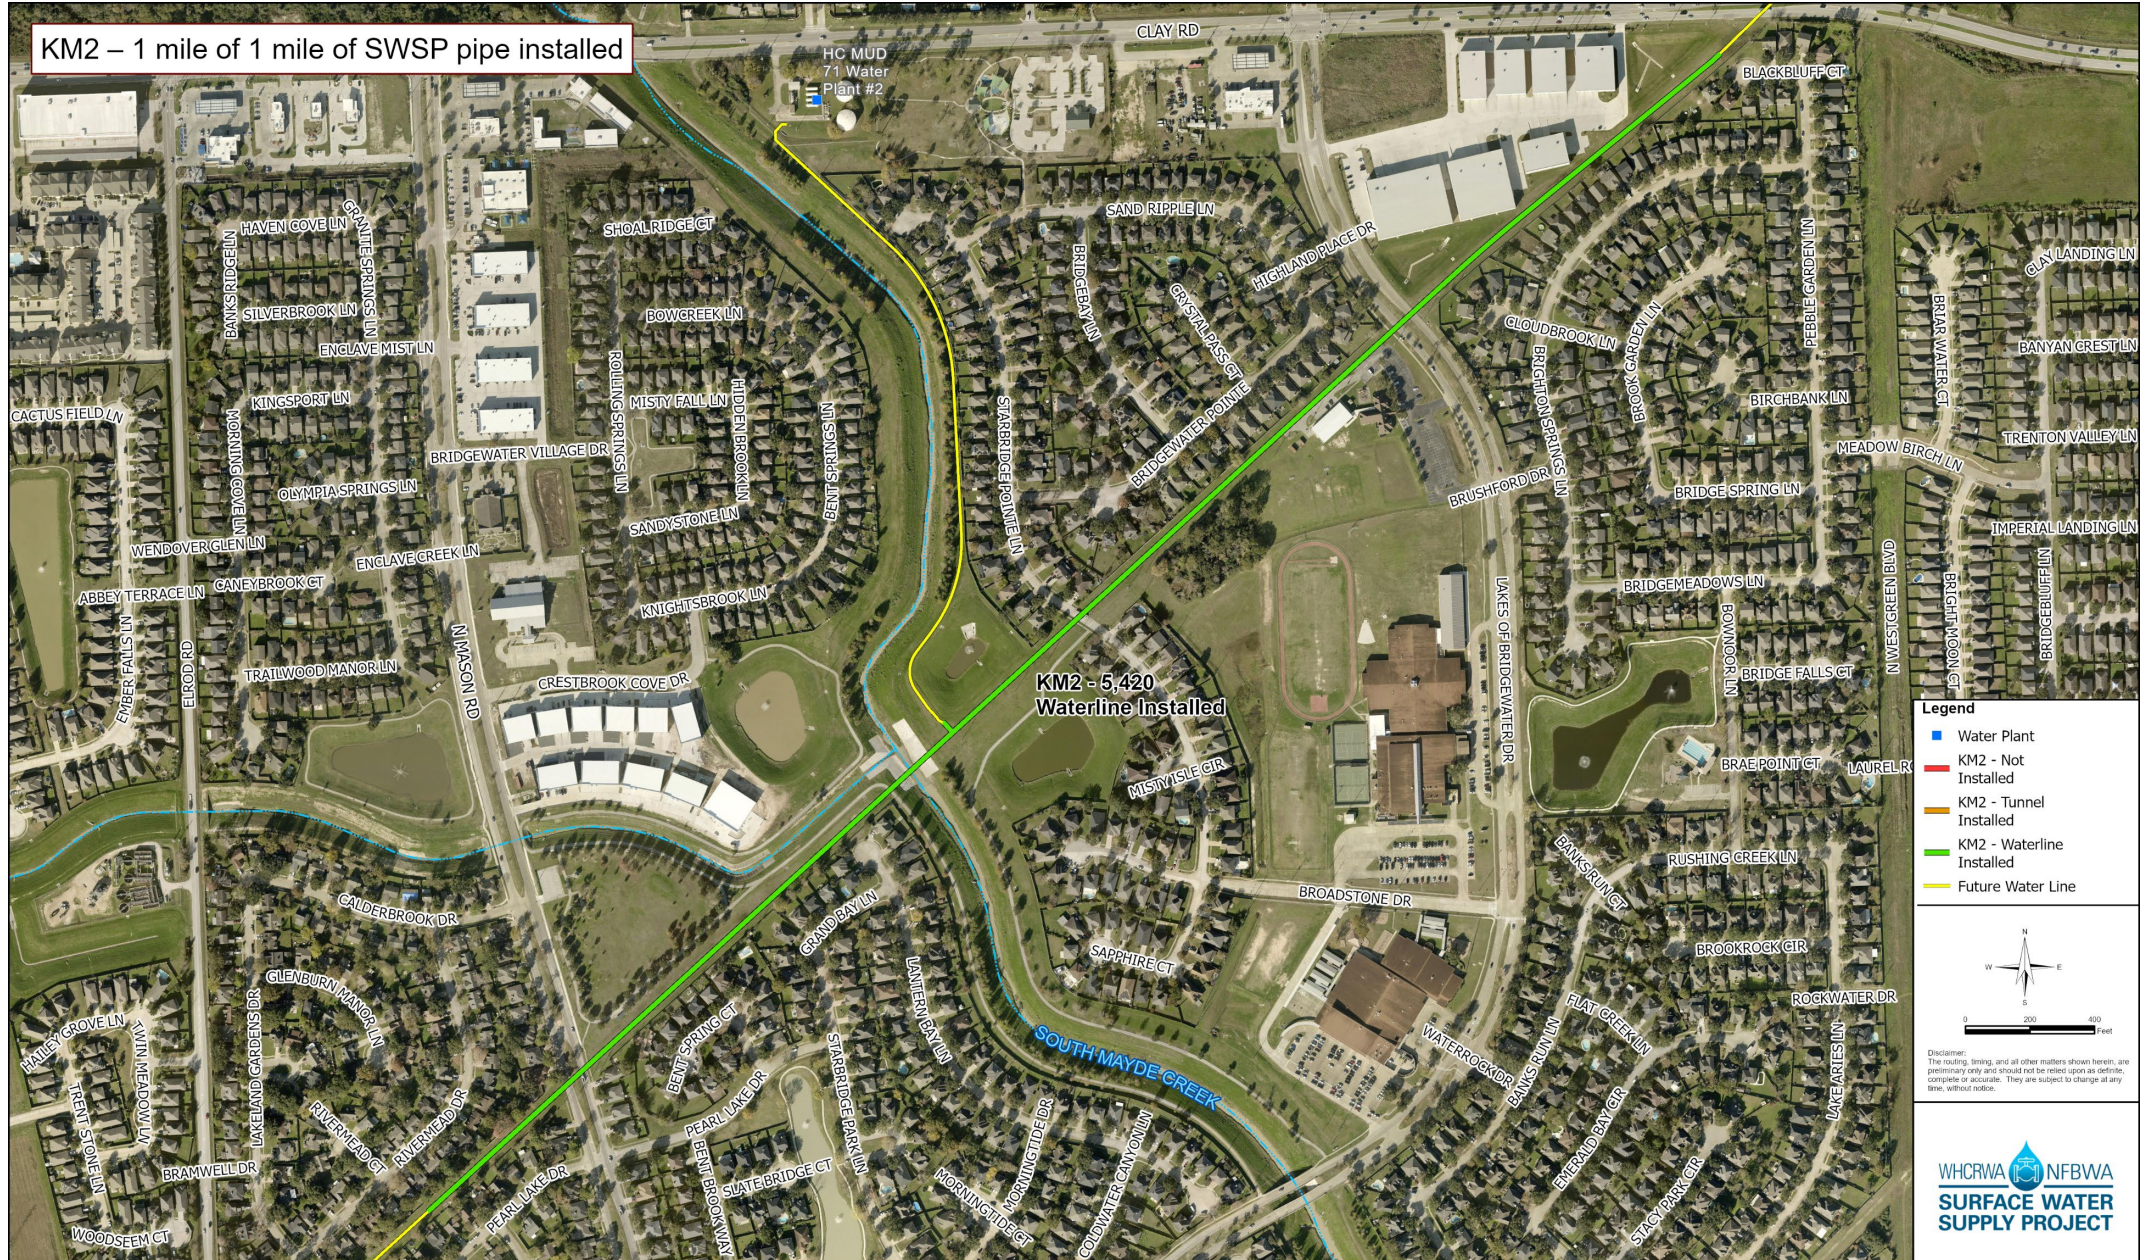

Project Name
KM2


1/25/2026 6/25/2026

Segment KM-2

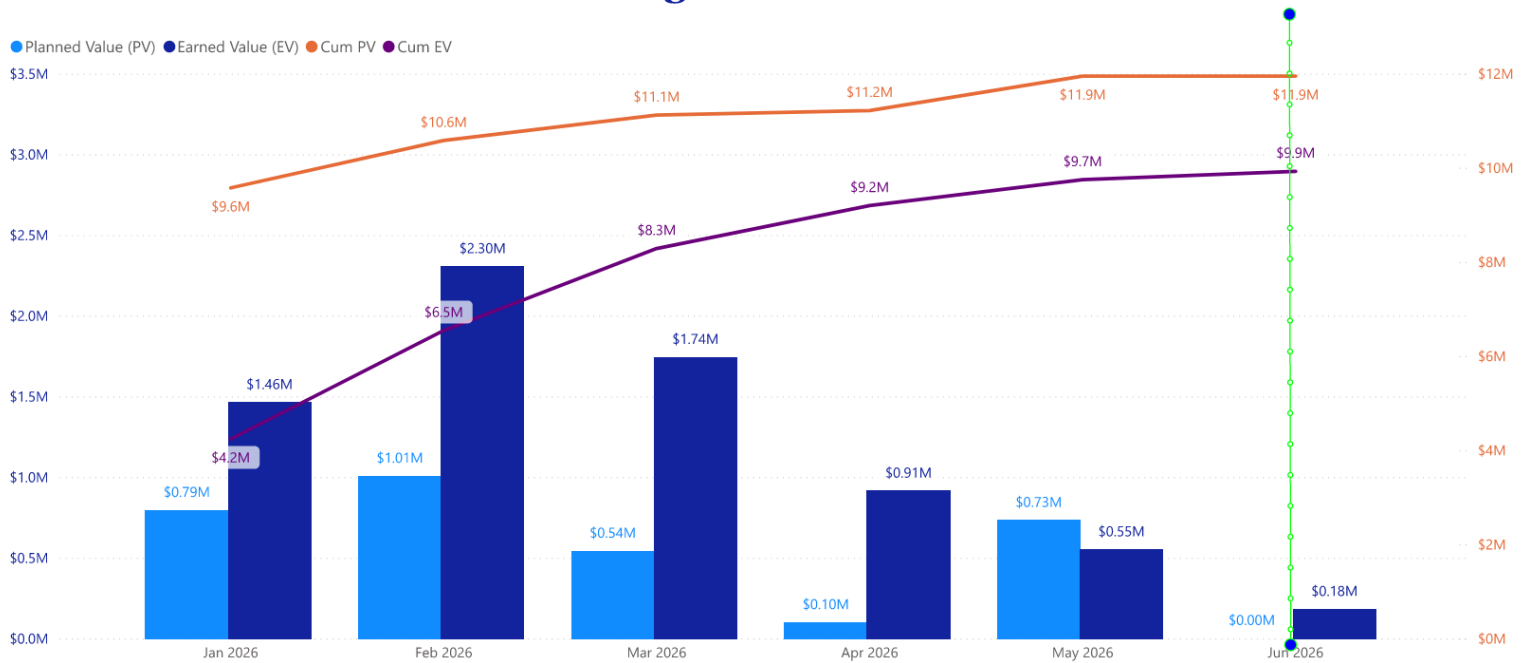

Construction Progress – Kinder Morgan-3

KM3 – 423 feet of SWSP tunnel installed and 0.21 miles of 1 mile of SWSP pipe installed

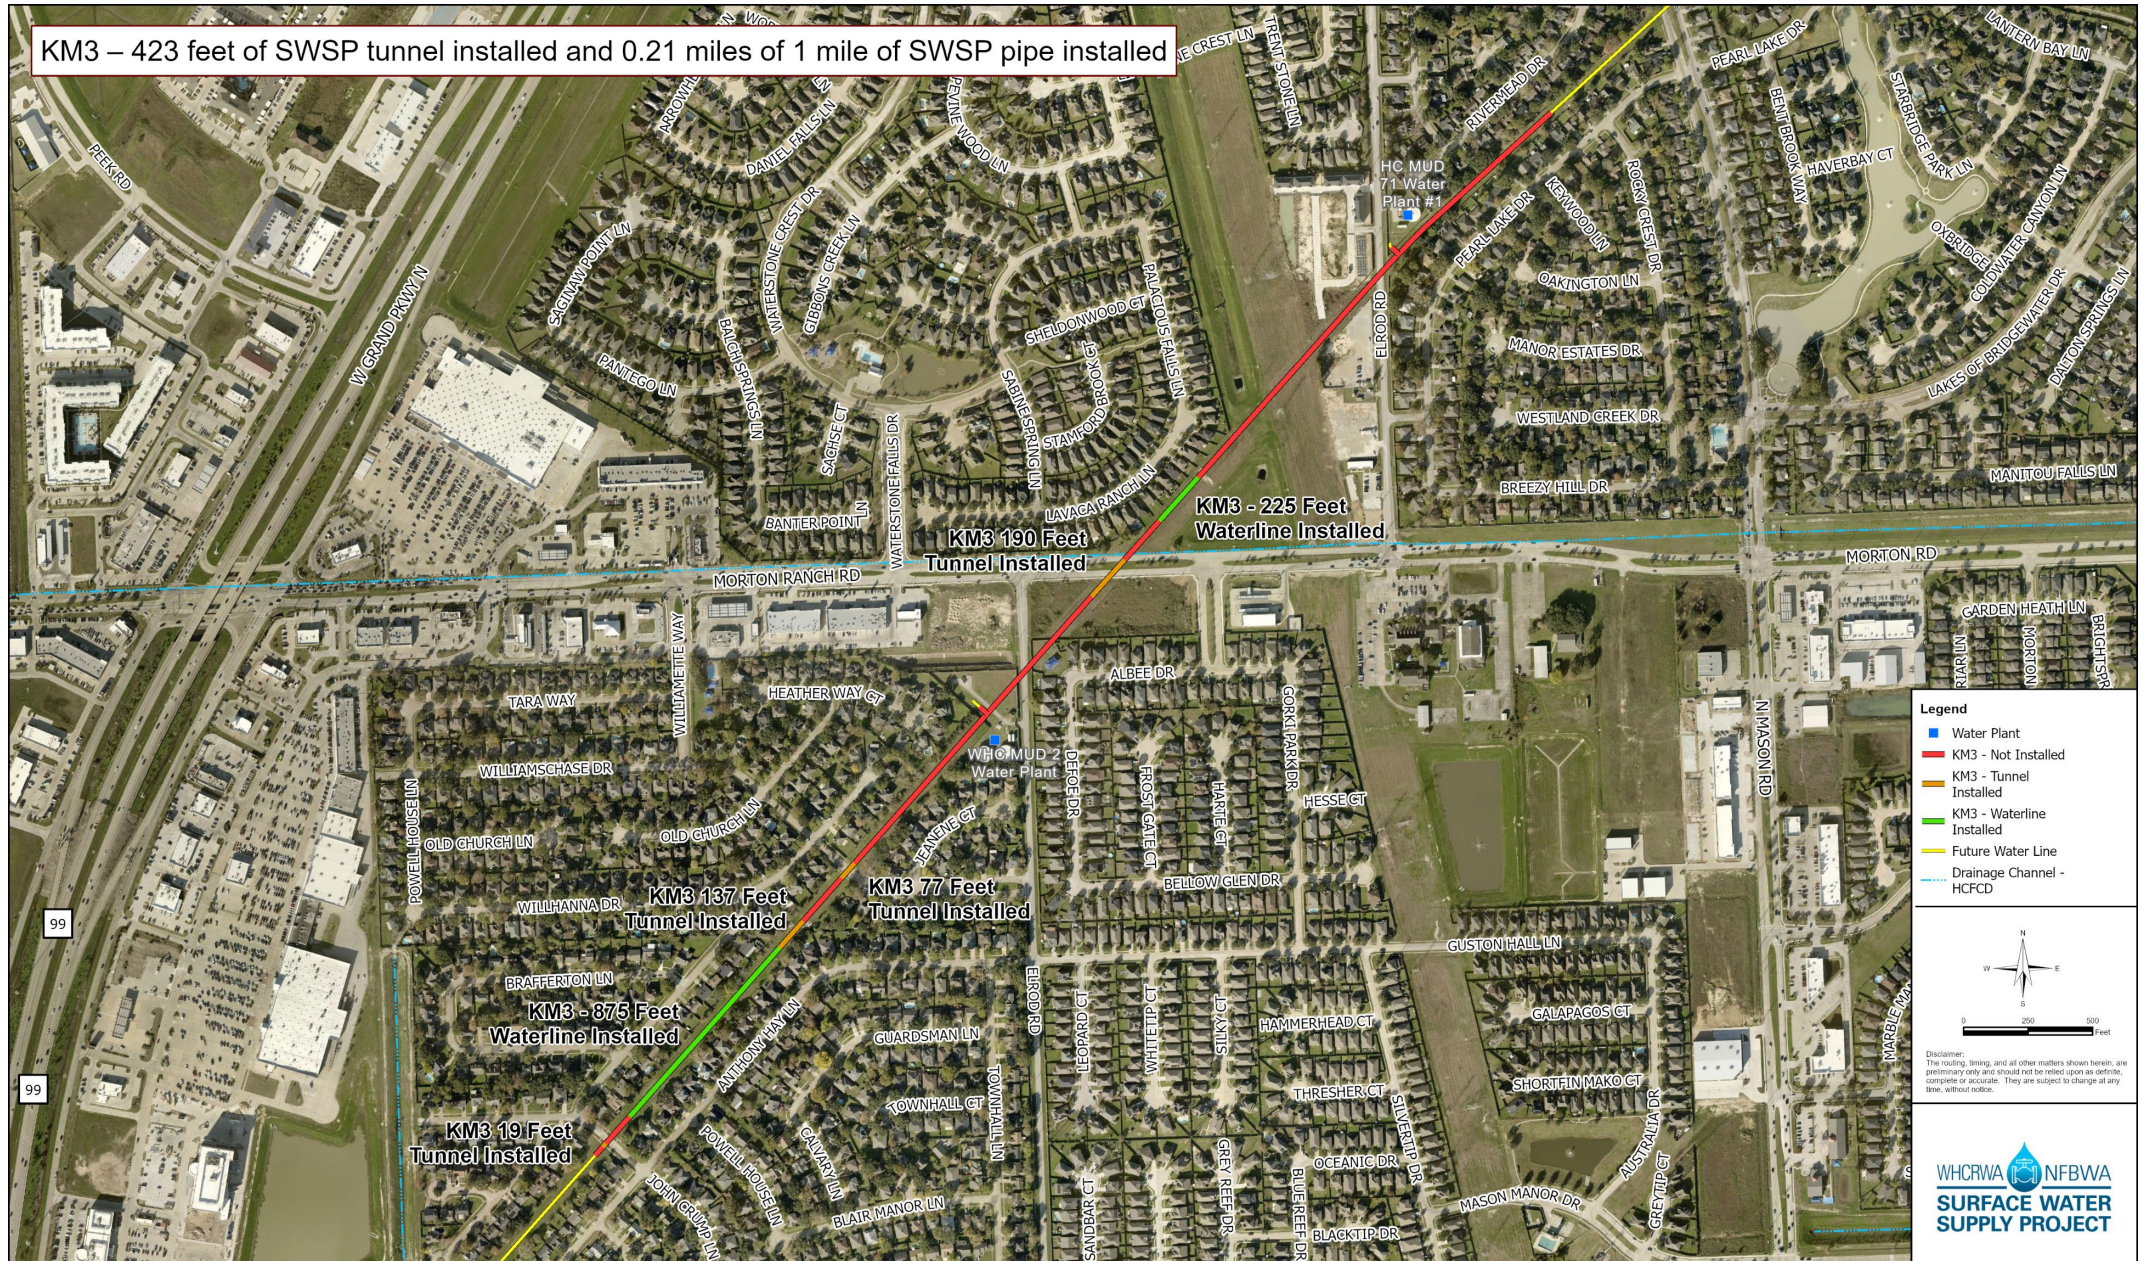


Project Name
KM3

1/25/2026 6/25/2026



Segment KM-3

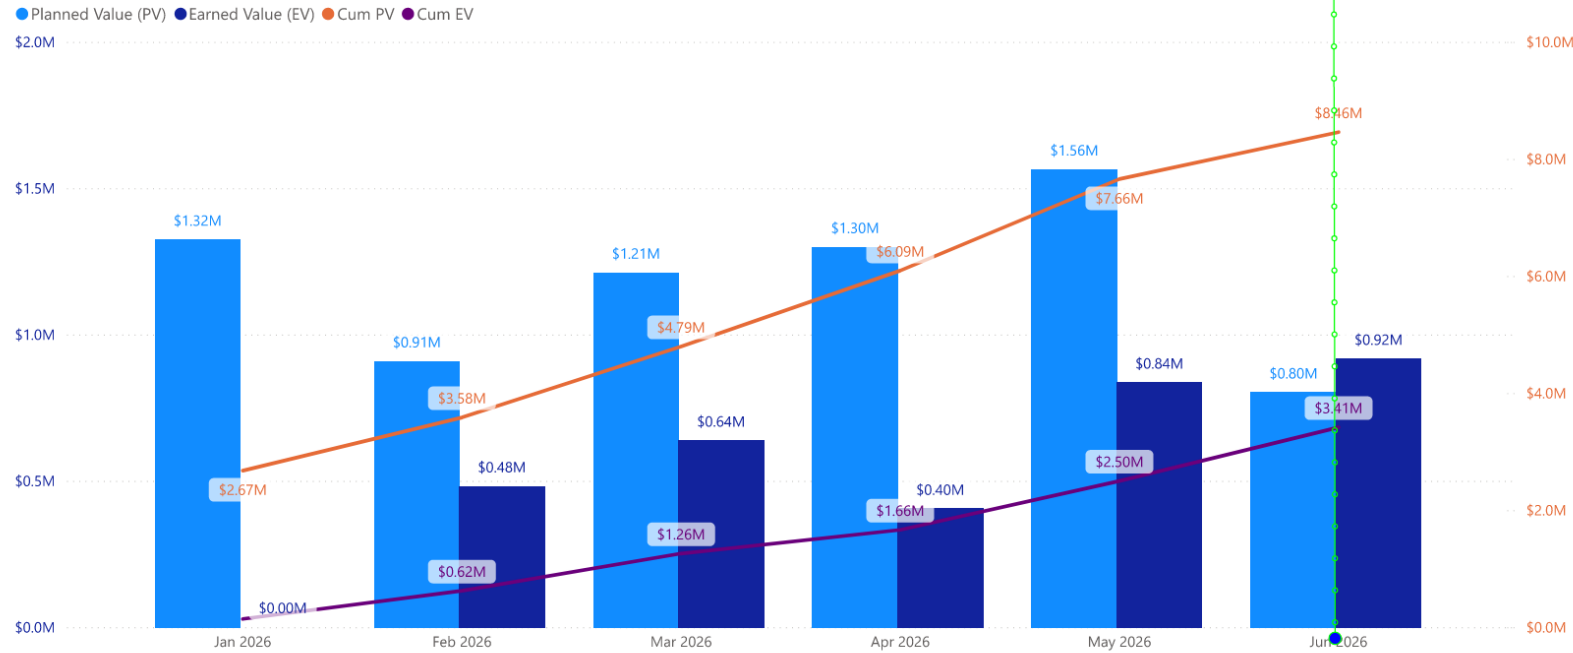

Annular Grouting Setup at NGPL Easement Tunnel




66-inch Waterline Open-Cut Installation




Tunneling Operations at Morton Ranch Road


Construction Progress – Kinder Morgan-5

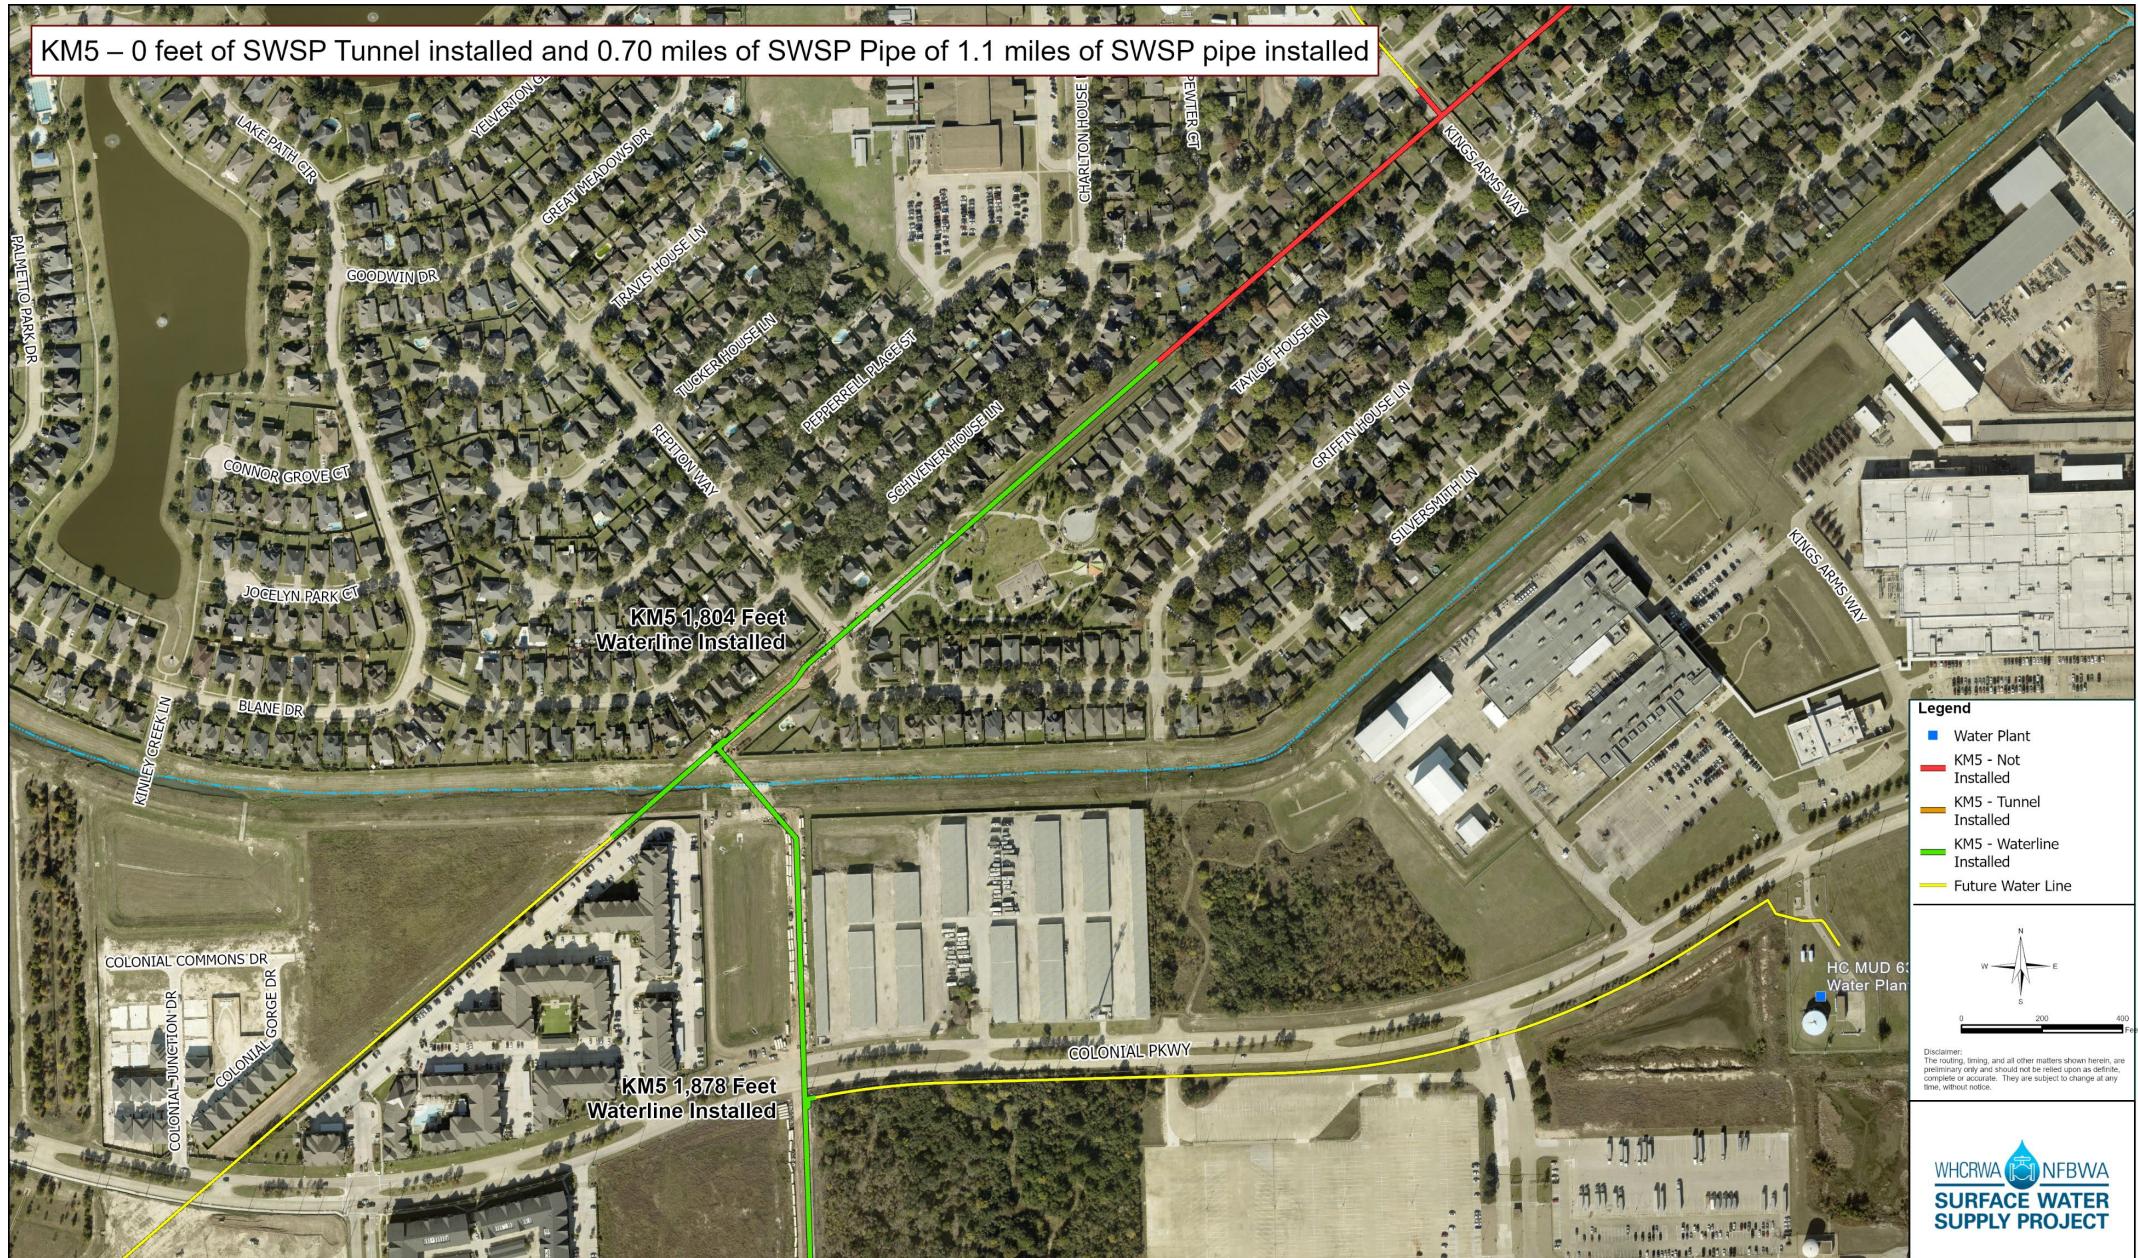

Segment KM-5

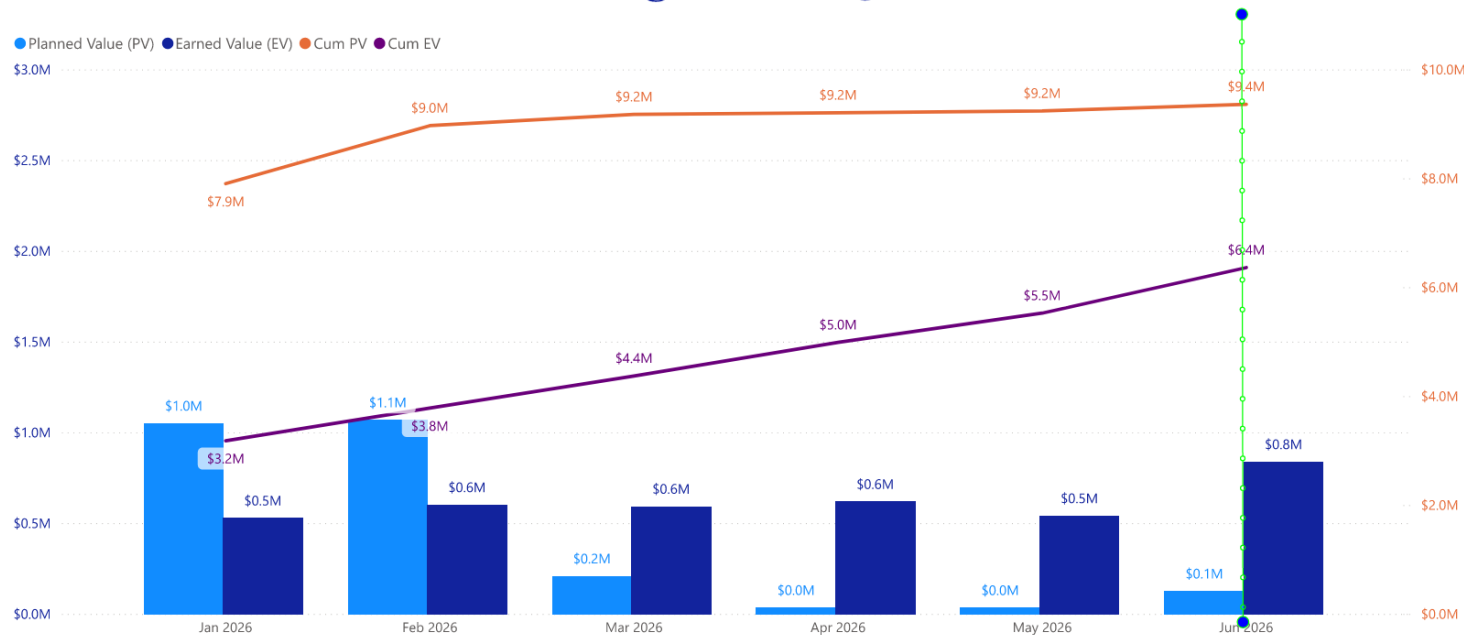


Re-Pump Station

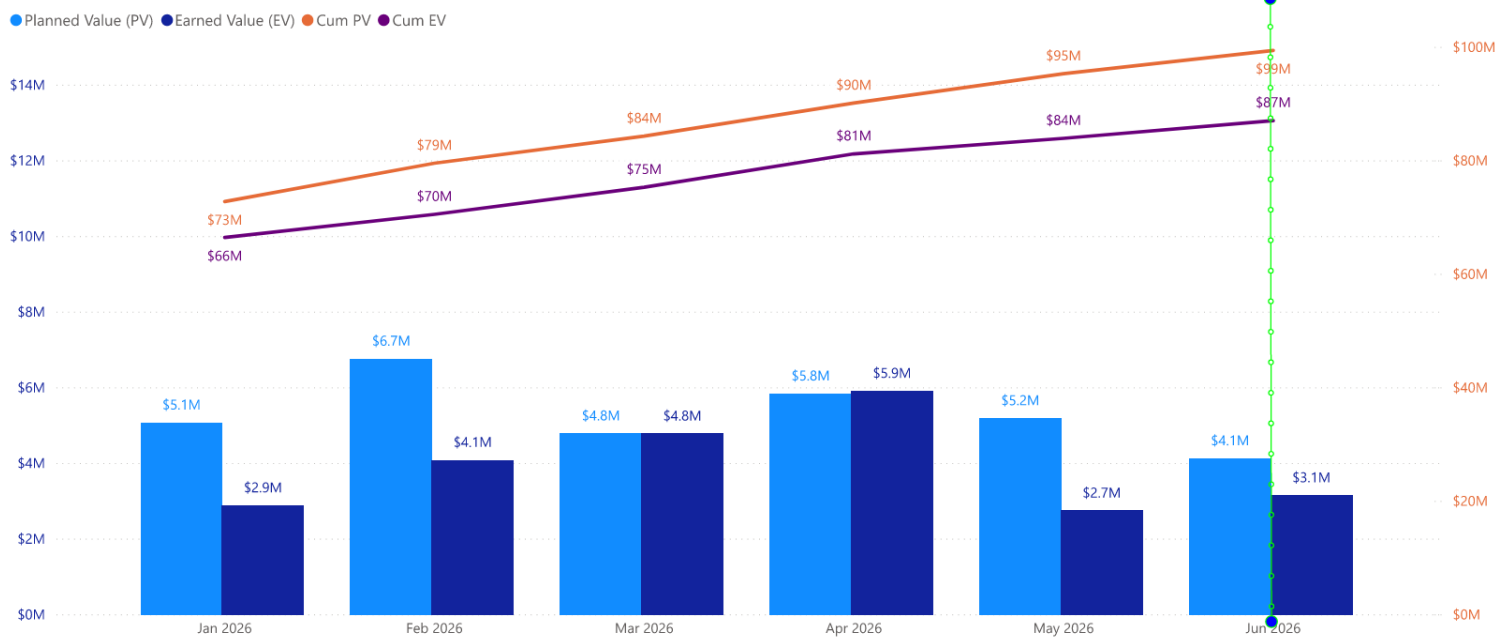

SWSP Re-Pump Station



Disinfection Facility

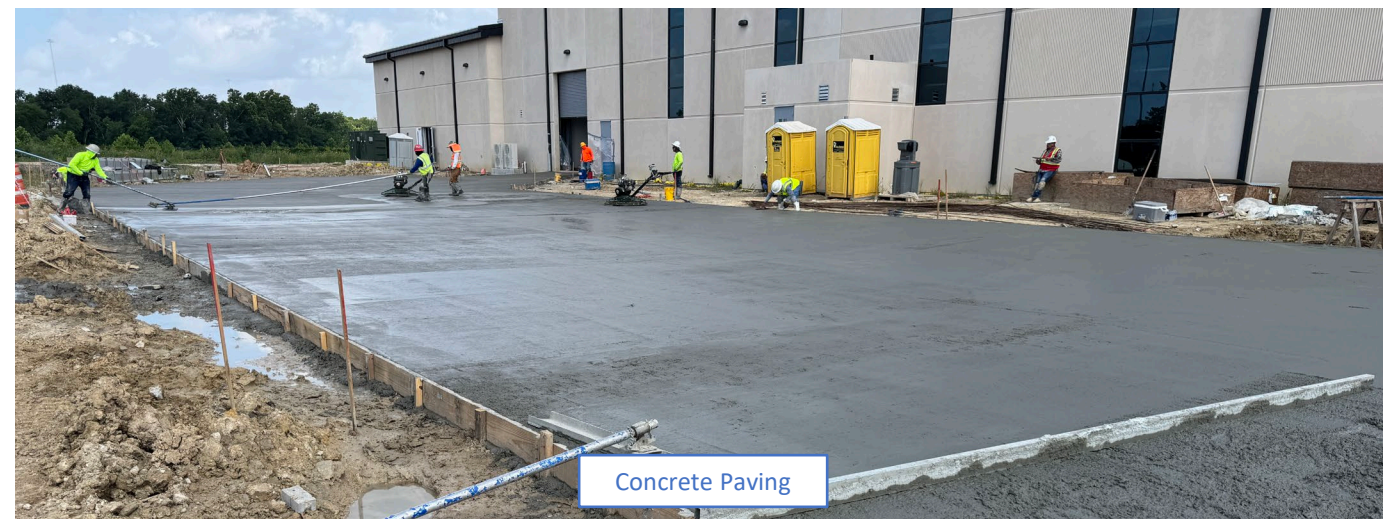





Concrete Paving



35 kV Switchgear Delivery

SWSP I-10 METER STATION


I-10 Meter Station

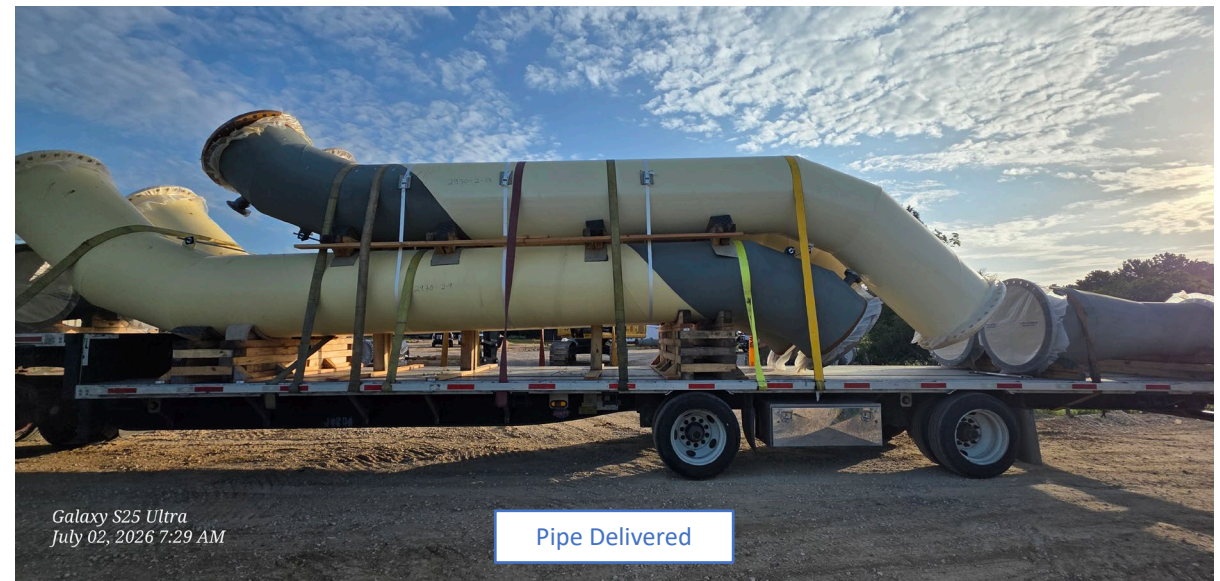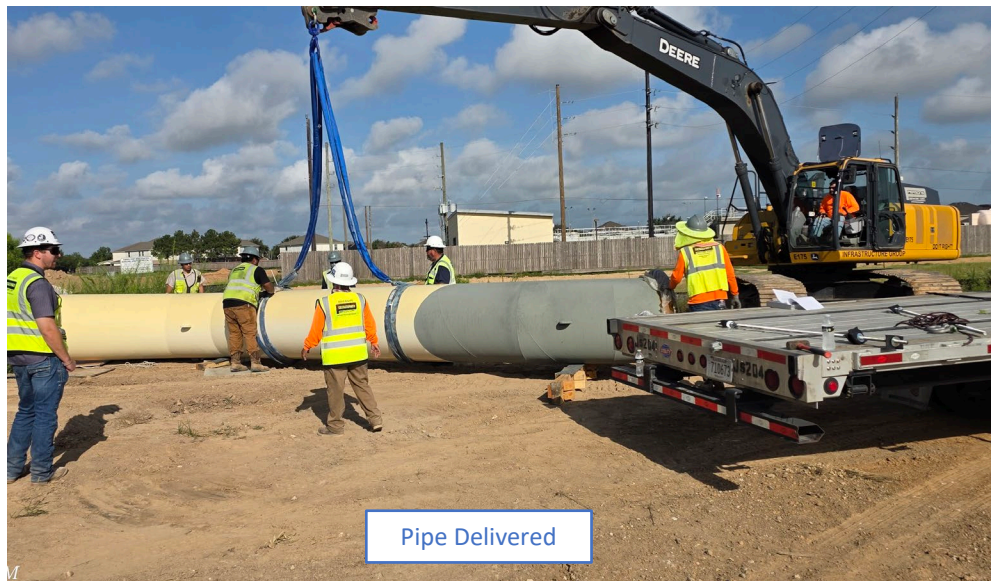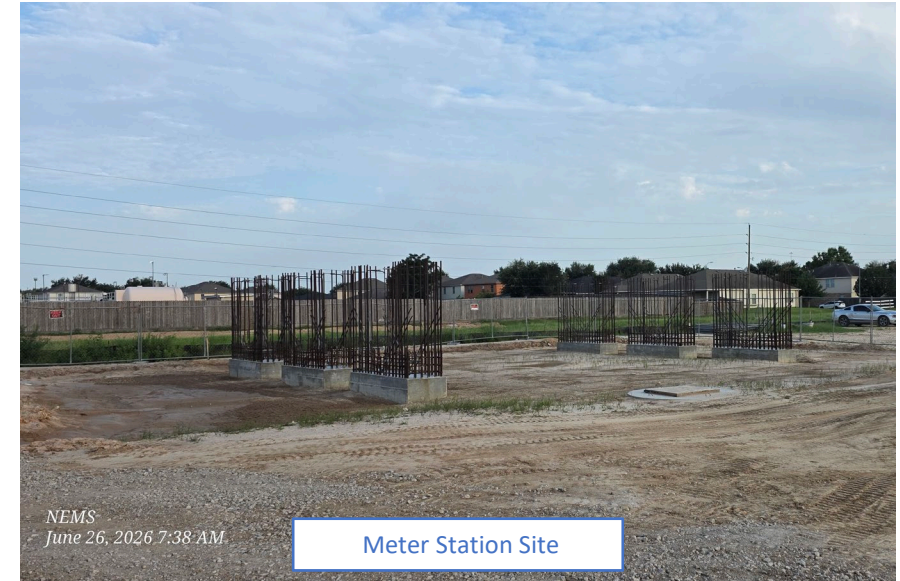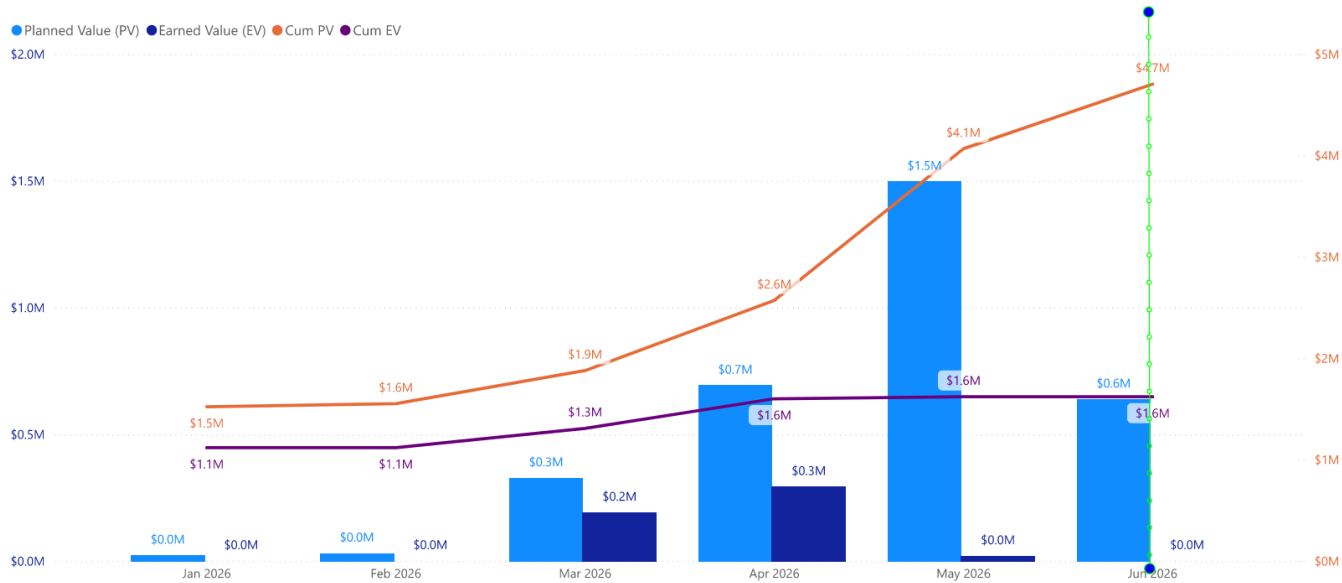


CIP CONTRACTS



Contract 64 – Installing Waterline

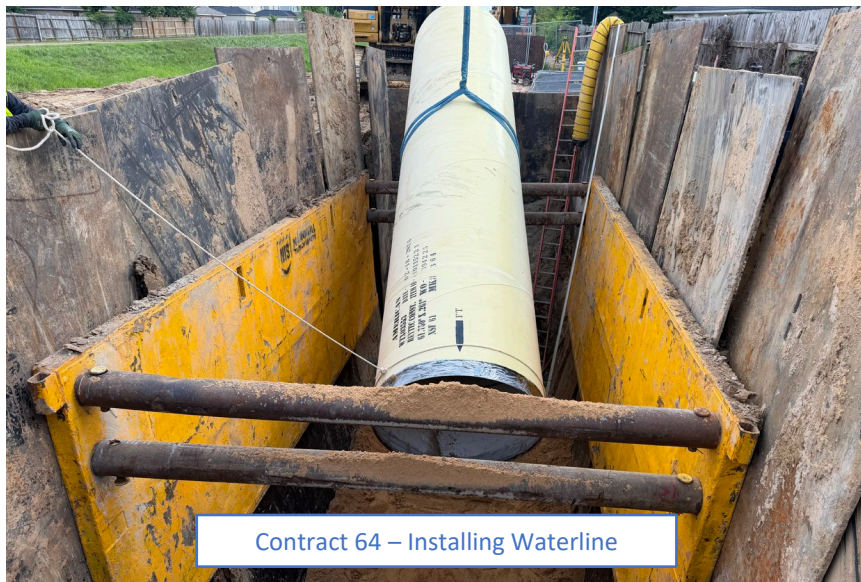

Contract 64 – Installing Waterline

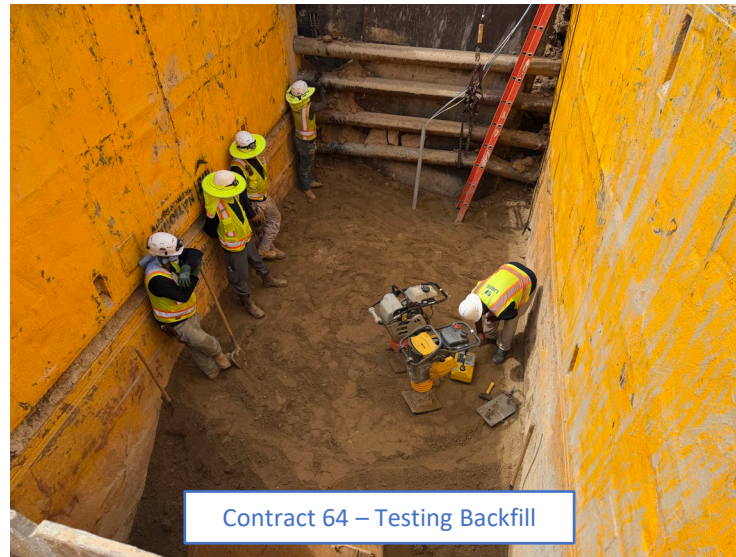

Contract 64 – Testing Backfill



Contract 64 – Bear Creek Tunnel
