

May 2026 Monthly Construction Status Report

Updated: 06.09.2026



CPS - Starting Central Pump Station into Distribution

WHCRWA Ongoing Construction Projects

Central Pump Station

CONSTRUCTION OF A CENTRAL PUMP STATION THAT WILL RECEIVE WATER FROM THE RE-PUMP STATION AND THEN TRANSFER WATER TO MUDS

Segment A1-A2

11 MILES OF 96-INCH WATER LINE FROM HOPPER RD. TO THE WHCRWA METER STATION NEAR THE NEWPP, INCLUDING SWSP DISINFECTION

RePump Station

CONSTRUCTION OF A 160 MGD REPUMP STATION FACILITY INCLUDING TWO 10 MILLION GALLON TANKS

NorthEast Meter Station

CONSTRUCTION OF A METER STATION AT COH/WHCRWA INTERFACE

Kinder Morgan 1, 2, 3, 4, 5, & 6 - (6 Projects)

6 MILES OF 66-INCH AND 1,300 LF OF 84-INCH WATERLINE FROM SEGMENT C1 CONNECTION TO THE I-10 METER STATION


I-10 Meter Station

CONSTRUCTION OF A METER STATION AT THE NFBWA INTERFACE

CIP Projects

CONTRACT 51
CONTRACT 63
CONTRACT 64
CONTRACT 65

Current SWSP Construction Projects Overview

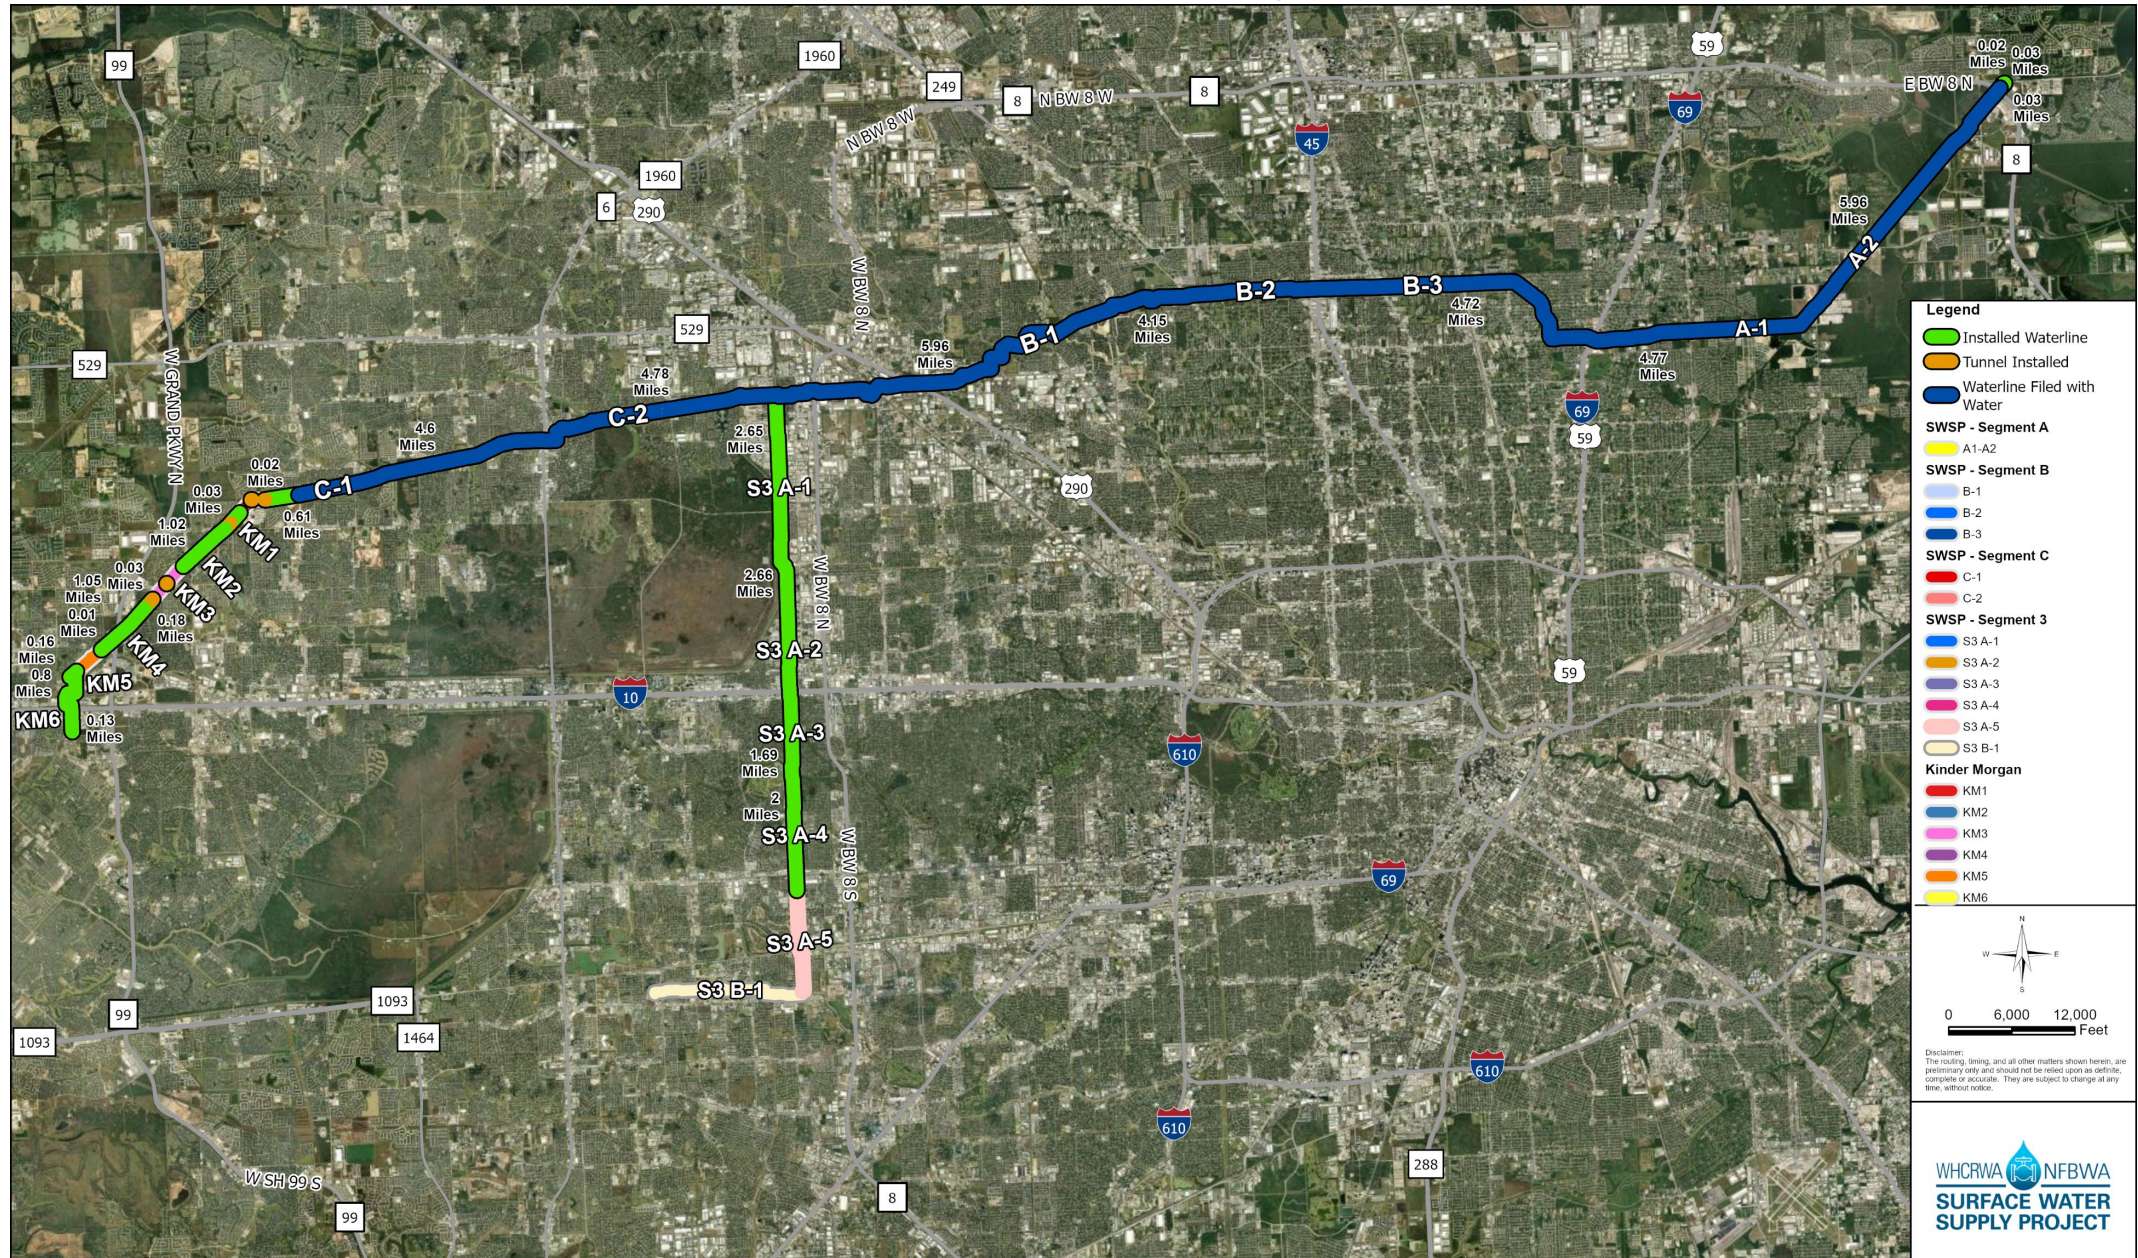


Tunneling (LF) by Project

● Installed (LF) ● Remaining (LF)

65K
Budgeted

64K
Installed

1K
Remaining

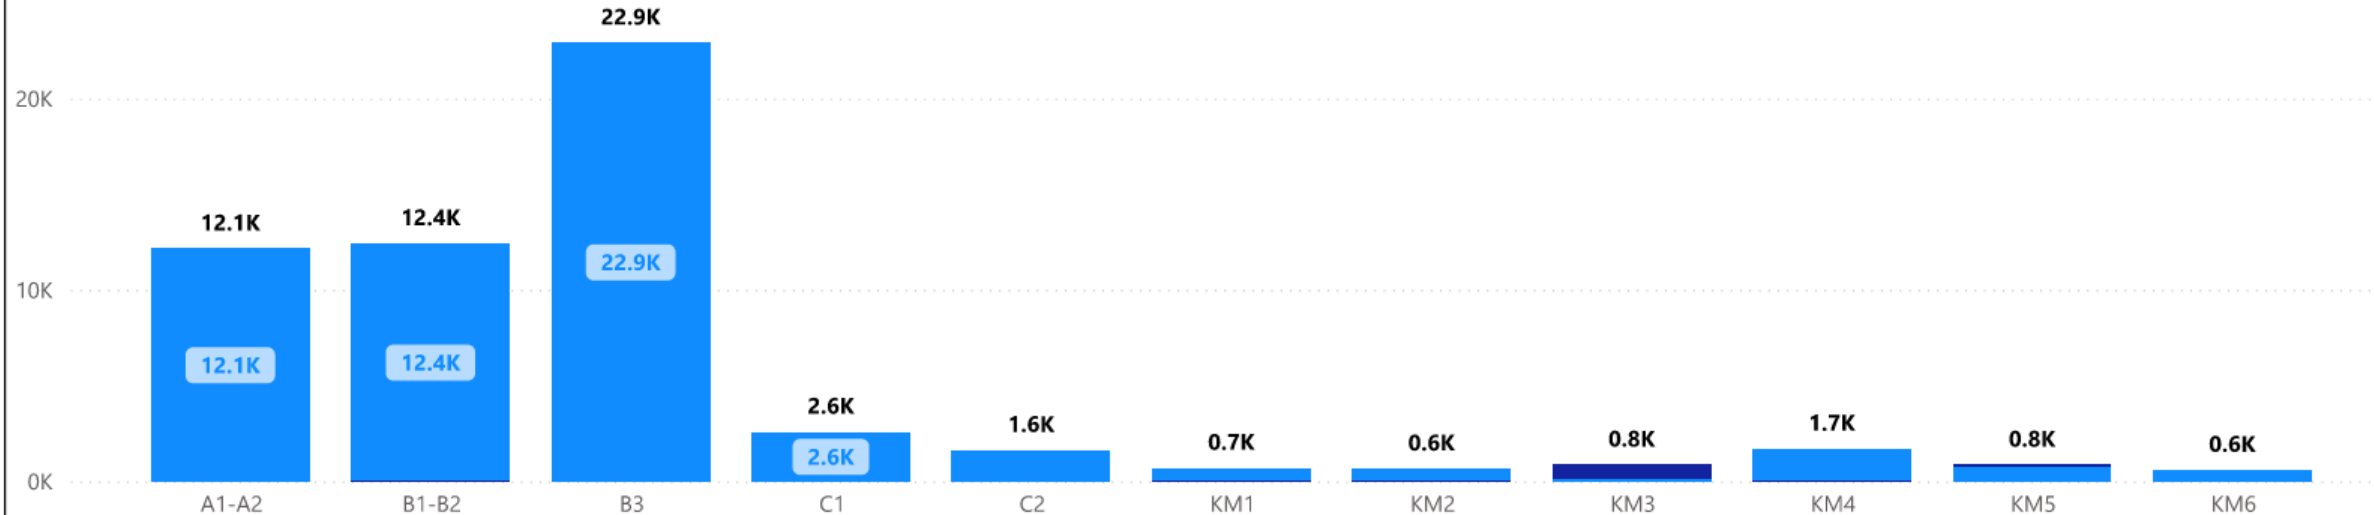


Open Cut (LF) by Project

● Installed (LF) ● Remaining (LF)


211K
Budgeted

200K
Installed


11K
Remaining

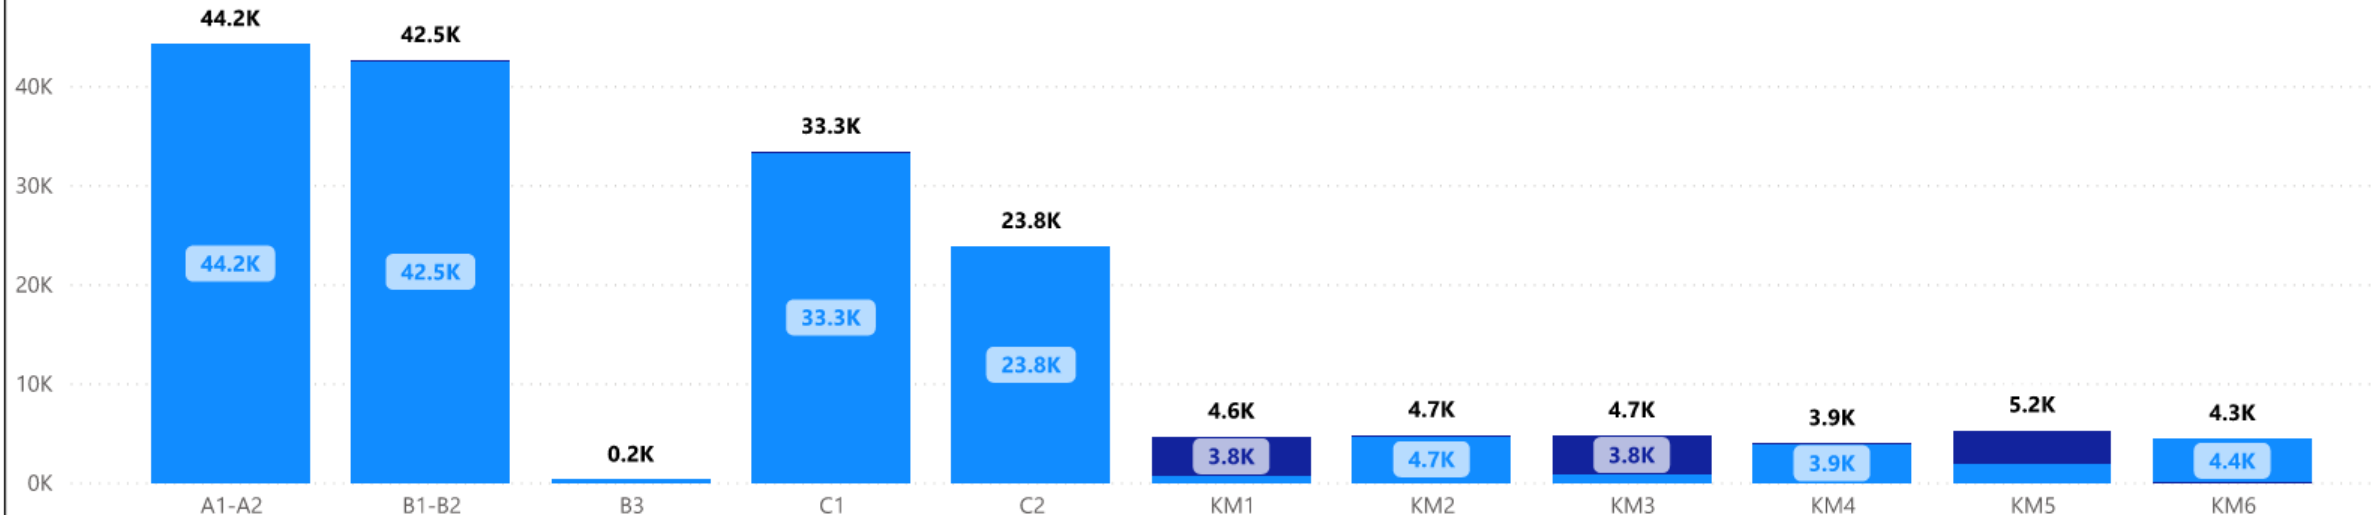

Construction Progress – Segment A1-A2

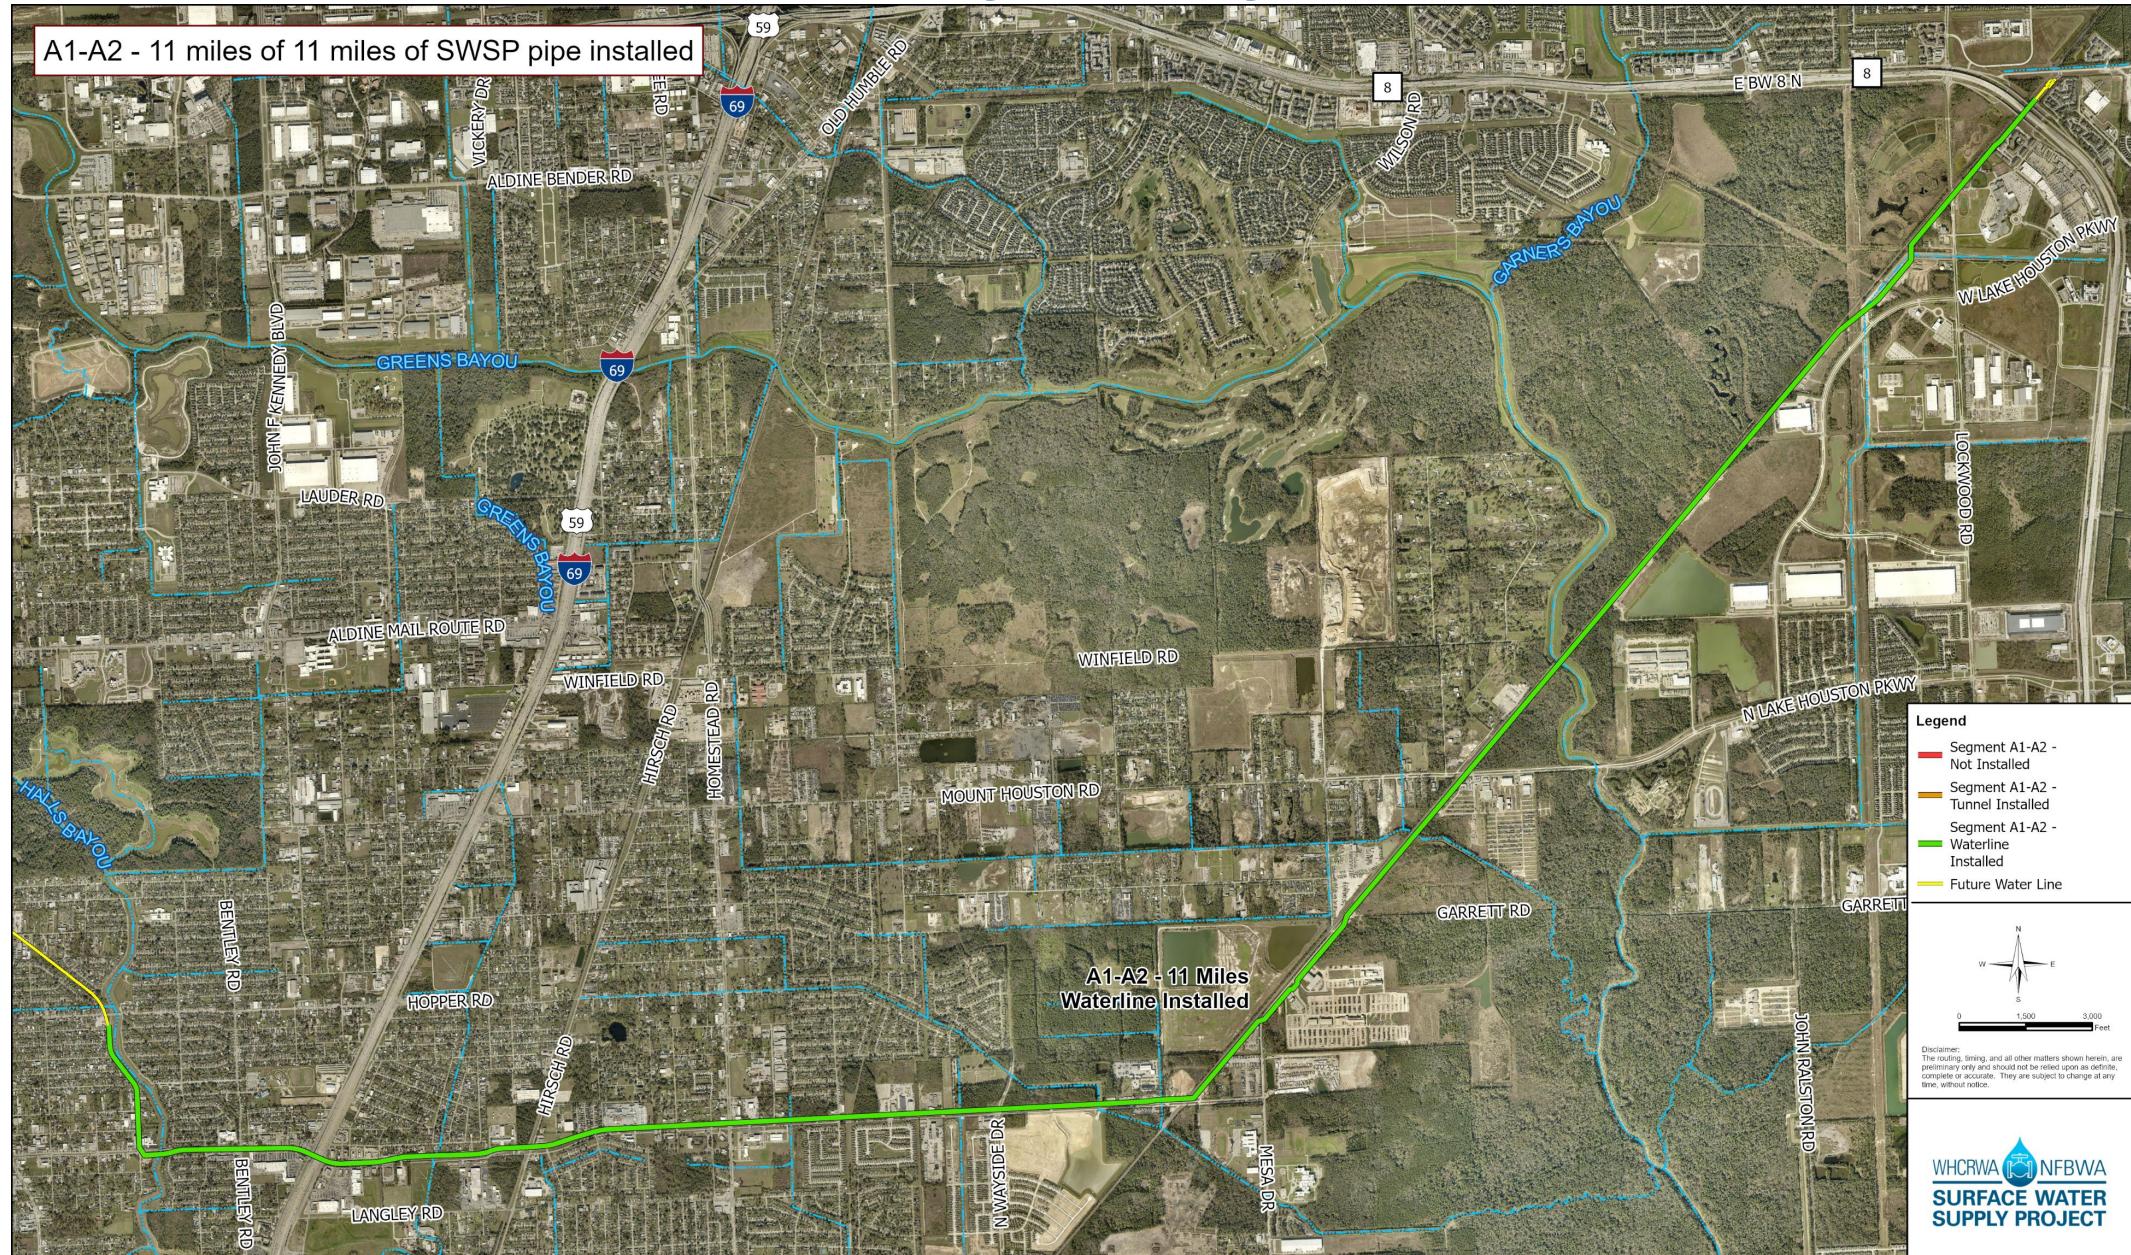


Segment A1|A2

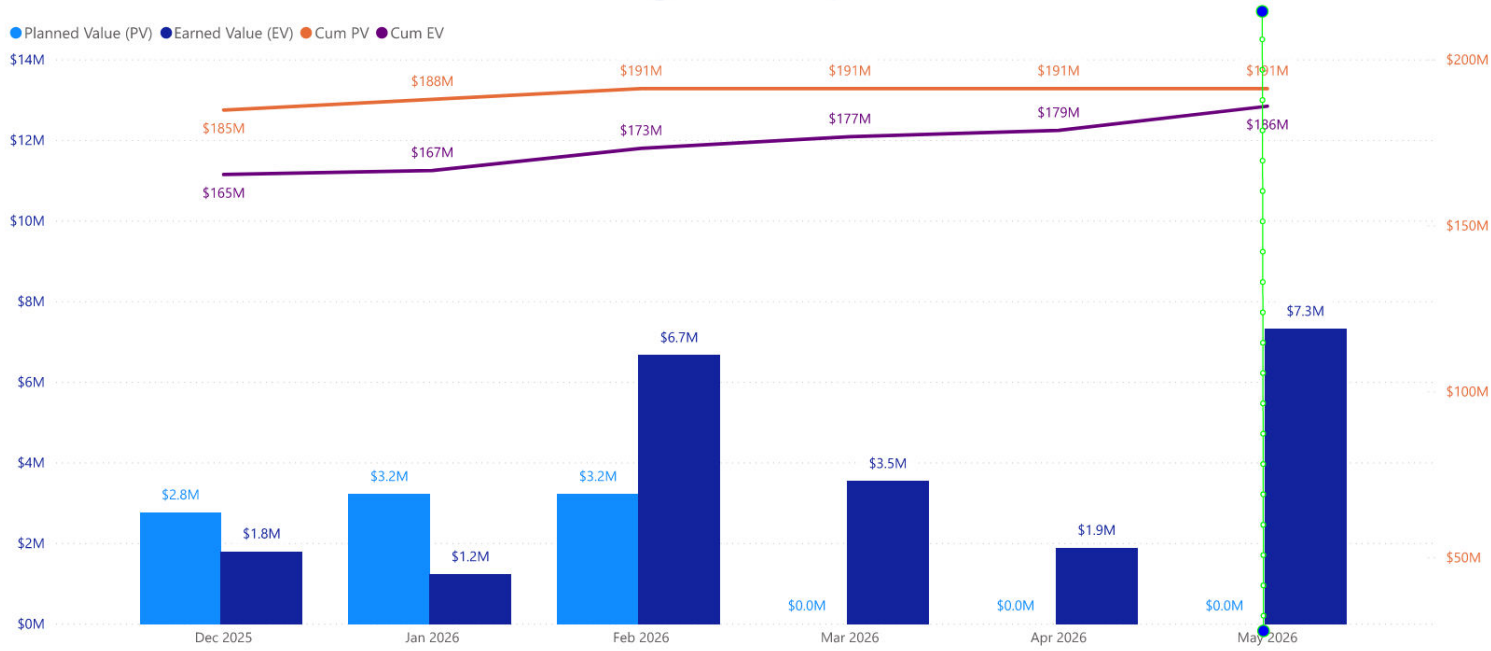

SWSP Segment A1-A2



Testing to Confirm Arrival of Chlorine Slug to CPS

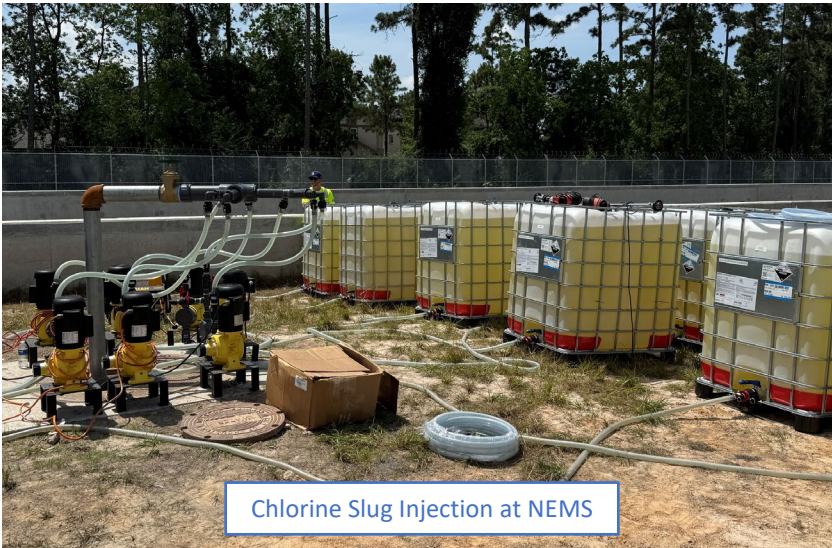

Chlorine Slug Injection at NEMS





Following Chlorine Slug along SWSP and Confirming Residuals Using Test Strips


Construction Progress – Kinder Morgan-1




Segment KM-1

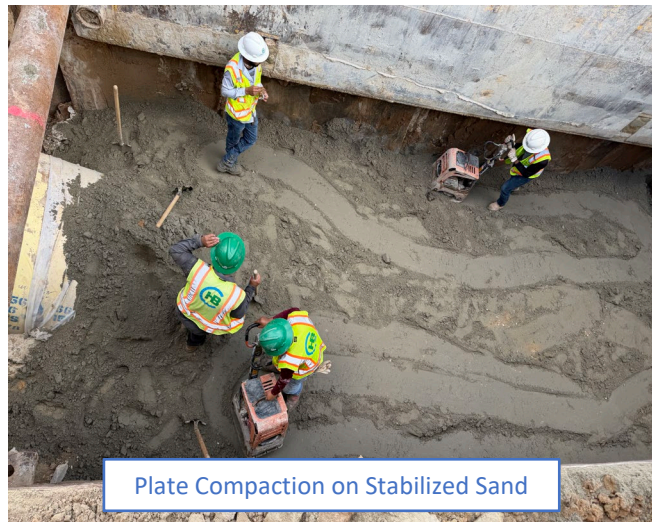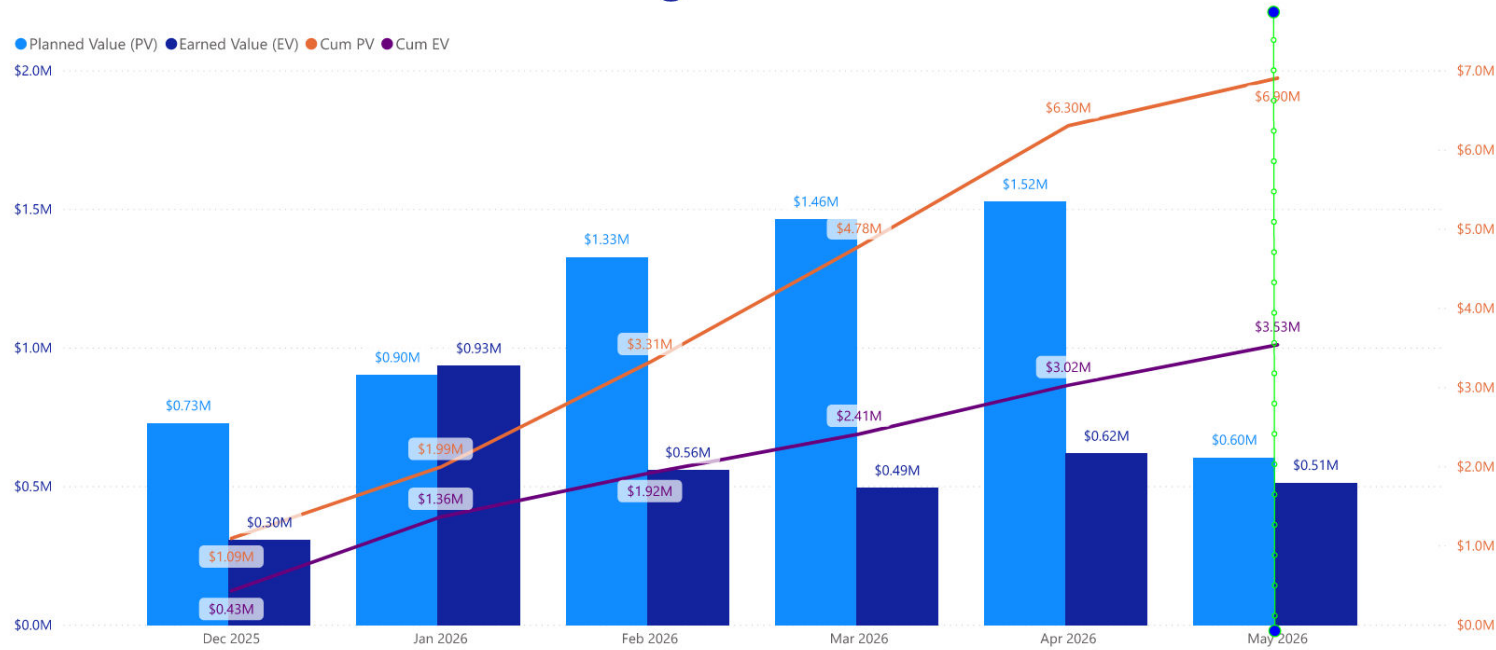

Construction Progress – Kinder Morgan-2

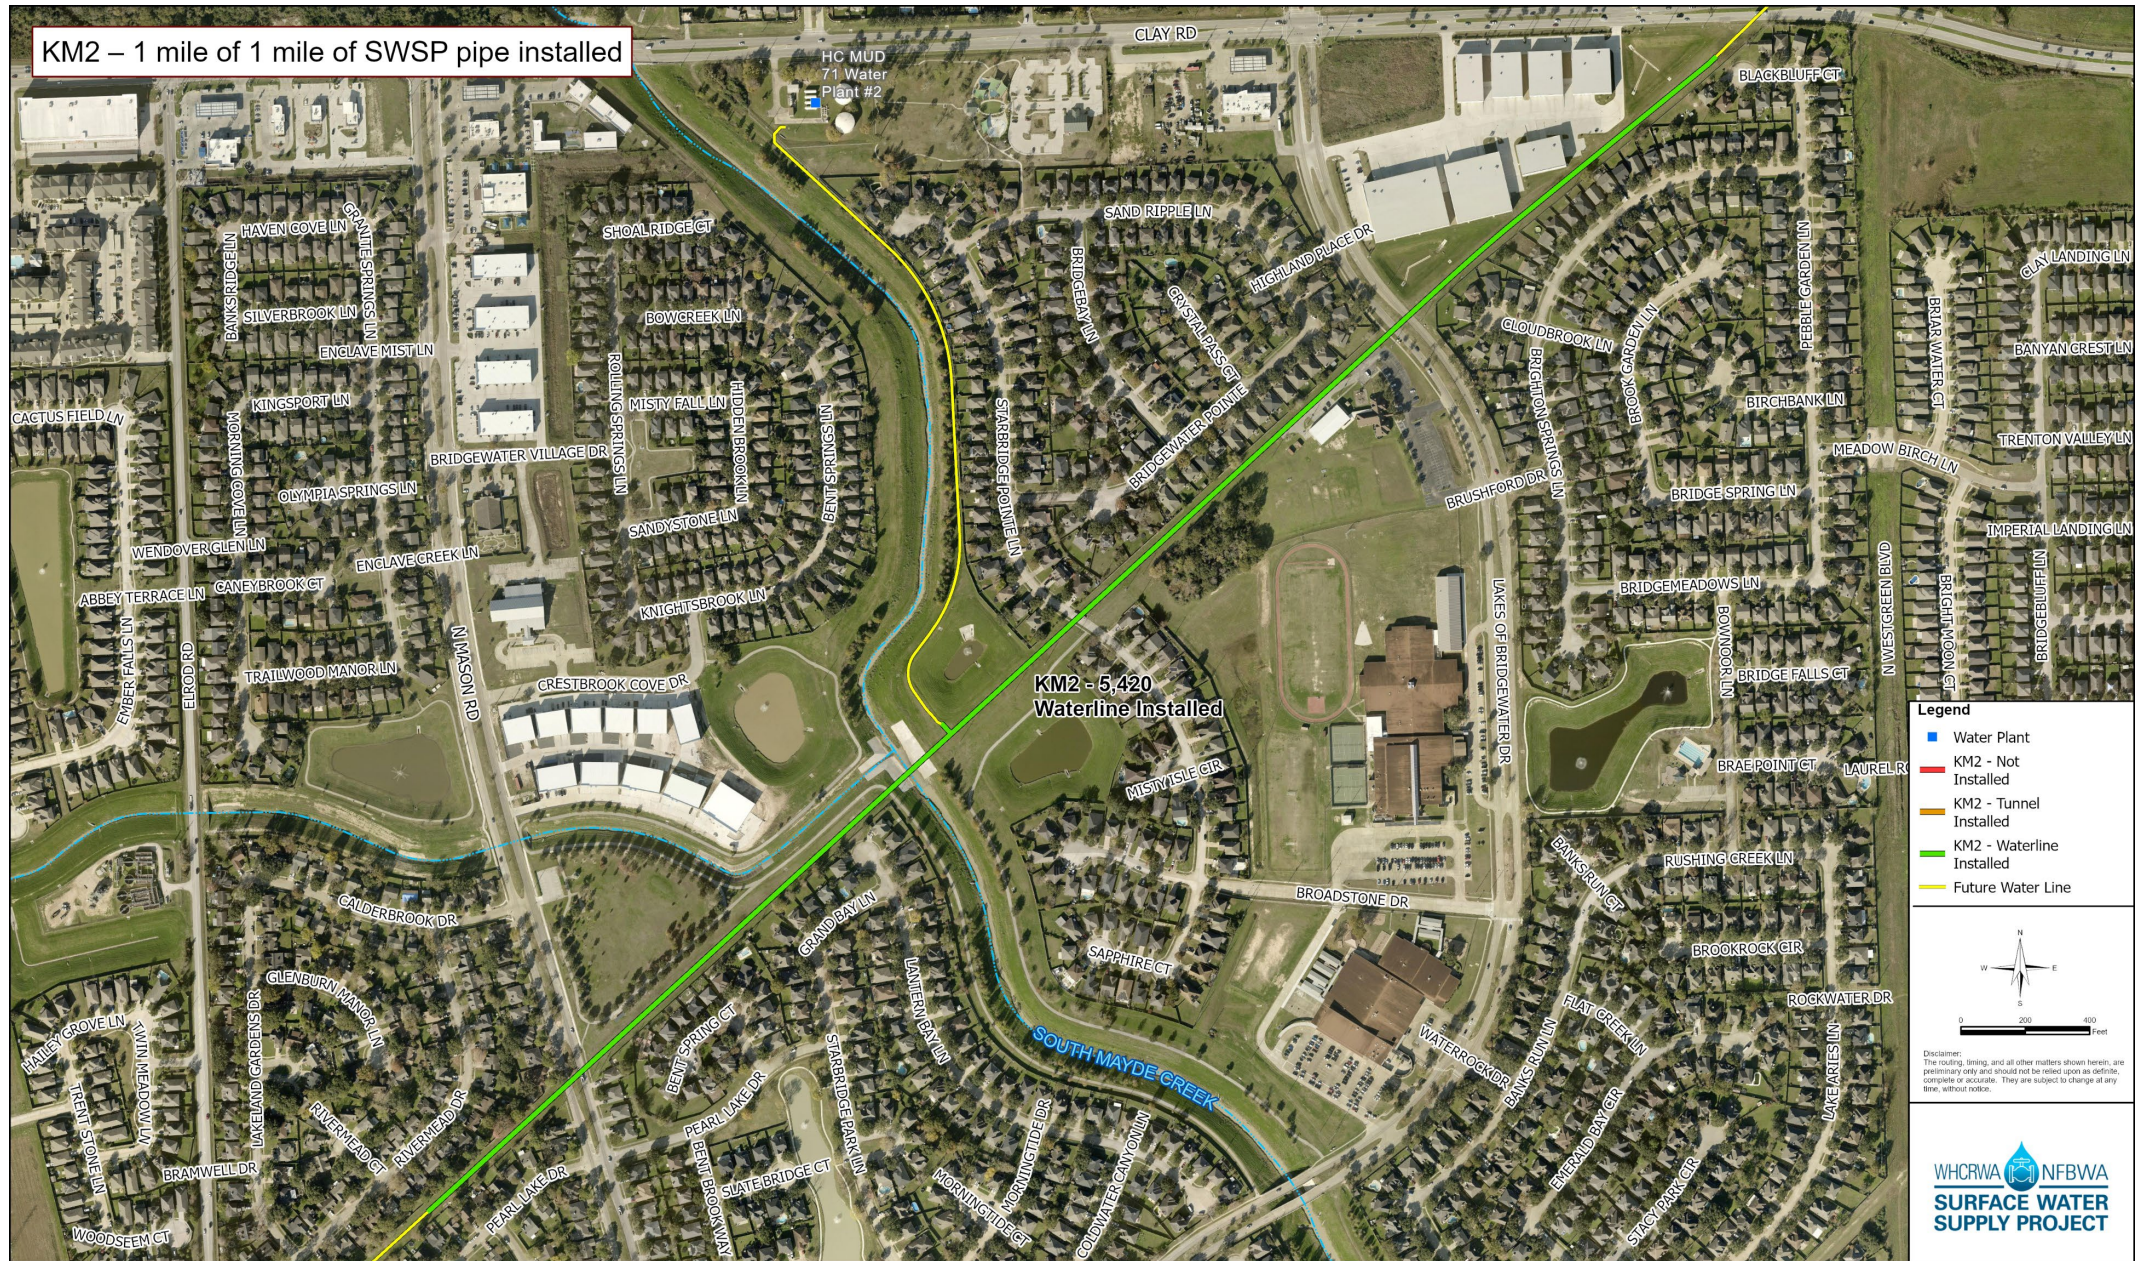

Segment KM-2

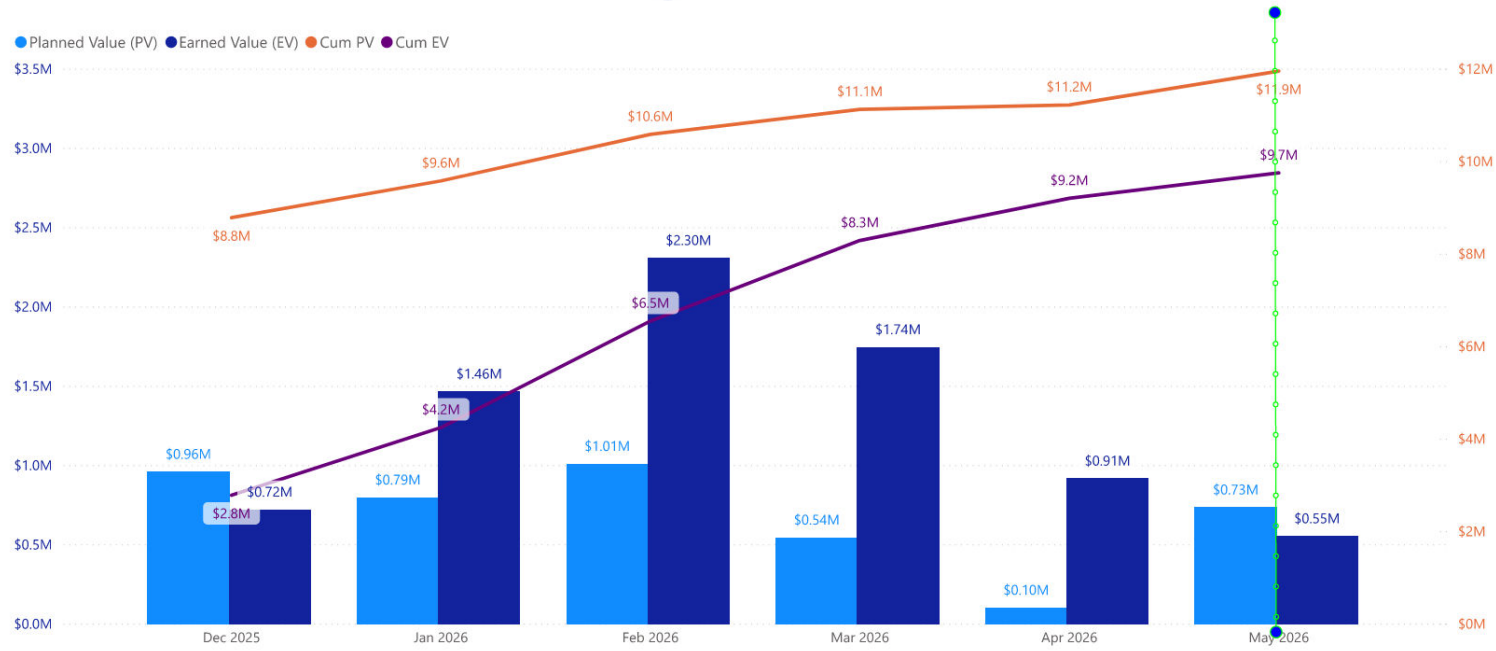

Working on Control Cabinet at Meter Vault




Installing 12-inch Waterline in Auger Bore




Plumbing Access Manways throughout Project

Construction Progress – Kinder Morgan-3

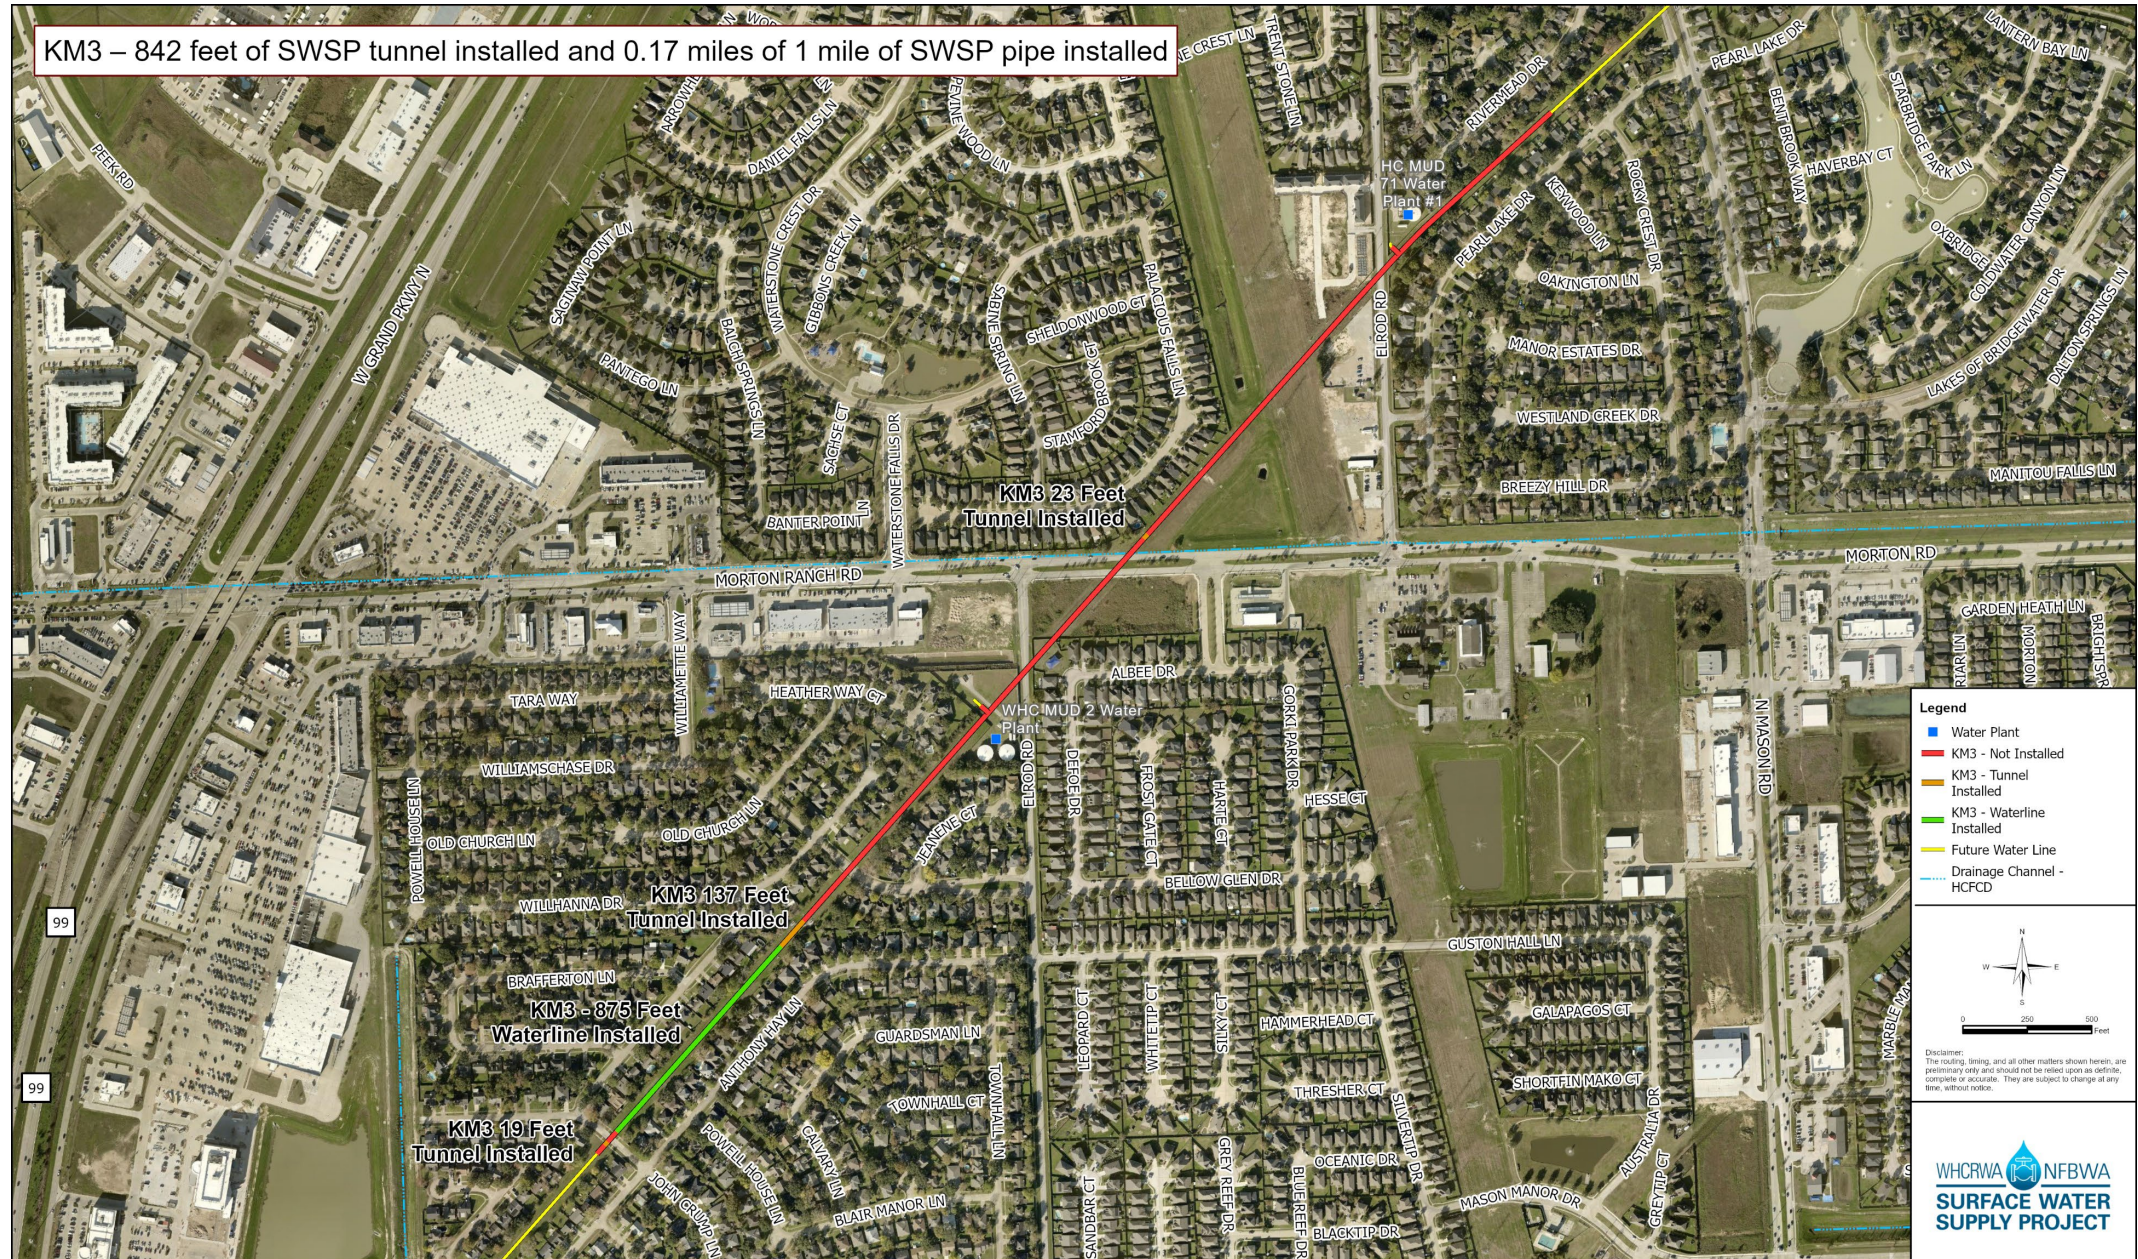


Segment KM-3

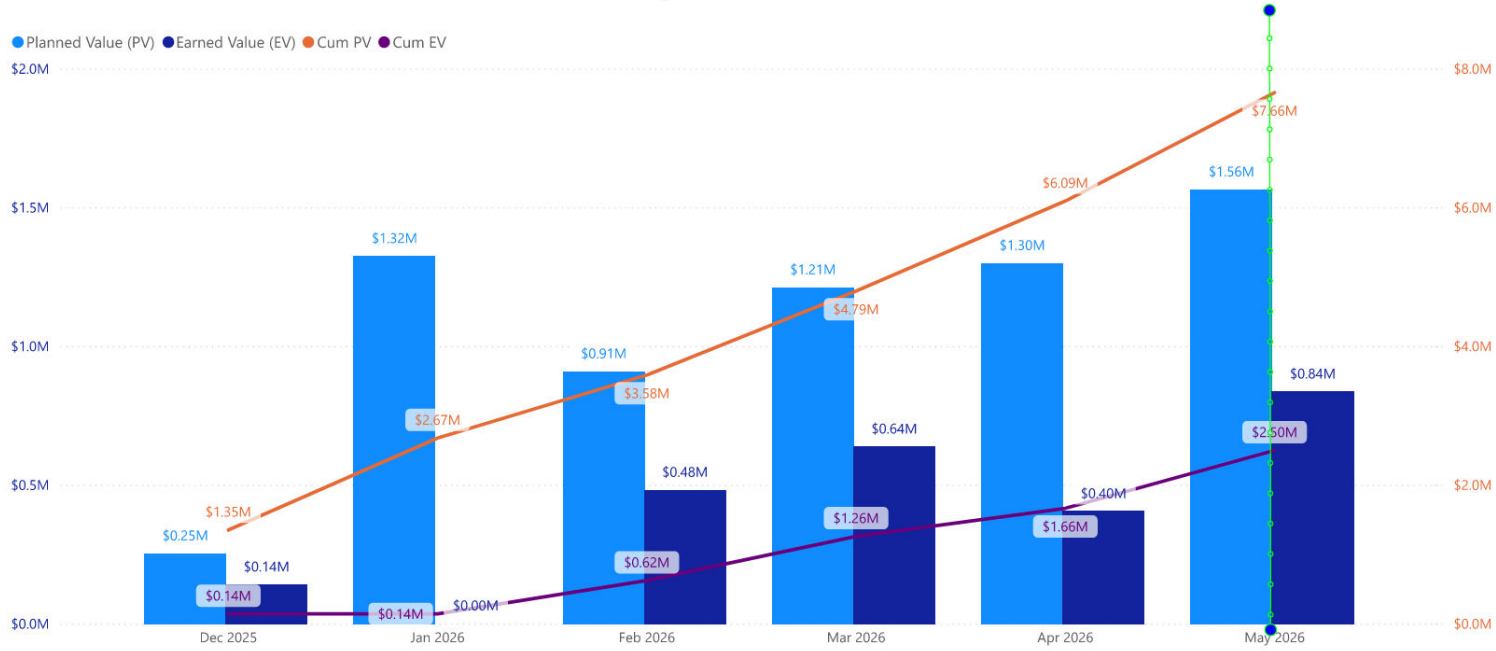


Construction Progress – Kinder Morgan-5

KM5 – 0 feet of SWSP Tunnel installed and 0.52 miles of SWSP Pipe of 1.1 miles of SWSP pipe installed

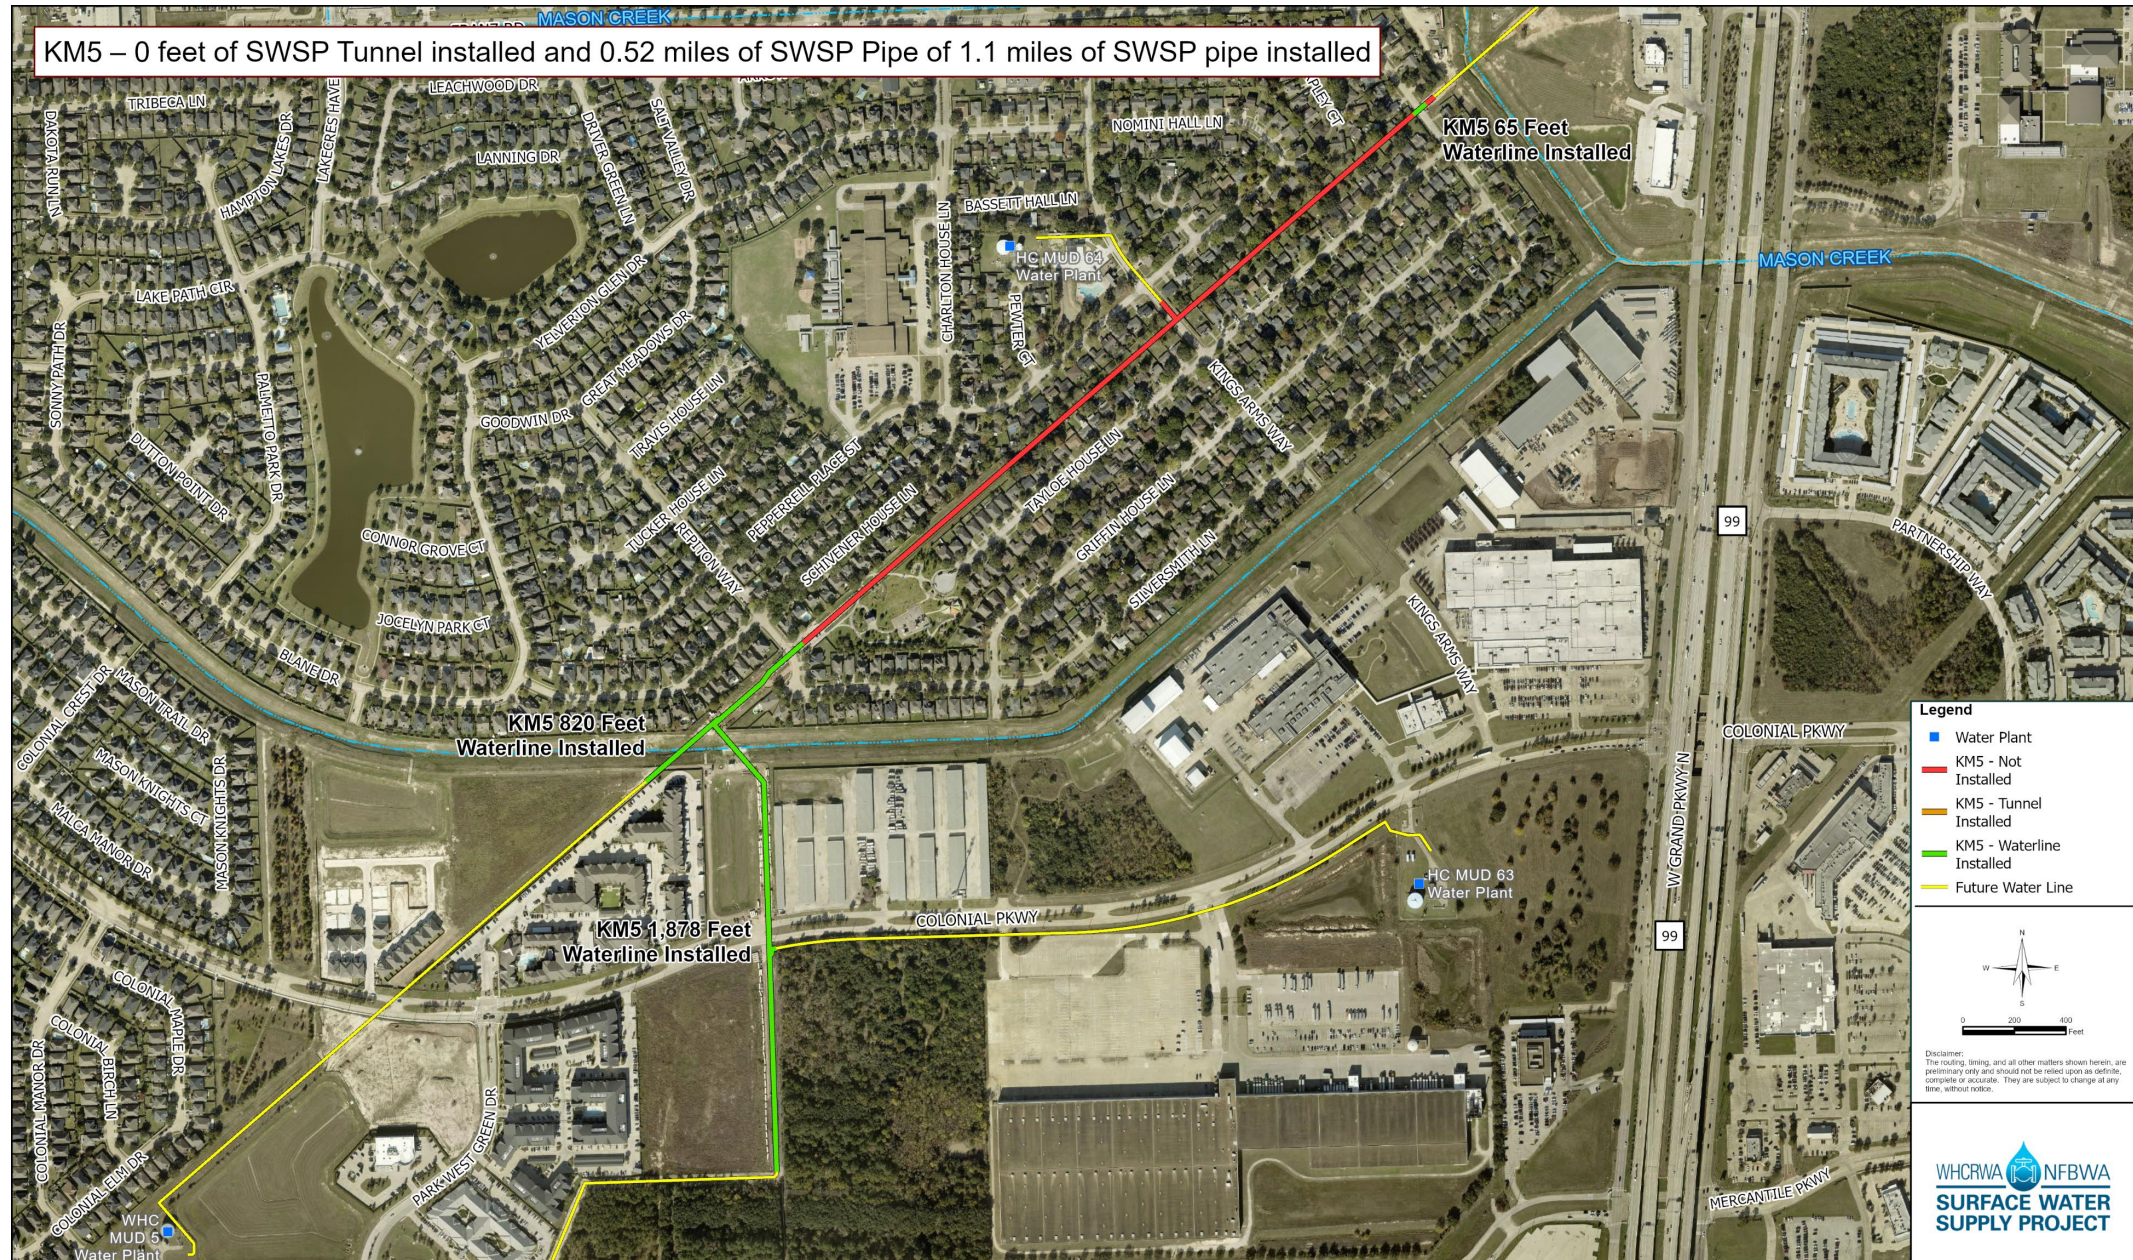


Kinder Morgan 5 - Construction Progress


Segment KM-5

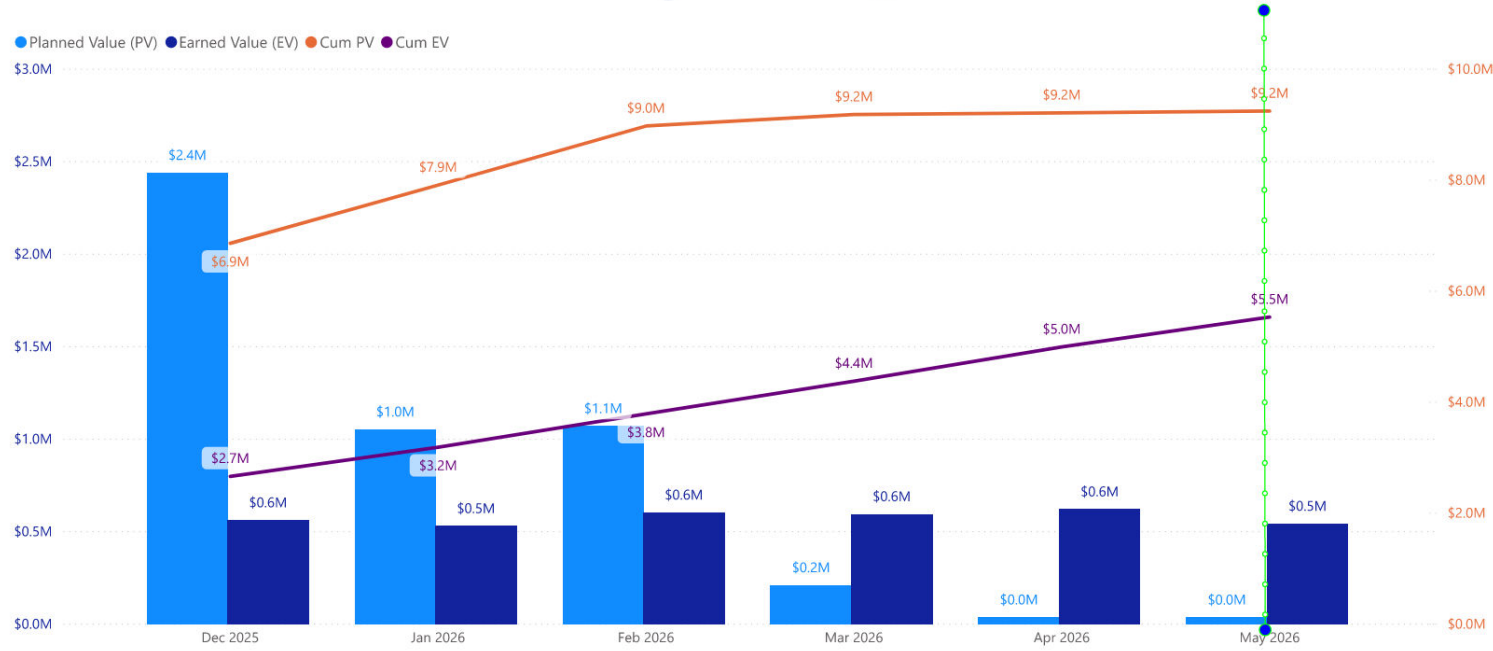

Central Pump Station

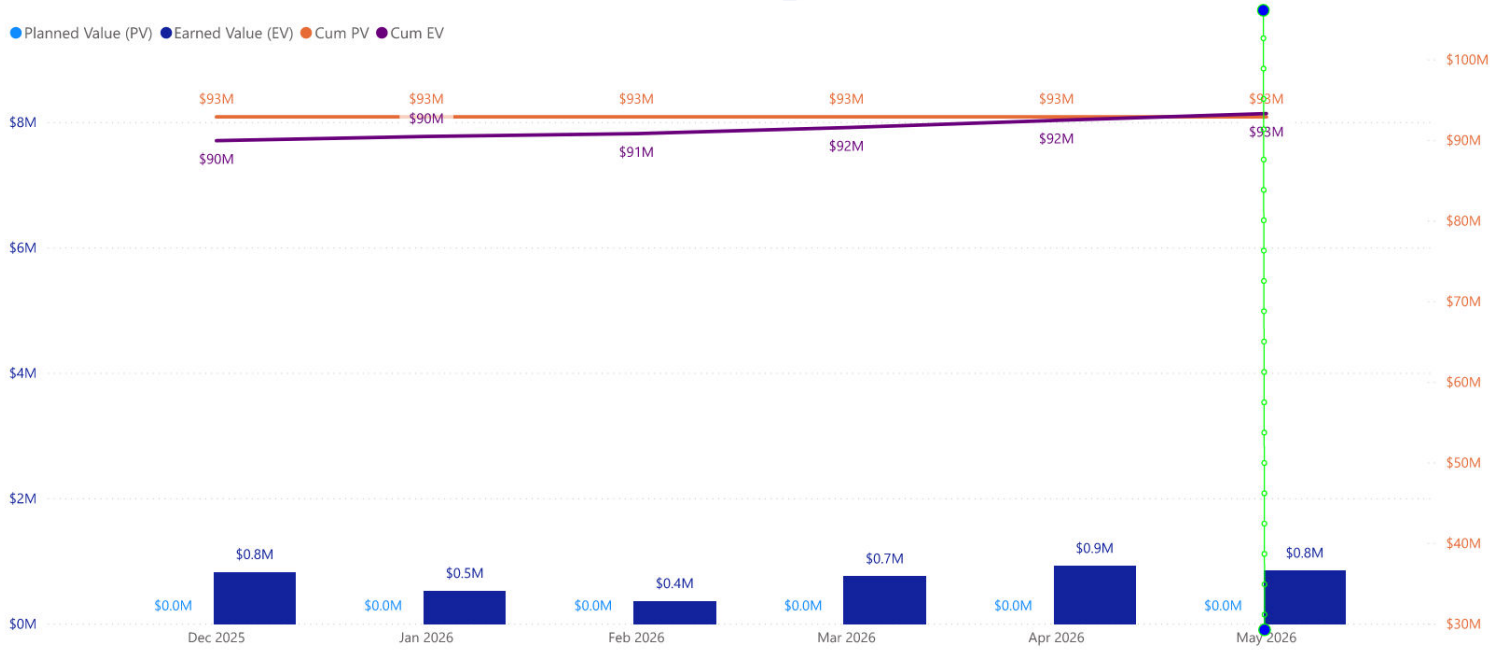


Re-Pump Station

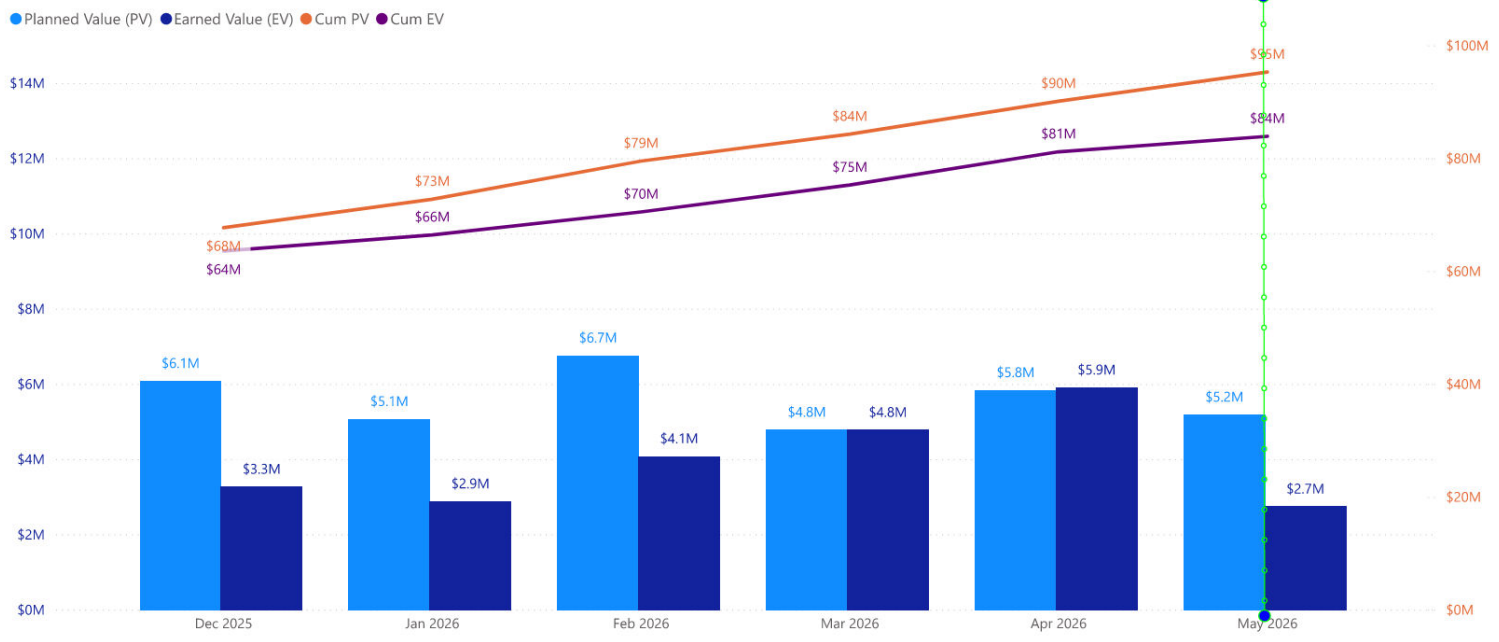

SWSP Re-Pump Station



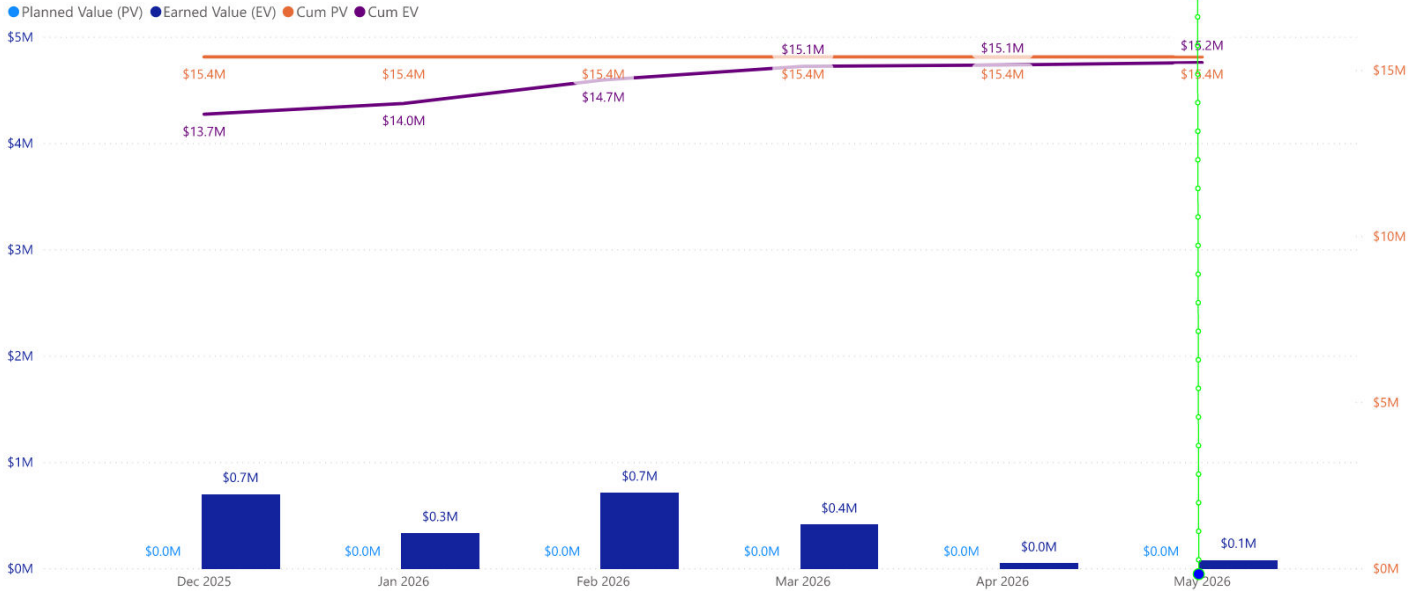

SWSP Northeast Meter Station



Installing Speed Bumps





Generator Testing



Installing Rock Under Meter Station Piping

I-10 Meter Station

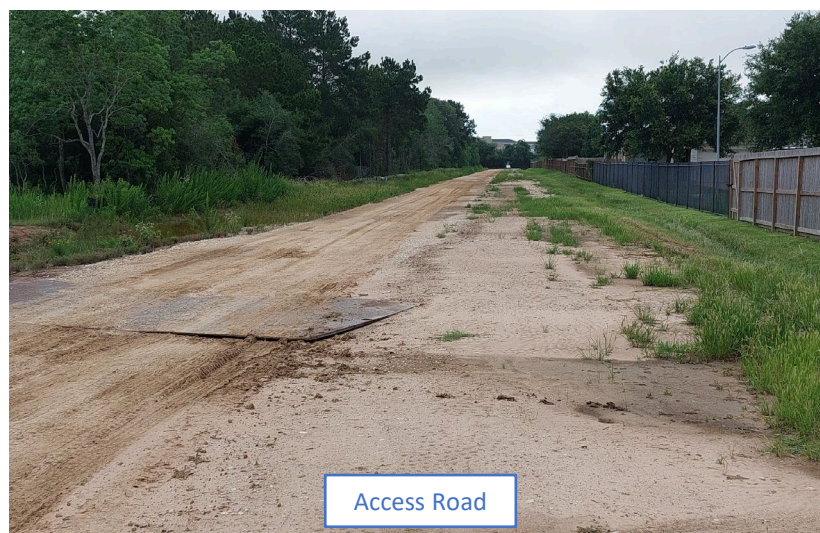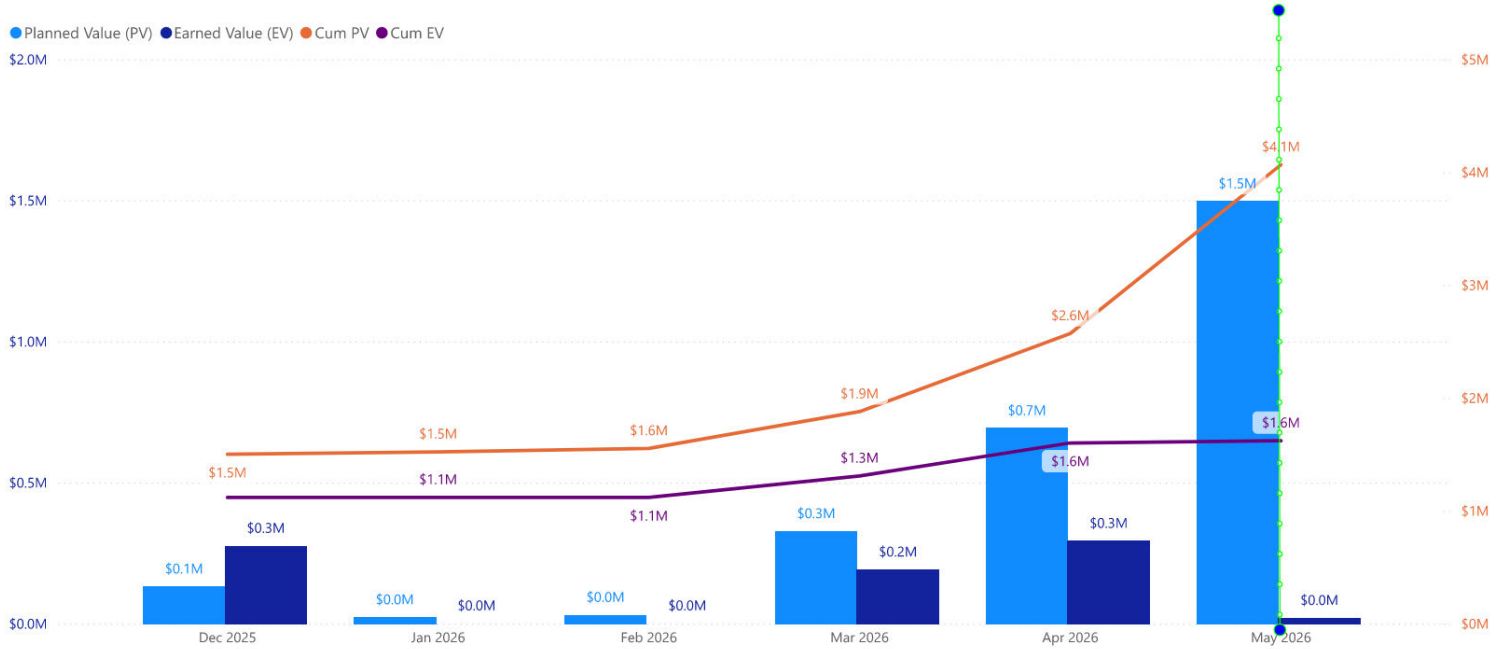

CIP CONTRACTS



Contract 64 – MUD 167 Meter Station



Contract 51 – Installing Spacers on Waterline



Contract 64 – Tunnel Boring Machine



Contract 64 – Bear Creek Casing
